



Job Name: 26-3805 - Goldfinch Sewer Ph.3 Job Location: Evansville, IN Contractor: CAC Custom Homes					Plant: 100 9/29/2026 7:43:29 AM		Tech: J. Horsley PC: T. Lewis				
Structure ID: SSMH 727											
P2 MH048RS48XS			MH RISER w/XYPEX/NO STEP T/G								
P5) 24" - CASTING HEIGHT - 7" P4) 24" - XYPEX GRADE RING F/F - 4" P3) 48" - ECC CONE w/ 24" HOLE NO STEP w/ XYPEX F/G - 30" P2) 48" - MH RISER w/XYPEX/NO STEP T/G - 48" P1) 48" - MH BASE w/XYPEX T/n - 24" 1) 48" - MH INVERT CHANNEL EWSU w/XYPEX - FULL HEIGHT 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) CASTING - HOE MC-315 F/C Sanitary 2) 48" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 2) PSX - 12-08 NYLO						0 lb 270 lb 2050 lb 3353 lb 2911 lb 1440 lb 0 lb 0 lb 0 lb 258 lb 0 lb 0 lb 0 lb 16 lb		Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. ADMIX = XYPEX C500-NF-RED 4. CASTING BY ICAST (HOE MC-315 F/C "SANITARY") REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.			
Rim: 385.8' Rim to Invert: 9.38' Slack: 1.564" Sump: 2.004" Step Position:						Structure Total: 10298 lb					
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1											
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											

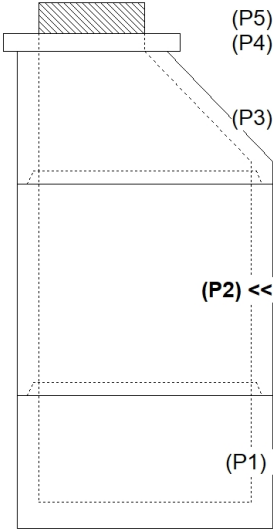


(P5)
(P4)
(P3)
(P2) <<
(P1)

RIGHT-SIDE UP VIEW (int. dimensions)



+ 0°-

INSIDE WALL DIMENSIONS

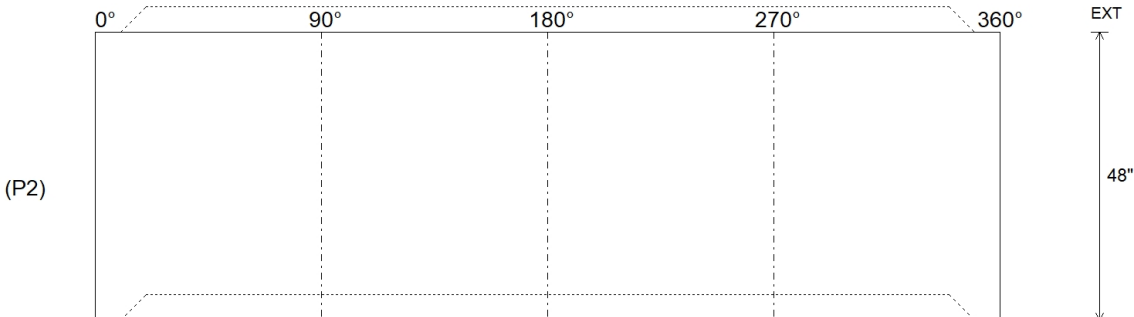

(P2)
48"

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: Groove	Wall Thickness: 5" Floor Height: 0"	Height (Int): 48" Height (Ext): 48"	Weight (Net): 3353 lb Volume (Net): 0.86cu.yd
----------------------------------	------------------------------------	--	--	--
