


Job Name: 26-3805 - Goldfinch Sewer Ph.3 Job Location: Evansville, IN Contractor: CAC Custom Homes				Plant: 100 9/29/2026 7:43:07 AM		Tech: J. Horsley PC: T. Lewis					
Structure ID: SSMH 729											
P1 MH048BA30X				MH BASE w/XYPEX T/n							
P3) 24" - CASTING HEIGHT - 7" P2) 48" - ECC CONE w/ 24" HOLE NO STEP w/ XYPEX F/G - 36" P1) 48" - MH BASE w/XYPEX T/n - 30" 1) 48" - MH INVERT CHANNEL EWSU w/XYPEX - FULL HEIGHT 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) CASTING - HOE MC-315 F/C Sanitary 1) 48" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 1) PSX - 12-08 NYLO						0 lb 3000 lb 3378 lb 1440 lb 0 lb 0 lb 258 lb 0 lb 0 lb 8 lb Structure Total: 8084 lb		Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. ADMIX = XYPEX C500-NF-RED 4. CASTING BY ICAST (HOE MC-315 F/C "SANITARY") REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.			
Rim: 386'				Rim to Invert: 6'		Slack: 1.004"		Sump: 2.004"		Step Position:	
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	380'	0°	0"	8" PVC SDR26	8.5"	PSX 12-08 NYLO	12"	12.129"	0"	0"	
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											

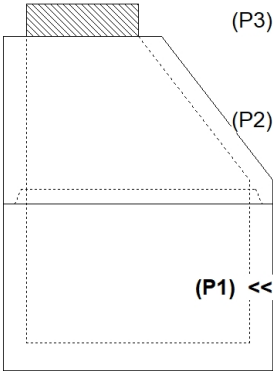


(P3)

(P2)


(P1) <<

RIGHT-SIDE UP VIEW (int. dimensions)




Invert: 1
Degree: 0°
Horz: 0"
Hole: 12"
Up(): 0"

UPSIDE-DOWN VIEW (int. dimensions)



Invert: 1
Degree: 0°
Horz: 0"
Hole: 12"
Up(): 0"


INSIDE WALL DIMENSIONS



(P1)

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 30" Height (Ext): 36"	Weight (Net): 3378 lb Volume (Net): 0.86cu.yd
----------------------------------	---------------------------------	--	--	--

Job Name: 26-3805 - Goldfinch Sewer Ph.3 Job Location: Evansville, IN Contractor: CAC Custom Homes				Plant: 100 9/29/2026 7:43:07 AM		Tech: J. Horsley PC: T. Lewis						
Structure ID: SSMH 729												
P1A MH048BA30X				MH BASE w/XYPEX T/n								
P3) 24" - CASTING HEIGHT - 7" P2) 48" - ECC CONE w/ 24" HOLE NO STEP w/ XYPEX F/G - 36" P1) 48" - MH BASE w/XYPEX T/n - 30" 1) 48" - MH INVERT CHANNEL EWSU w/XYPEX - FULL HEIGHT 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) CASTING - HOE MC-315 F/C Sanitary 1) 48" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 1) PSX - 12-08 NYLO						0 lb 3000 lb 3378 lb 1440 lb 0 lb 0 lb 258 lb 0 lb 0 lb 8 lb ----- 8084 lb		Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. ADMIX = XYPEX C500-NF-RED 4. CASTING BY ICAST (HOE MC-315 F/C "SANITARY") REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.				
Rim: 386' Rim to Invert: 6' Slack: 1.004" Sump: 2.004" Step Position:												
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset		
Invert 1	380'	0°	0"	8" PVC SDR26	8.5"	PSX 12-08 NYLO	12"	12.129"	0"	0"		
Invert 2												
Invert 3												
Invert 4												
Invert 5												
Invert 6												
Invert 7												
Invert 8												

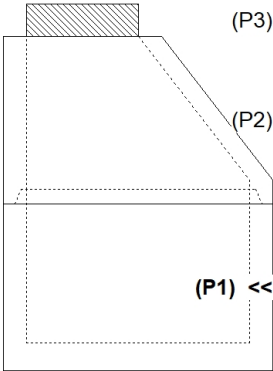


(P3)

(P2)


(P1) <<

RIGHT-SIDE UP VIEW (int. dimensions)




Invert: 1
Degree: 0°
Horz: 0"
Hole: 12"
Up(): 0"

FOR INVERT ONLY



Invert: 1
Degree: 0°
Horz: 0"
Hole: 12"
Up(): 0"

INSIDE WALL DIMENSIONS



(P1)

360° 270° 180° 90° 0°

6" 30" EXT

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 30" Height (Ext): 36"	Weight (Net): 3378 lb Volume (Net): 0.86cu.yd
----------------------------------	---------------------------------	--	--	--
