

Job Name: 25-1401 Irwin Landing Ph. 1
Job Location: Murfreesboro, TN
Contractor: Bear Construction LLC

Plant: Beaver Dam

6/9/2026 10:40:23 AM

Tech: S. Felletter

PC: Erica Bradley



Structure ID: R18

P3 GR28x28x8x3

GRADE RING F/F

P4) 28" x 28" - CASTING HEIGHT - 5"
P3) 28" x 28" - GRADE RING F/F - 3"
P2) 48" - MH FLAT TOP w/28"x28" Hole F/G - 12"
P1) 48" - MH BASE T/n - 60"
1) 48" - STORM INVERT CHANNEL - 1/4 HEIGHT
1) CASTING - JBS 3104-V SINGLE SET
1) 48" - Conseal CS-102 1.00"
2) 28" x 28" - Conseal CS-102 1.00"
3) Hole - 26
5) MH Step ML-10-TDS-NCR - 10"

0 lb
290 lb
1368 lb
4822 lb
1075 lb
250 lb
0 lb
0 lb
0 lb
0 lb

Structure Total: 7805 lb

Structure Notes:


1. PER ASTM C478 SPECIFICATIONS.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. CASTING BY ICAST (JBS-3104 SINGLE SET).

REINFORCING PER ASTM A615 (GRADE 60).

- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W..
- RISER/WALLS (As .12)
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

NOTES:

1. MANUFACTURED TO ASTM C-478 (LATEST REVISION).
2. CONCRETE = 4,000 PSI @ 28 DAYS.
3. REINFORCING: #4 BAR AS SHOWN (GRADE 60 KSI).
4. LIFTS: 2 EA. CONAC .8 TON WIRE ROPE ANCHORS REQUIRED.

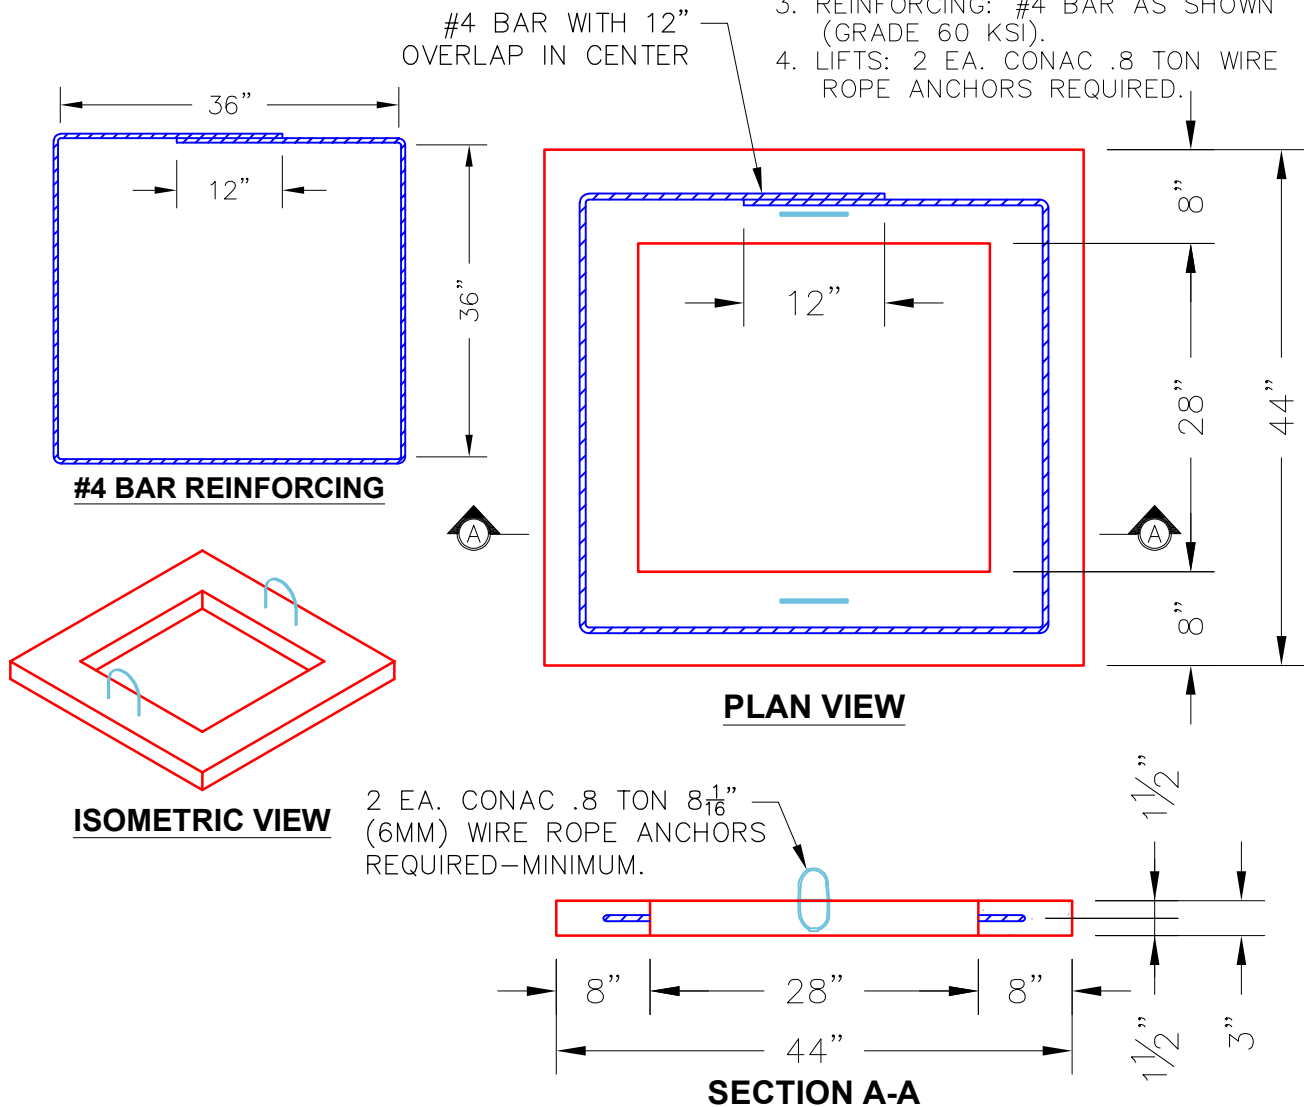

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Flat

Wall Thickness: 8"

Height (Ext): 3"

Weight (Net): 290 lb
Volume (Net): 0.07cu.yd
