

Job Name: 26-3750 - Stratman Johnson PUD Lot 10
Job Location: Evansville, IN
Contractor: Bieber Lawn, Lake, & Forestry LLC

Plant: Beaver Dam

Tech: J. Coppage

9/25/2026 12:27:05 PM

PC: T. Lewis



Structure ID: SSMH 600




P2 MH048LD12CDARED

MH FLAT TOP w/24" Hole ECC w/ConBlock-CDA Red

- P4) 24" - CASTING HEIGHT - 7"
P3) 24" - GRADE RING w/ConBlock-CDA Red - 4"
P2) 48" - MH FLAT TOP w/24" Hole ECC w/ConBlock-CDA Red - 12"
P1) 48" - MH BASE w/ConBlock-CDA Red - 24"
1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212
1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.)
1) 48" - MH INVERT CHANNEL EWSU w/ConBlock-CDA Red - FULL HEIGHT
1) CASTING - HOE MC-315 F/C Sanitary
1) 48" - Conseal CS-102 1.00" (Double)
2) 24" - Conseal CS-102 1.00" (Double)
1) PSX - 12-08 NYLO
1) PSX - 8QRS-S NYLO

- 0 lb
270 lb
1580 lb
2938 lb
0 lb
0 lb
1440 lb
258 lb
0 lb
0 lb
8 lb
6 lb
- Structure Notes:**
1. JR HOE MC-315 SANITARY PROVIDED BY ICAST.
2. PER ASTM C478 SPECIFICATIONS.
3. CONCRETE = 4,000 PSI AT 28 DAYS.
4. ADMIXTURE = CONBLOCK CDA RED.
5. REINFORCING PER ASTM A615 (GRADE 60).
- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.
- RISER/WALLS (As .12)
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.
6. **NO STEPS**

Structure Total: 6500 lb

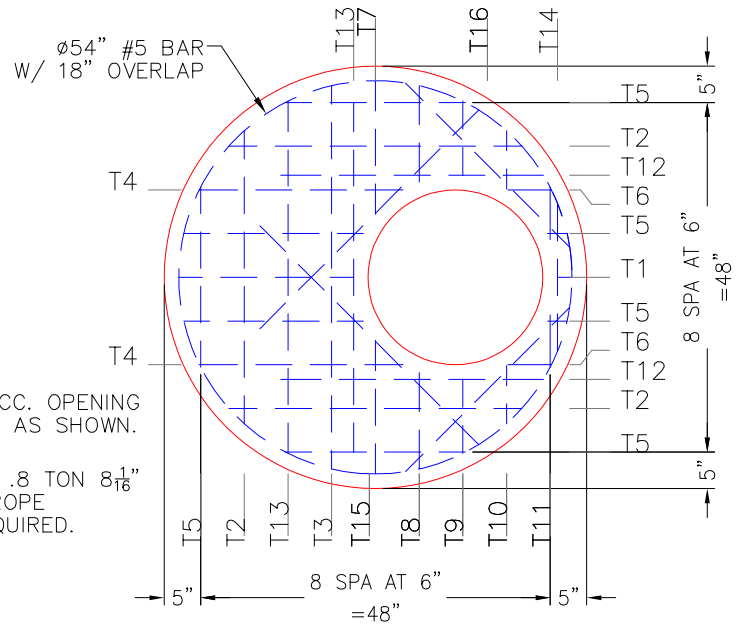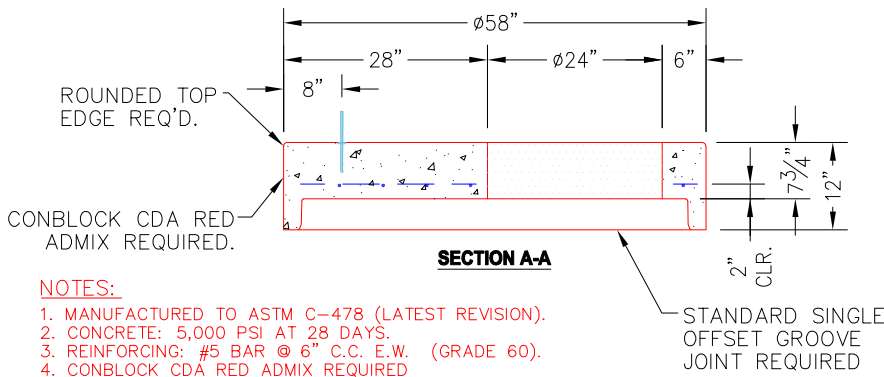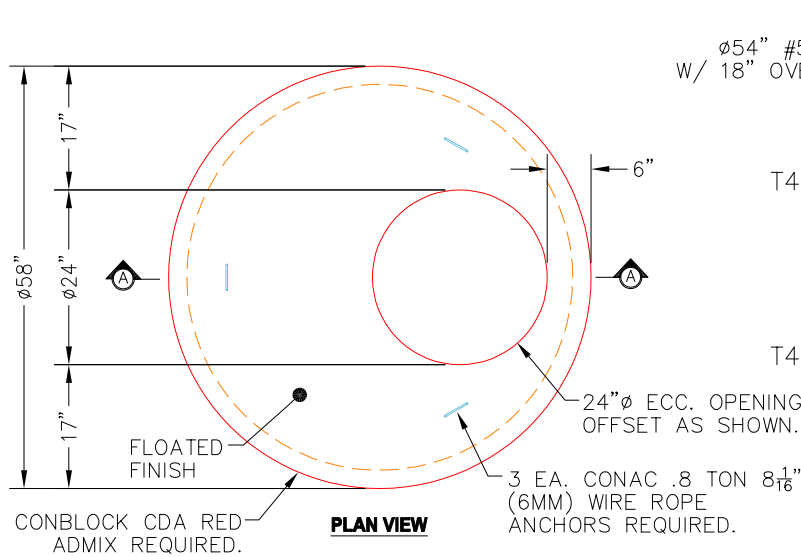

REBAR TAKEOFF (TOP LAYER)

BAR	SIZE	LENGTH	QTY	SHAPE
T1	5	24 in (2'-0")	1 pcs	STR
T2	5	40 in (3'-4")	3 pcs	STR
T3	5	53 in (4'-5")	1 pcs	STR
T4	5	28 in (2'-4")	2 pcs	STR
T5	5	25 in (2'-1")	5 pcs	STR
T6	5	6 in (0'-6")	2 pcs	STR
T7	5	18 in (1'-6")	2 pcs	STR
T8	5	13 in (1'-1")	2 pcs	STR
T9	5	10 in (0'-10")	2 pcs	STR
T10	5	8 in (0'-8")	2 pcs	STR
T11	5	7 in (0'-7")	2 pcs	STR
T12	5	36 in (3'-0")	2 pcs	STR
T13	5	48 in (4'-0")	2 pcs	STR
T14	5	20 in (1'-8")	1 pcs	STR
T15	5	42 in (3'-6")	2 pcs	DIAG
T16	5	32 in (2'-8")	2 pcs	DIAG

Total Pieces: 33 Pcs
Total Footage: 70.05 LF
Total Weight: 73.06 lbs (0.037 Tons)

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: Groove	Wall Thickness: 5"	Height (Ext): 12"	Weight (Net): 1580 lb Volume (Net): 0.39cu.yd
----------------------------------	----------------------------------	--------------------	-------------------	--
