

Job Name: 26-1987 Project Nova
Job Location: 200 South, IN 47882
Contractor: McCreary Concrete Products, Inc

Plant: 100
8/7/2026 9:24:06 AM

Tech: Jared - A
PC: Jay Ross Jarvis



Structure ID: STMH-1209A

P4 MH108RS54MH RISER

P6) 24" x 36" - CASTING HEIGHT - 6"
P5) 108" - MH FLAT TOP w/24" X 36" HOLE - 17"
P4) 108" - MH RISER - 54"
P3) 108" - MH RISER - 54"
P2) 108" - MH RISER - 96"
P1) 108" - MH BASE - 96"
4) 108" - Conseal CS-102 1.00"
1) 24" x 36" - Conseal CS-102 1.00"
1) Hole - 75
1) Hole - 62
26) MH Step ML-10-TDS-NCR - 10"


0 lb
12900 lb
16798 lb
16798 lb
29863 lb
36119 lb
0 lb
0 lb
0 lb
0 lb
0 lb
Structure Total: 112477 lb

Structure Notes: .
INDOT STATE PROJECT
1. INDOT MH TYPE M / ASTM C478 SPEC'S.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. NO INVERT CHANNEL.
4. REINFORCING PER ASTM A615 (GRADE 60).
- TOP SLAB = H20 LOADING.
- RISER/WALLS (As .30)
- FLOOR (As .62) #5 BARS AT 6" C.C.E.W.

Rim: 512.46' Rim to Invert: 26.45' Slack: 0.4" Sump: 6" Step Position: 90°

Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset
Invert 1										
Invert 2										
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)

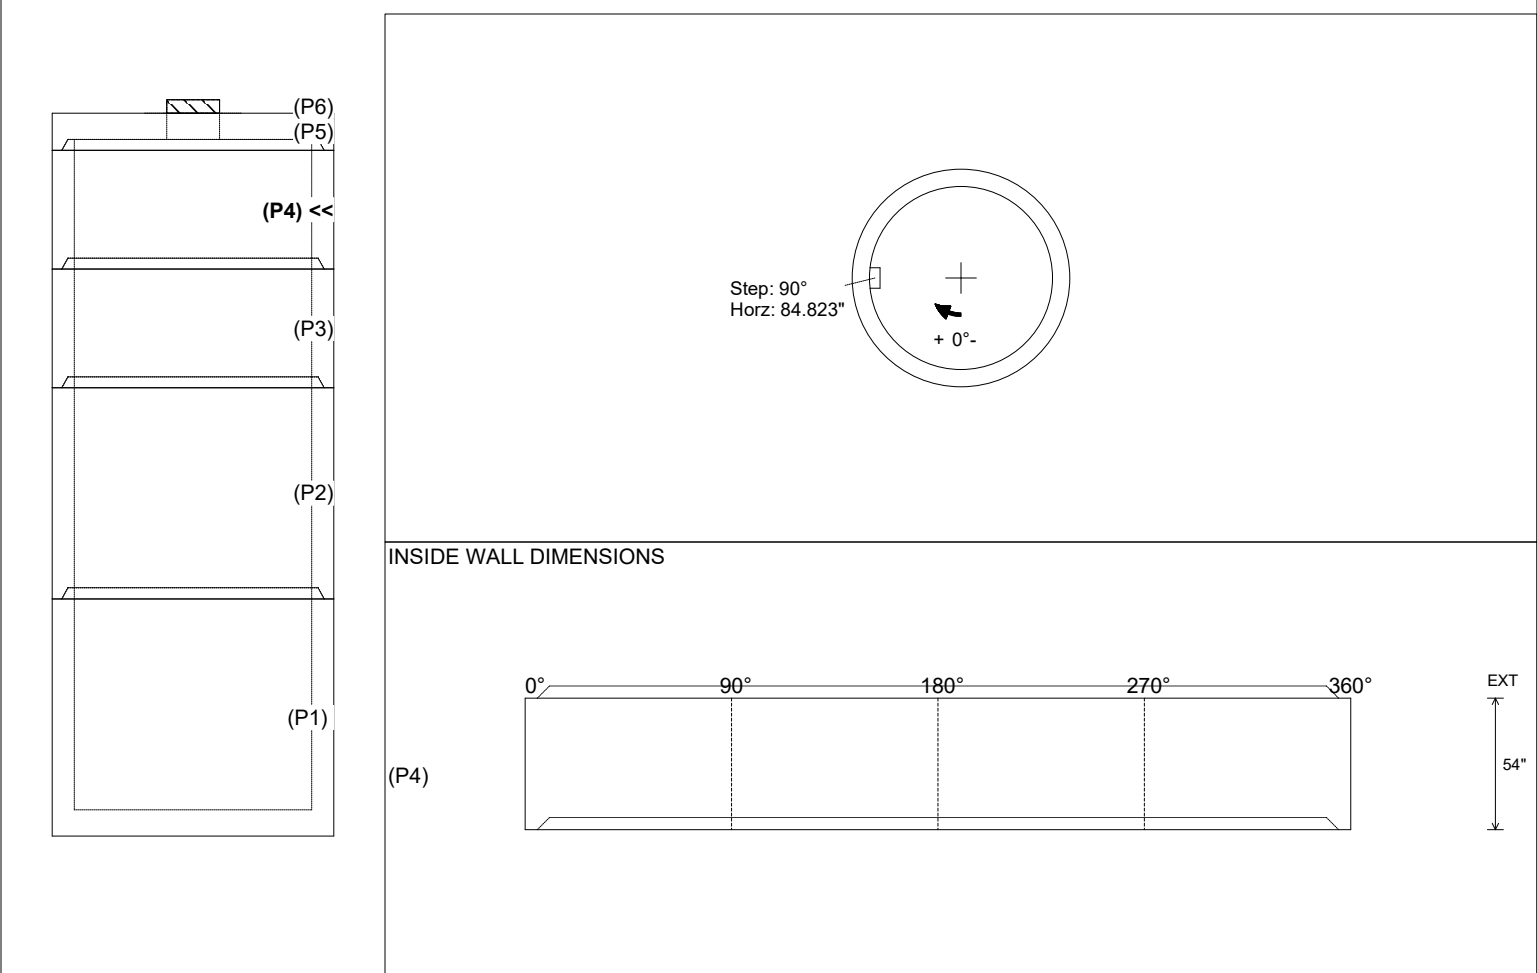

Coating (Int):
Coating (Ext):

Seam Up: Tongue
Seam Dn: Groove

Wall Thickness: 10"
Floor Height: 0"

Height (Int): 54"
Height (Ext): 54"

Weight (Net): 16798 lb
Volume (Net): 4.29cu.yd
