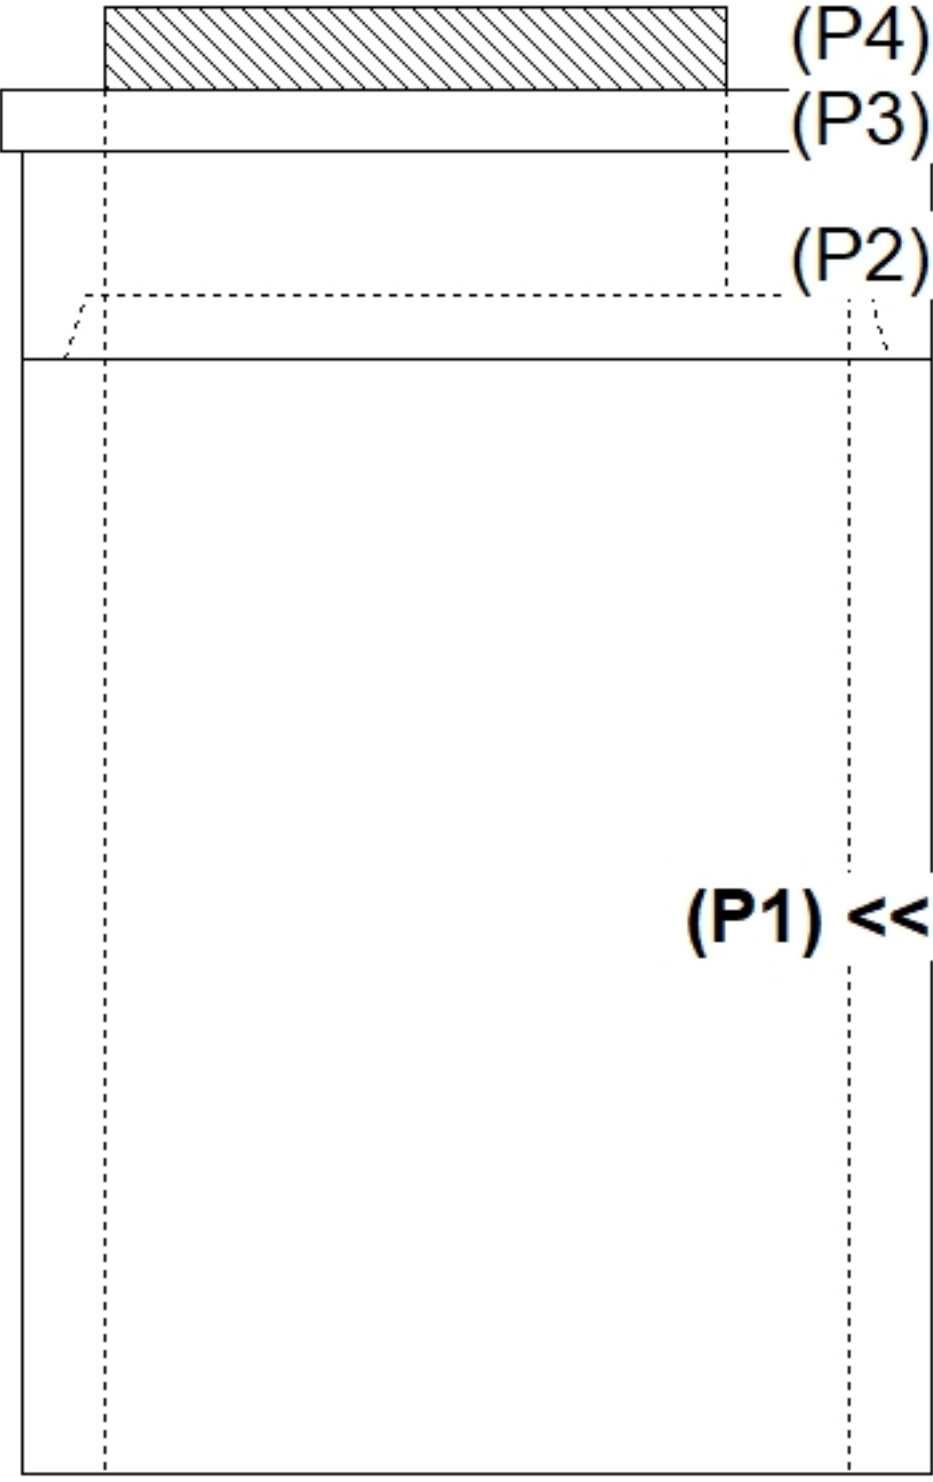
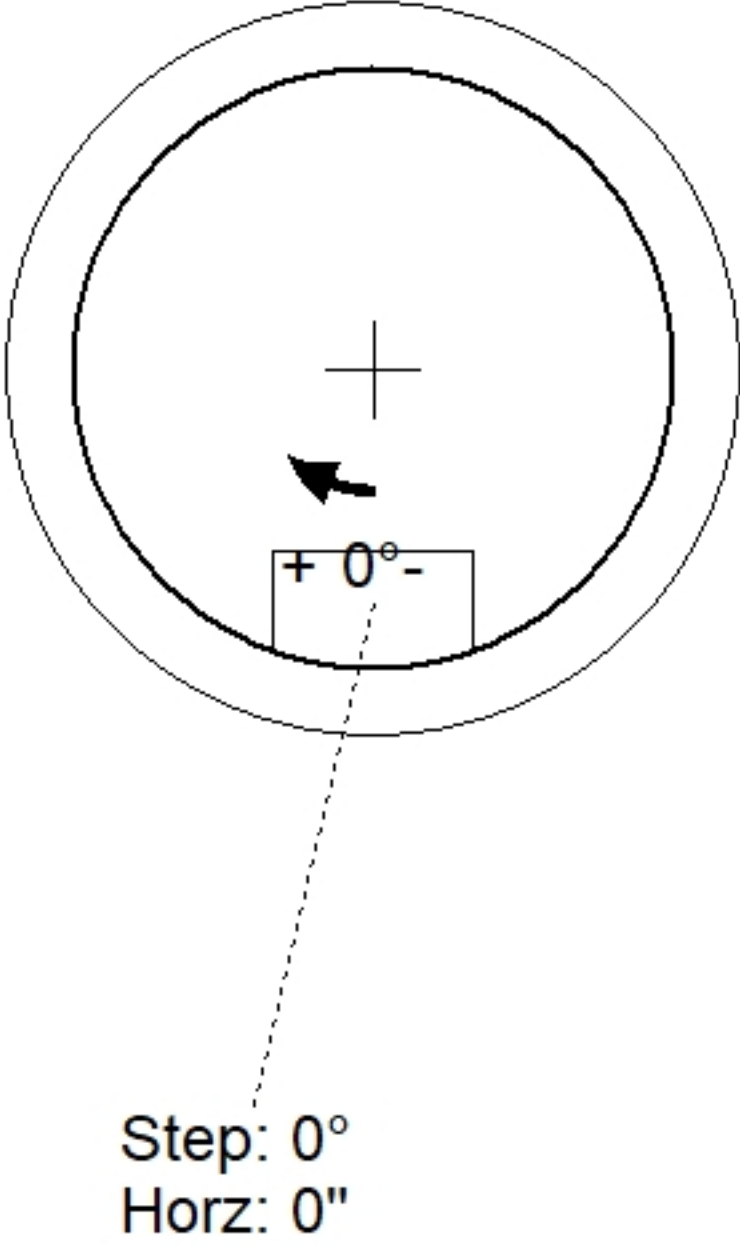
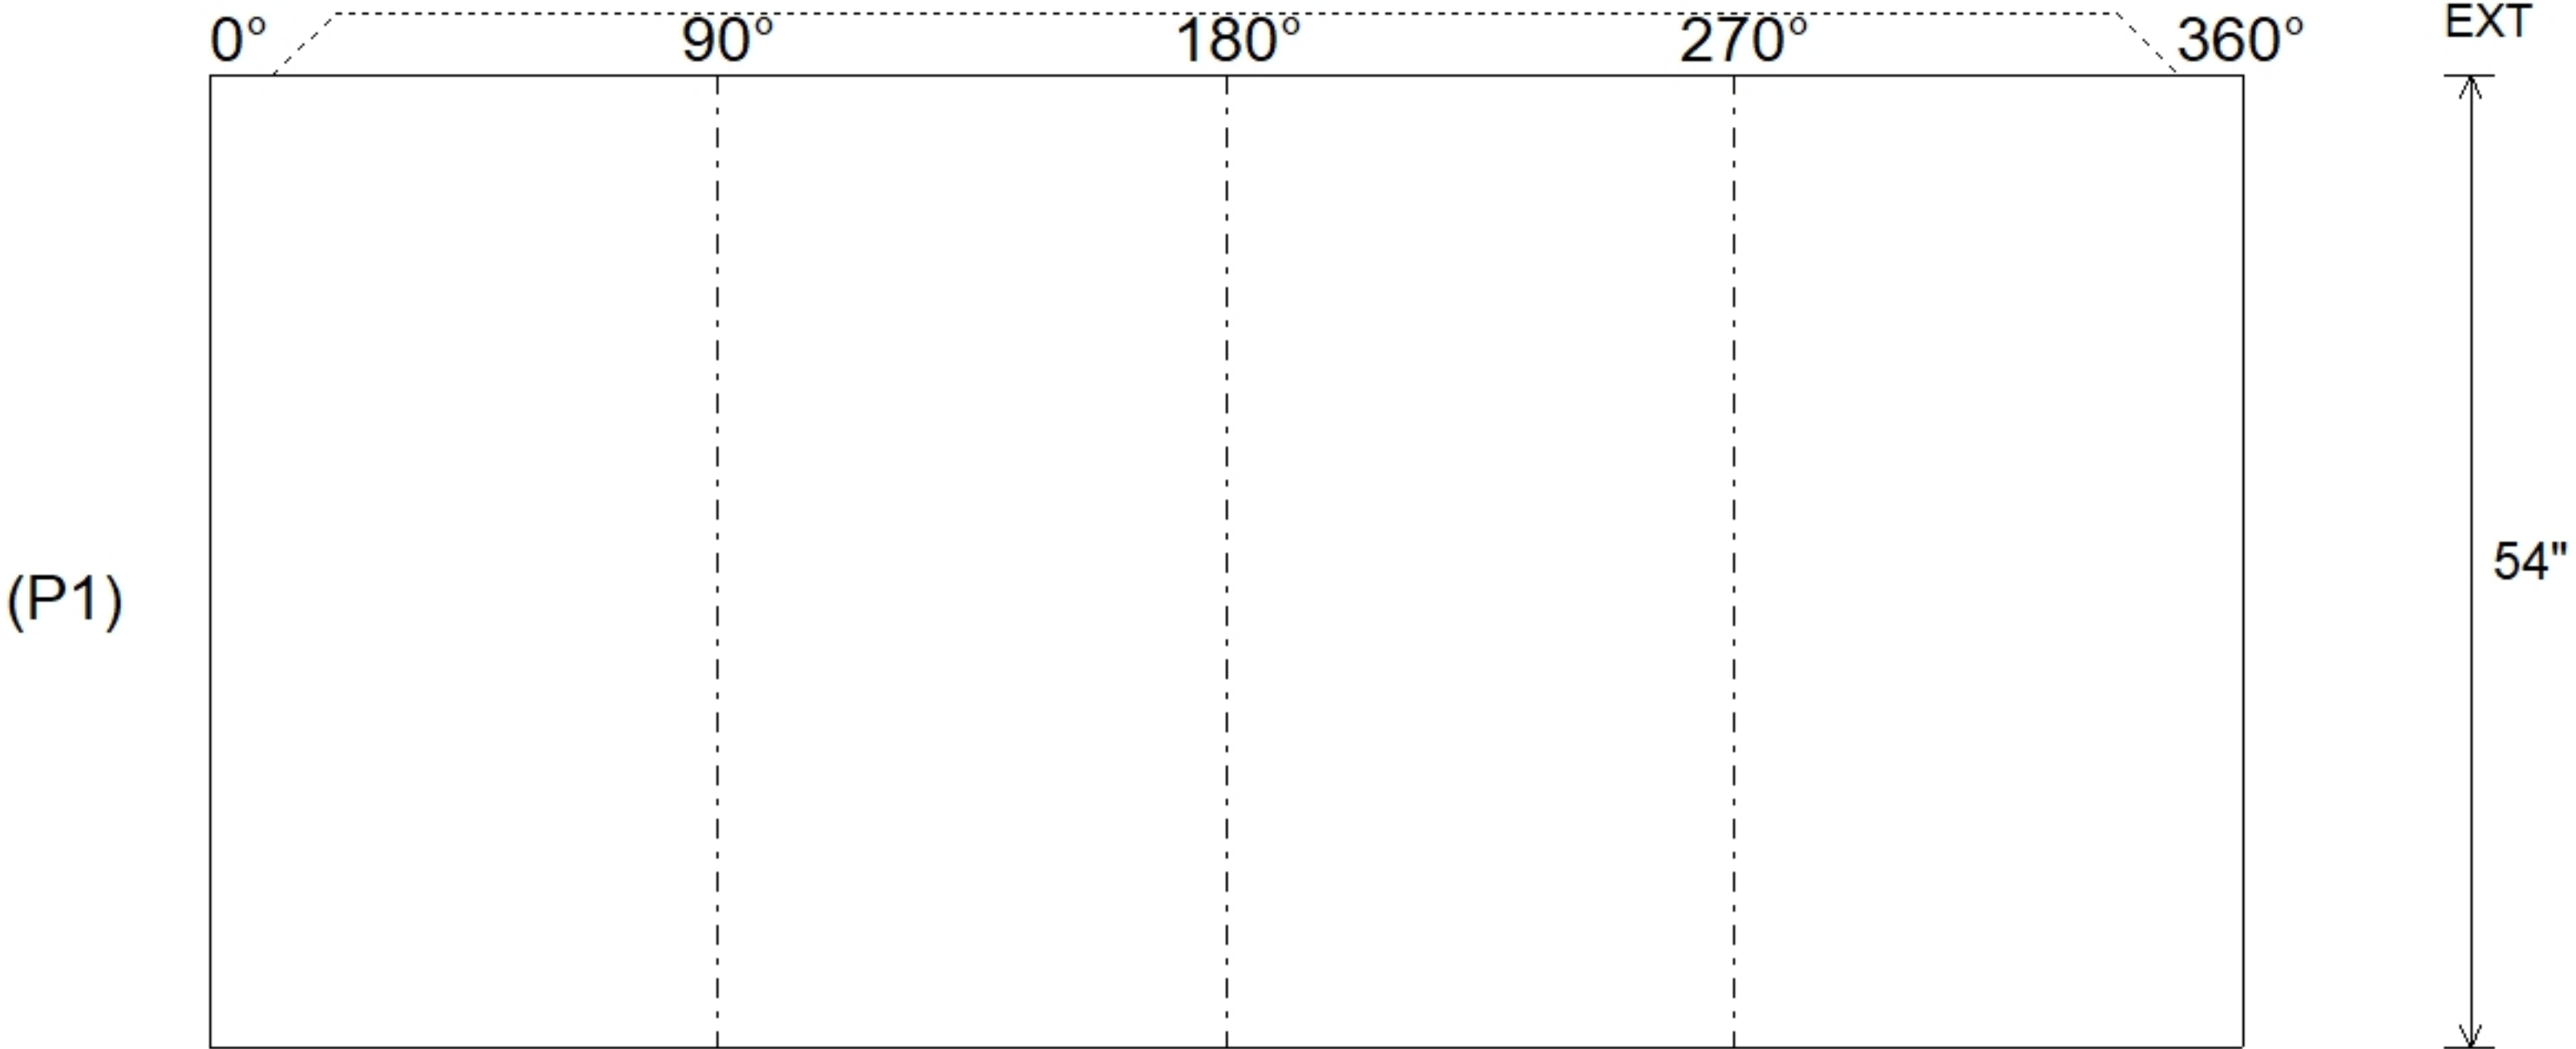


Job Name: 26-3046 903454 2026 Street Reconstruction					Plant: Beaver Dam		Tech: S. Felletter				
Job Location: Elk River, MN					7/17/2026 1:18:37 PM		PC: C. Goff				
Contractor: Contech Engineering Solutions											
Structure ID: Riser Set 2											
P1		MH036RS54			MH RISER T/F						
P4) 30" - CASTING HEIGHT - 4" P3) 30" - GRADE RING F/F - 3" P2) 36" - MH FLAT LID w/30in ECC Hole F/G - 10" P1) 36" - MH RISER T/F - 54" 1) CVSTENCILING 1) 36" - Conseal CS-102 1.00" 5) MH Step ML-10-TDS-NCR - 10"					0 lb 138 lb 683 lb 2278 lb 0 lb 0 lb 0 lb ----- Structure Total: 3099 lb		Structure Notes: . 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. 4" CASTING PROVIDED BY OTHERS. 4. CONTECH'S LOGO TO BE STENCILED ONTO THE OUTSIDE OF THE STRUCTURE. . REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W. - RISER/WALLS (As .12)				
Rim: 5.917' Rim to Invert: 0' Slack: 0" Sump: 0" Step Position: 0°											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (┘)	Offset	
Invert 1											
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											
RIGHT-SIDE UP VIEW (int. dimensions)											
											
INSIDE WALL DIMENSIONS											
											
Coating (Int):			Seam Up: Tongue		Wall Thickness: 4"		Height (Int): 54"		Weight (Net): 2278 lb		
Coating (Ext):			Seam Dn: Flat		Floor Height: 0"		Height (Ext): 54"		Volume (Net): 0.58cu.yd		
