

Job Name: 26-3046 903454 2026 Street Reconstruction
Job Location: Elk River, MN
Contractor: Contech Engineering Solutions

Plant: Beaver Dam

7/17/2026 1:18:26 PM

Tech: S. Felletter

PC: C. Goff



Structure ID: Riser Set 4

P2 MH036LD10-30ECC

MH FLAT LID w/30in ECC Hole F/G

- P4) 30" - CASTING HEIGHT - 4"
P3) 30" - GRADE RING F/F - 3"
P2) 36" - MH FLAT LID w/30in ECC Hole F/G - 10"
P1) 36" - MH RISER T/F - 54"
1) CVSTENCILING
1) 36" - Conseal CS-102 1.00"
5) MH Step ML-10-TDS-NCR - 10"



- 0 lb
138 lb
683 lb
2278 lb
0 lb
0 lb
0 lb
- Structure Notes:**
1. PER ASTM C478 SPECIFICATIONS.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. 4" CASTING PROVIDED BY OTHERS.
4. CONTECH'S LOGO TO BE STENCILED ONTO THE OUTSIDE OF THE STRUCTURE.

Structure Total: 3099 lb

REINFORCING PER ASTM A615 (GRADE 60).
- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.
- RISER/WALLS (As .12)

NOTES:

1. MANUFACTURED TO ASTM C-478 (LATEST REVISION).
2. CONCRETE: 4,000 PSI AT 28 DAYS.
3. REINFORCING: #5 BAR @ 6" O.C. E.W. (GRADE 60).

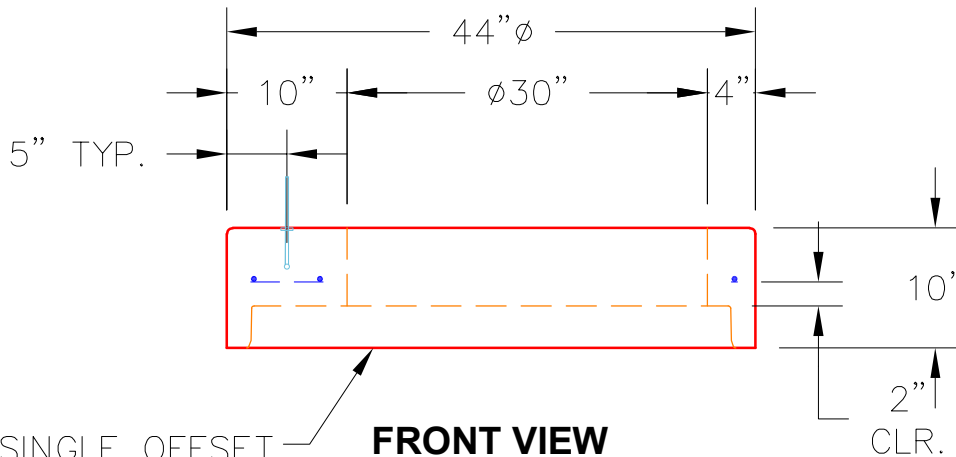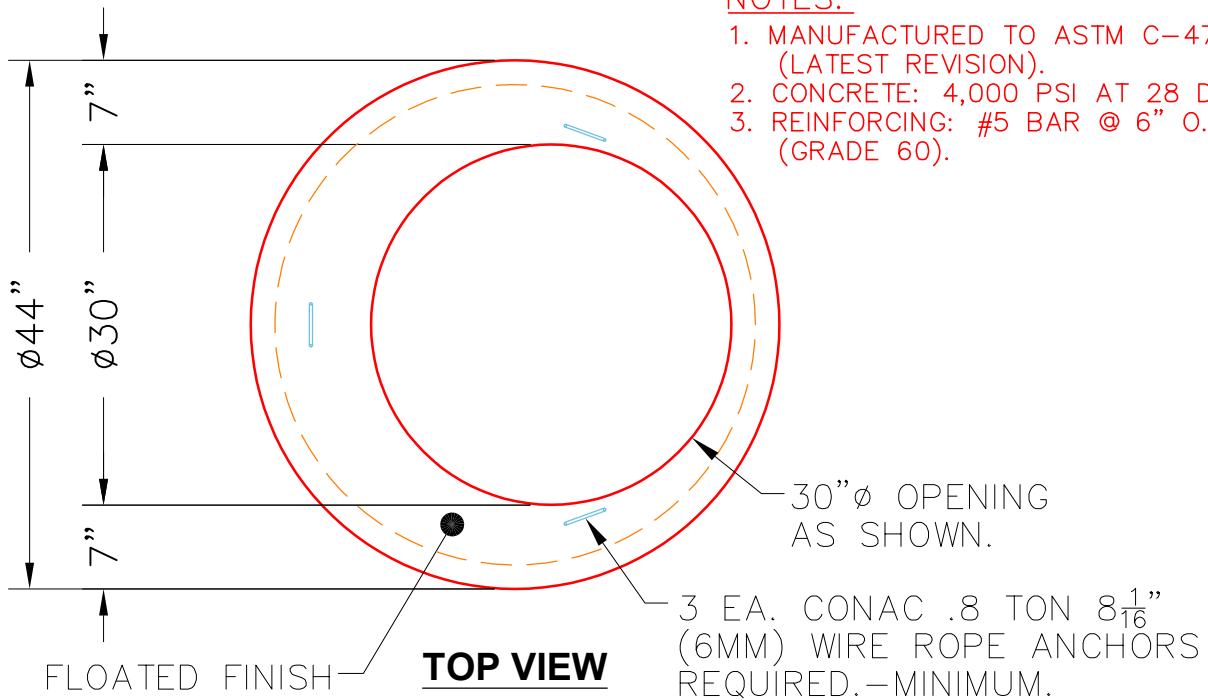

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Groove

Wall Thickness: 4"

Height (Ext): 10"

Weight (Net): 683 lb
Volume (Net): 0.17cu.yd
