

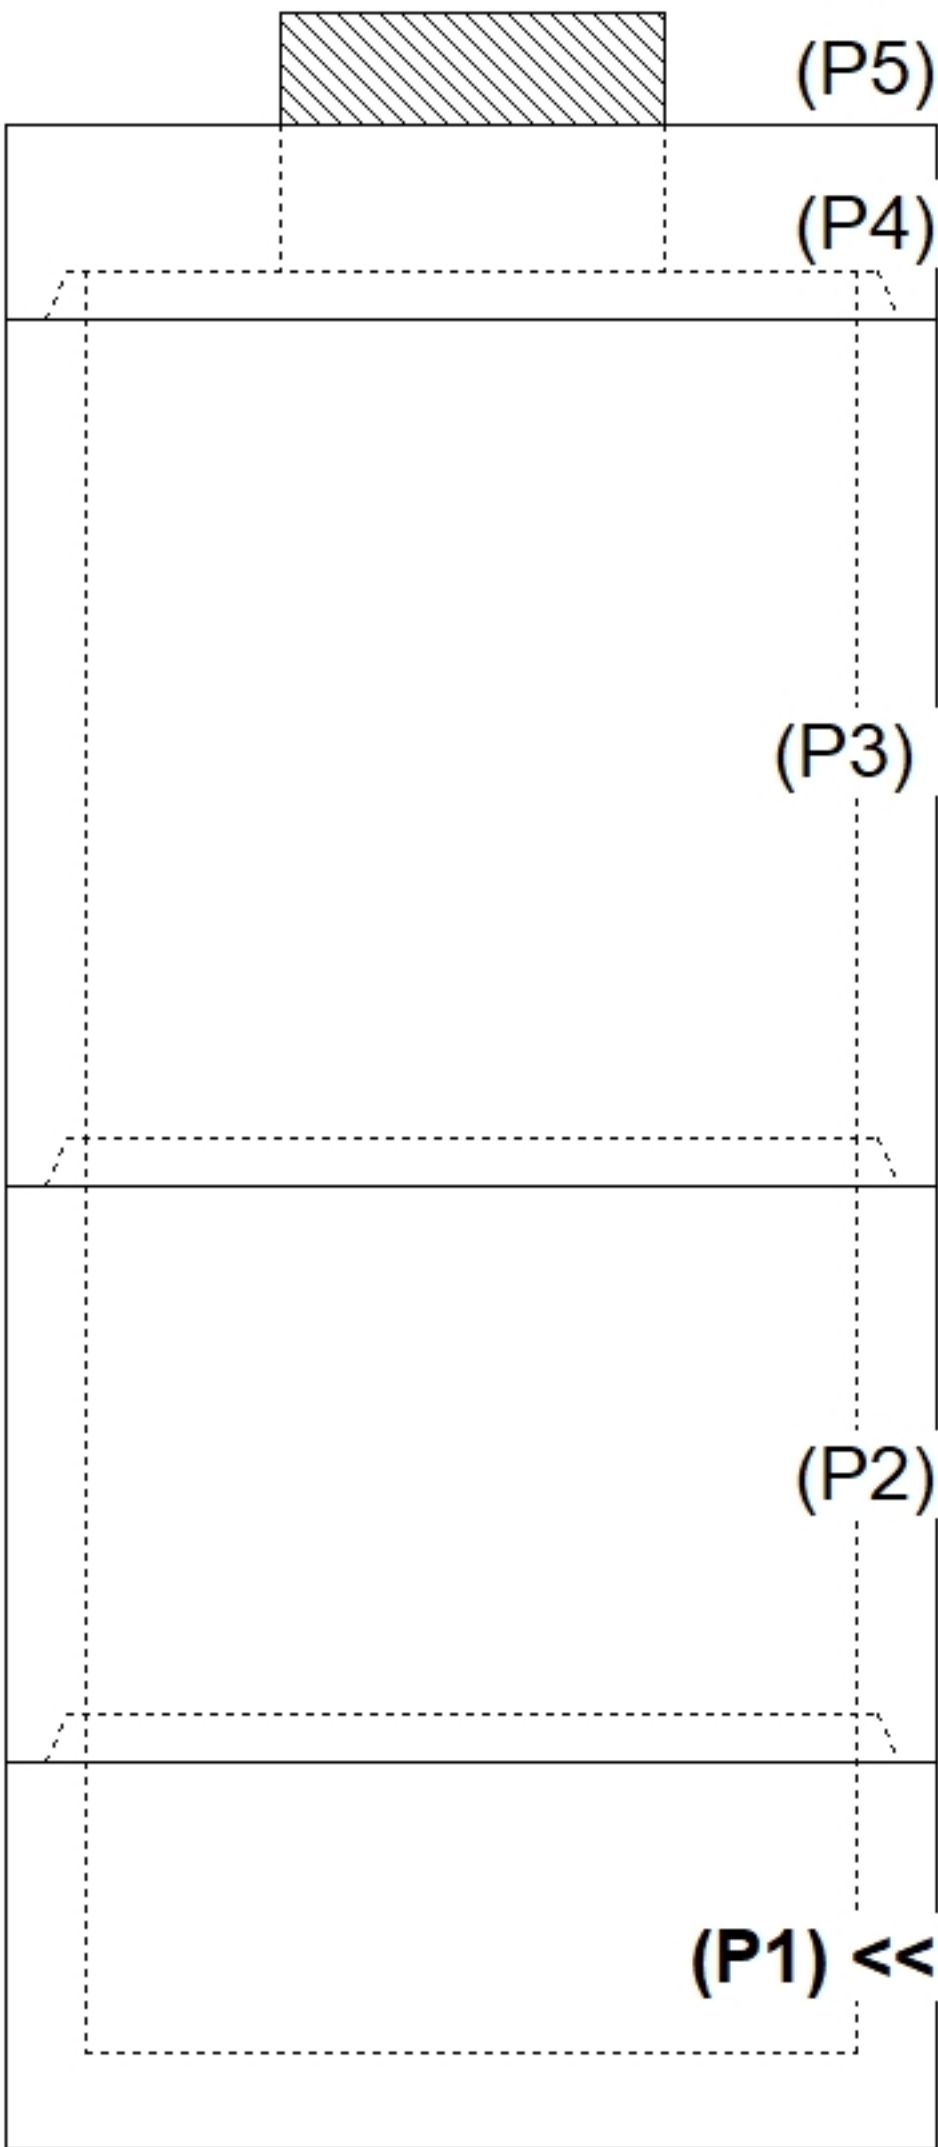
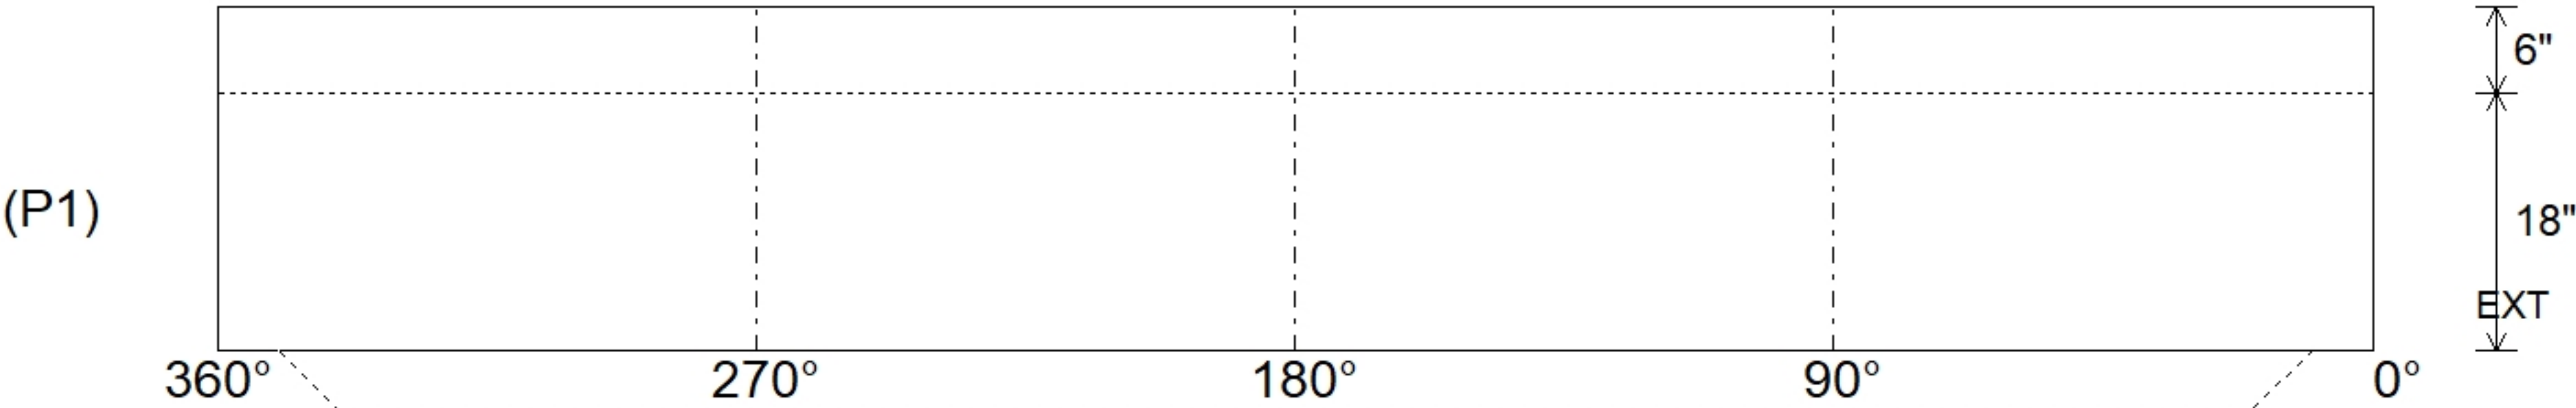


Job Name: 26-2975 ADS Dunlap Multifamily Job Location: Louisville, KY Contractor: ADS Advanced Drainage Systems, Inc.					Plant: Beaver Dam 7/17/2026 12:56:12 PM		Tech: S. Felletter PC: T. Ryan						
Structure ID: QL1													
P1		MH048BA18		MH BASE T/n									
P5) 24" - CASTING HEIGHT - 7" P4) 48" - MH FLAT LID w/24" Center Hole F/G - 12" P3) 48" - MH RISER SPECIAL T/G - 54" P2) 48" - MH RISER T/G - 36" P1) 48" - MH BASE T/n - 18" 1) ASSEMBLY REQUIRED 1) CASTING - HOE MC-375 F/C Storm 3) 48" - Conseal CS-102 1.00" 1) 24" - Conseal CS-102 1.00" 2) Hole - 14						0 lb 1580 lb 3593 lb 2515 lb 2588 lb 0 lb 271 lb 0 lb 0 lb 0 lb ----- 10546 lb		Structure Notes: . 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY ICAST (HOE MC-375 F/C "STORM"). 4. P2 & P3 RISERS TO BE MECHANICALLY ATTACHED PRIOR TO INTERNAL INSTALLATION/DELIVERY . REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W. - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.					
Rim: 636.88'		Rim to Invert: 3.83'		Slack: -0.04"		Sump: 81"		Step Position:					
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset			
Invert 1													
Invert 2													
Invert 3													
Invert 4													
Invert 5													
Invert 6													
Invert 7													
Invert 8													
RIGHT-SIDE UP VIEW (int. dimensions)  UPSIDE-DOWN VIEW (int. dimenions) 													
 INSIDE WALL DIMENSIONS 													
Coating (Int): Coating (Ext):				Seam Up: Tongue Seam Dn: n/a		Wall Thickness: 5" Floor Height: 6"		Height (Int): 18" Height (Ext): 24"		Weight (Net): 2588 lb Volume (Net): 0.66cu.yd			
