




Job Name: 24-4208 - KYTC Christian Co. Call 100 (ID 241018) Job Location: Hopkinsville, KY Contractor: Scotty's Contracting & Stone, LLC				Plant: Beaver Dam 7/30/2026 8:55:29 AM		Tech: J. Horsley PC: C. Goff					
Structure ID: 246 (428+75 LT)											
P1 BX2430-08BA30				BOX BASE 8inW, 8inF F/n							
P2) 24" x 30" - CASTING HEIGHT - 3.75" P1) 24" x 30" - BOX BASE 8inW, 8inF F/n - 30" 1) CASTING - HOE KY-460-11 F/G (DBI 11) 1) 24" x 30" - Conseal CS-102 1.00" 1) Hole - 20				0 lb 3844 lb 421 lb 0 lb 0 lb ----- 0 lb Structure Total: 4265 lb		Structure Notes: . **KYTC STATE PROJECT** 1. KYTC DBI TYPE 11 / ASTM C-913 SPEC'S. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY ICAST (HOE KY-460-11 F/G). REINFORCING PER ASTM A615 (GRADE 60). - WALLS (As .31) #5 BARS AT 12" C.C.E.W.. - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.					
Rim: 539.9'				Rim to Invert: 2.92'		Slack: 1.29"		Sump: 0"		Step Position:	
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	536.98'	270°	23"	15" HDPE	17.6"	Hole 20	20"	20"	-1.3"	0"	
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											

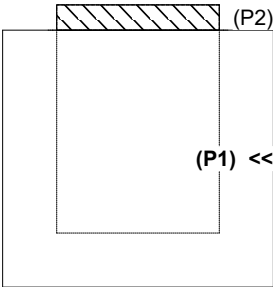



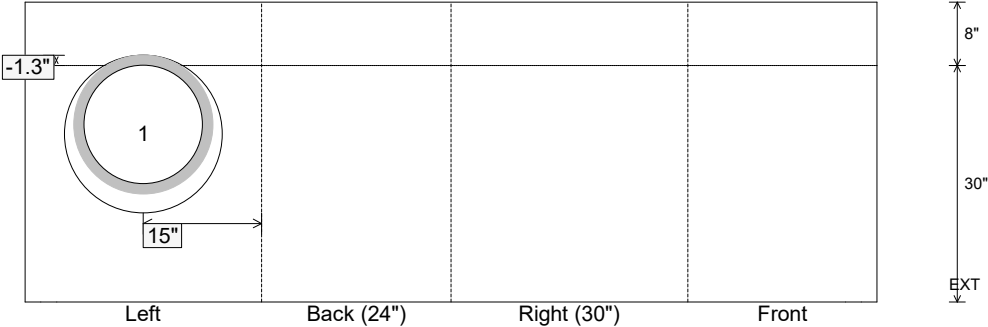

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: n/a	Wall Thickness: 8" Floor Height: 8"	Height (Int): 30" Height (Ext): 38"	Weight (Net): 3844 lb Volume (Net): 0.98cu.yd
----------------------------------	-------------------------------	--	--	--
