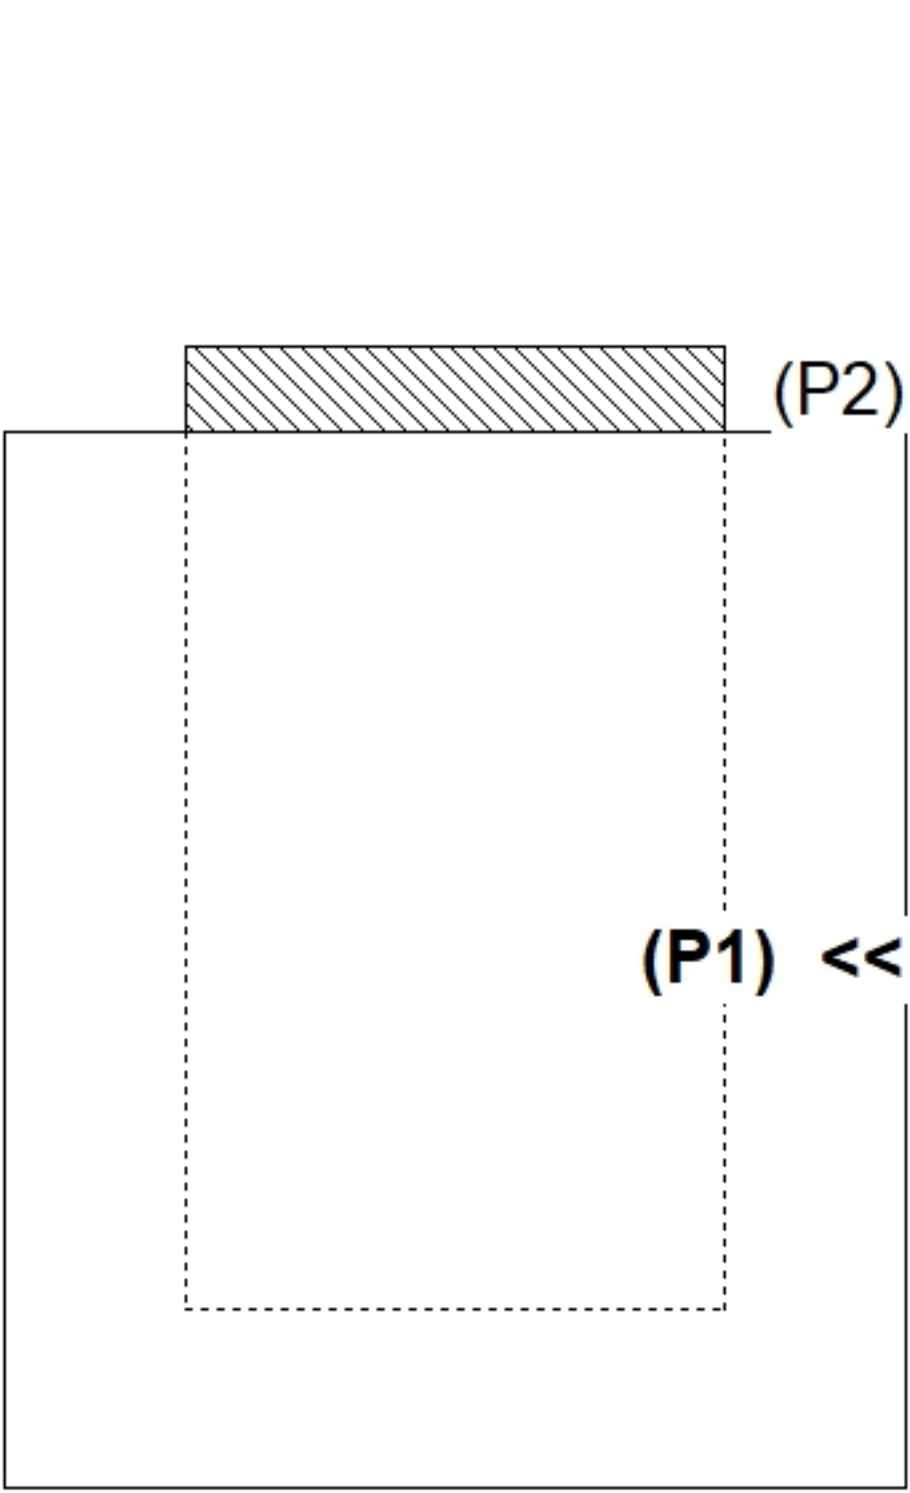
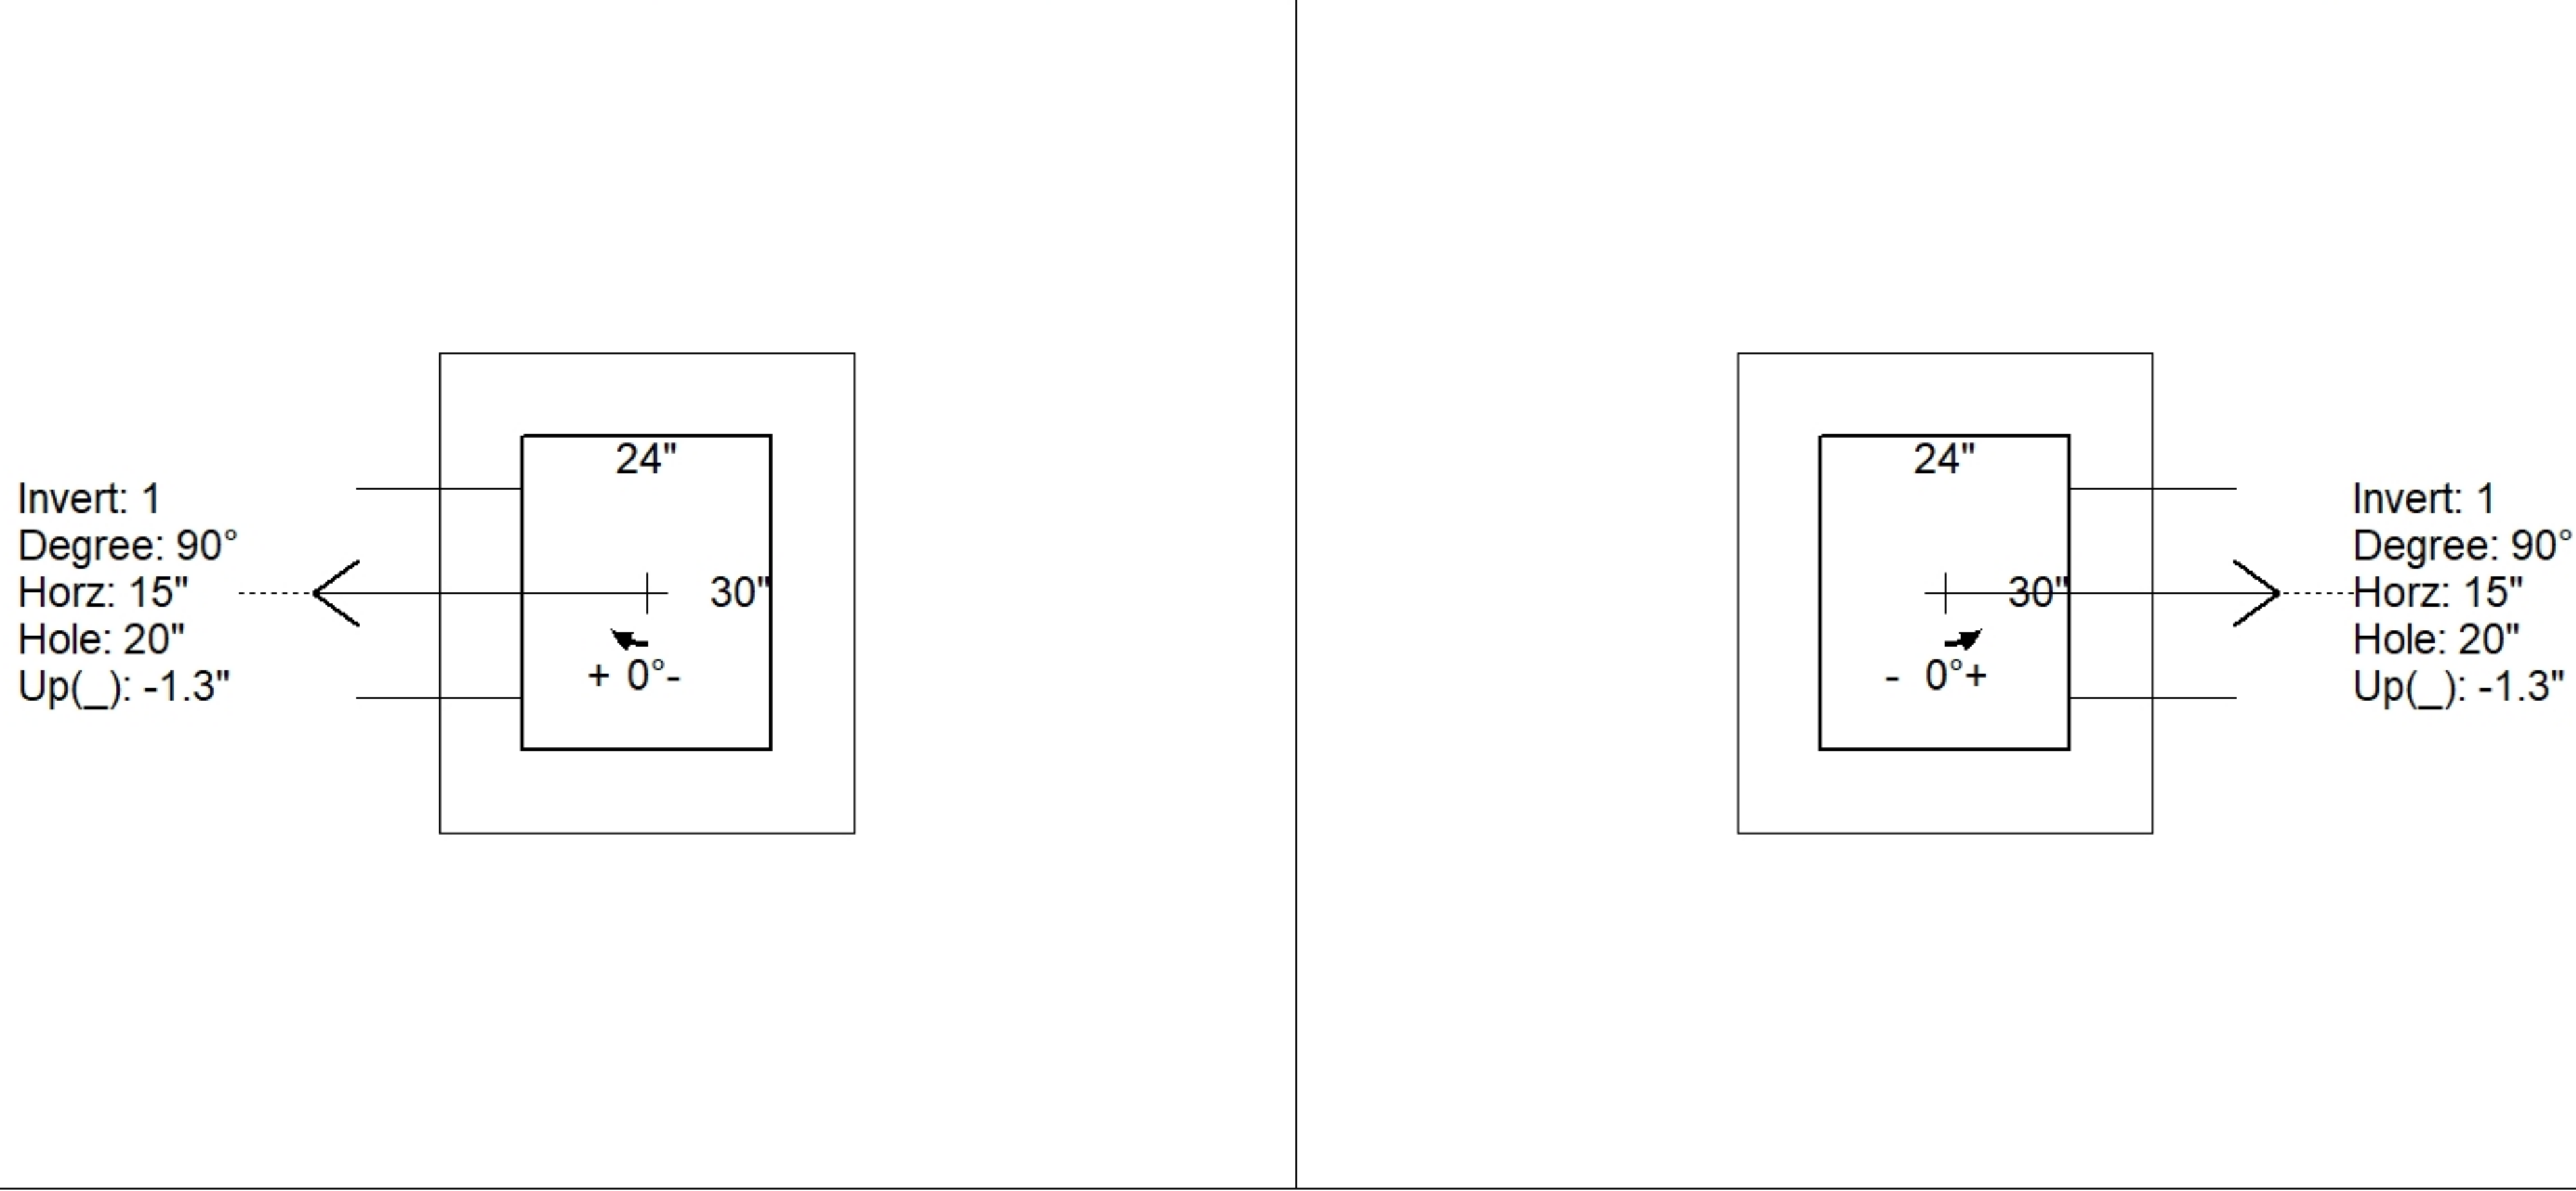
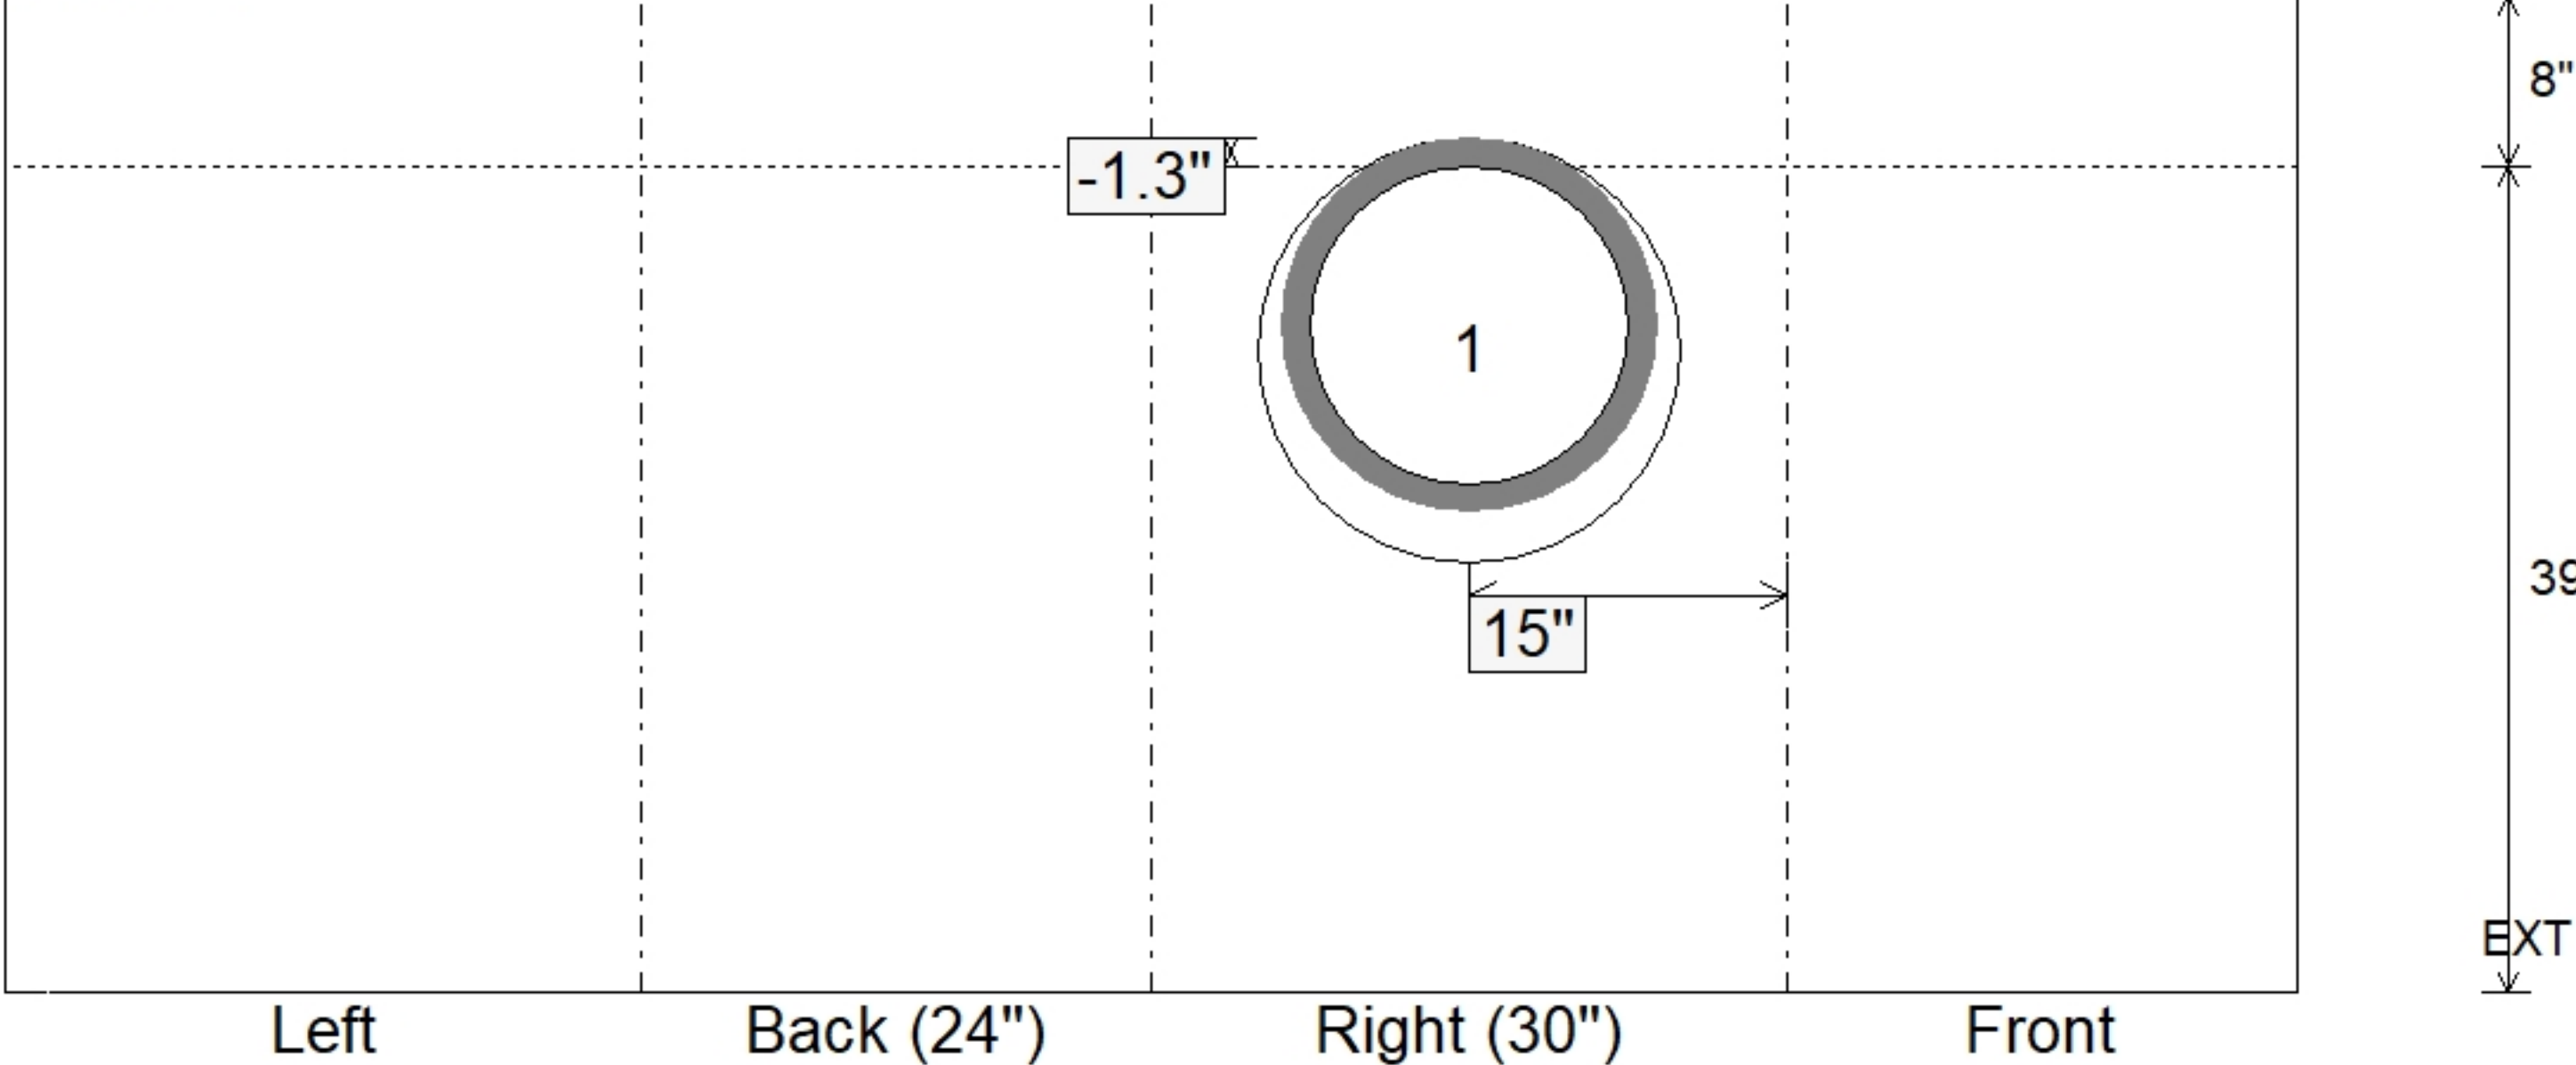


Job Name: 24-4208 - KYTC Christian Co. Call 100 (ID 241018) Job Location: Hopkinsville, KY Contractor: Scotty's Contracting & Stone, LLC					Plant: Beaver Dam 8/3/2026 4:20:52 PM		Tech: J. Horsley PC: C. Goff						
Structure ID: 284 (443+60 RT)													
P1		BX24300808VF			BOX BASE 8inW, 8inF, Variable Ht F/n								
P2) 24" x 30" - CASTING HEIGHT - 3.75" P1) 24" x 30" - BOX BASE 8inW, 8inF, Variable Ht F/n - 39" 1) CASTING - HOE KY-460-11 F/G (DBI 11) 1) 24" x 30" - Conseal CS-102 1.00" 1) Hole - 20						0 lb 4690 lb 421 lb 0 lb 0 lb ----- 5111 lb Structure Total:		Structure Notes: . **KYTC STATE PROJECT** 1. KYTC DBI TYPE 11 / ASTM C-913 SPEC'S. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY ICAST (HOE KY-460-11 F/G). . REINFORCING PER ASTM A615 (GRADE 60). - WALLS (As .31) #5 BARS AT 12" C.C.E.W.. - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.					
Rim: 528.5'		Rim to Invert: 3.63'		Slack: 0.81"		Sump: 0"		Step Position:					
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset			
Invert 1	524.87'	90°	23"	15" HDPE	17.6"	Hole 20	20"	20"	-1.3"	0"			
Invert 2													
Invert 3													
Invert 4													
Invert 5													
Invert 6													
Invert 7													
Invert 8													
RIGHT-SIDE UP VIEW (int. dimensions)						UPSIDE-DOWN VIEW (int. dimenions)							
													
INSIDE WALL DIMENSIONS													
Coating (Int): Coating (Ext):			Seam Up: Flat Seam Dn: n/a		Wall Thickness: 8" Floor Height: 8"		Height (Int): 39" Height (Ext): 47"		Weight (Net): 4690 lb Volume (Net): 1.2cu.yd				
