

Job Name: 25-1601C Spring Creek Parkway  
 Job Location: Clarksville, TN  
 Contractor: Byard Construction, LLC

Plant: Beaver Dam  
 8/7/2026 1:07:52 PM

Tech: J. Coppage  
 PC: A. Chambers



## Structure ID: 3in GR



### P5 GR28x34x6x3

### GRADE RING

P13) 28" x 34" - GRADE RING - 3"  
 P12) 28" x 34" - GRADE RING - 3"  
 P11) 28" x 34" - GRADE RING - 3"  
 P10) 28" x 34" - GRADE RING - 3"  
 P9) 28" x 34" - GRADE RING - 3"  
 P8) 28" x 34" - GRADE RING - 3"  
 P7) 28" x 34" - GRADE RING - 3"  
 P6) 28" x 34" - GRADE RING - 3"  
 P5) 28" x 34" - GRADE RING - 3"  
 P4) 28" x 34" - GRADE RING - 3"  
 P3) 28" x 34" - GRADE RING - 3"  
 P2) 28" x 34" - GRADE RING - 3"  
 P1) 28" x 34" - GRADE RING - 3"  
 13) 28" x 34" - Conseal CS-102 1.00"

Structure Notes:  
 1. PER ASTM C913 SPECIFICATIONS.  
 2. CONCRETE = 4,000 PSI AT 28 DAYS.  
 3. REINFORCING PER ASTM A615 (GRADE 60).  
 - AS SHOWN BELOW

224 lb  
 224 lb  
 224 lb  
 224 lb  
 224 lb  
 224 lb  
 224 lb  
 224 lb  
 224 lb  
 224 lb  
 224 lb  
 224 lb  
 224 lb  
 224 lb  
 224 lb  
 0 lb  
 Structure Total: 2906 lb

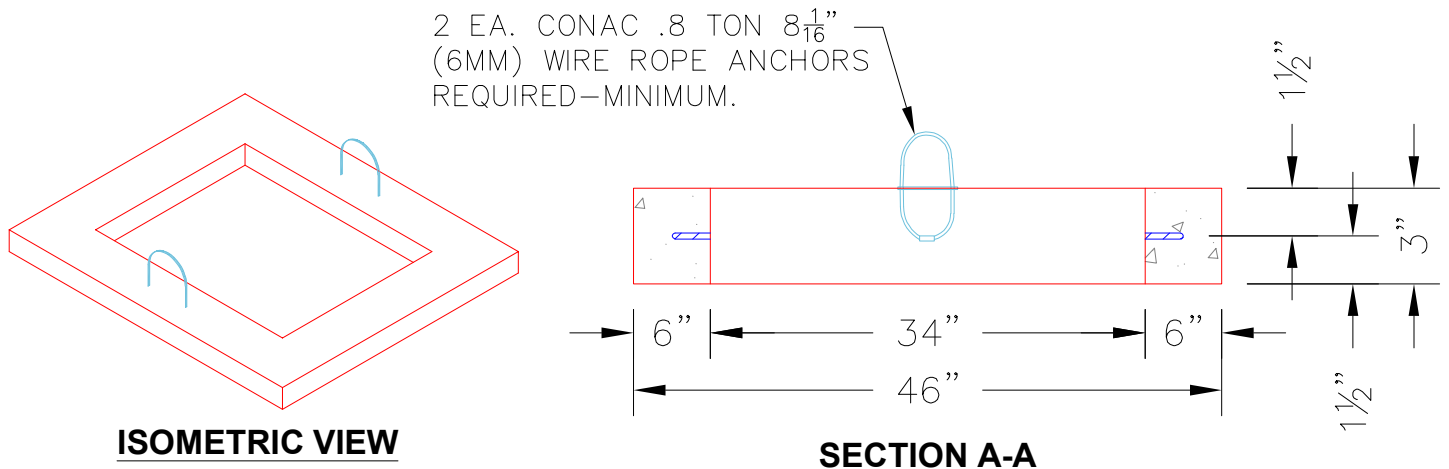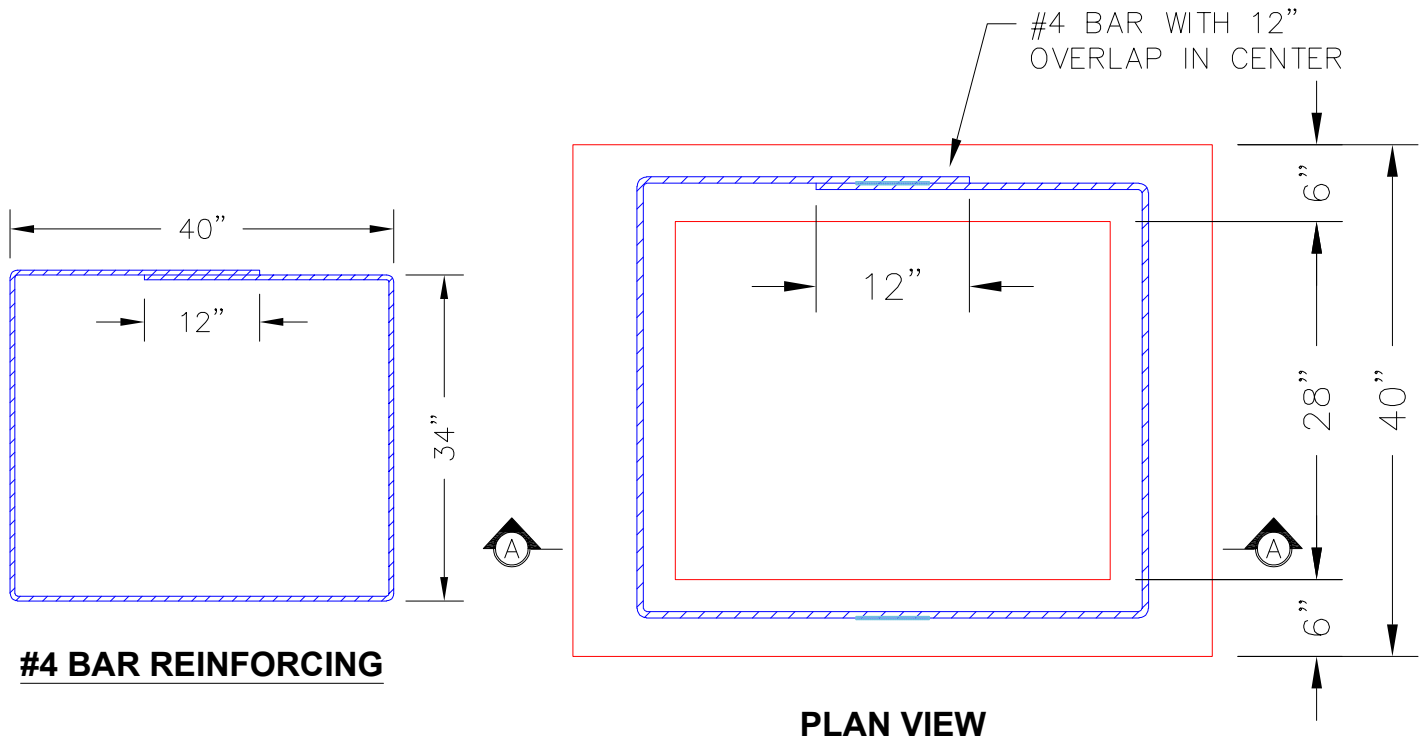

|                                  |                                |                    |                  |                                                 |
|----------------------------------|--------------------------------|--------------------|------------------|-------------------------------------------------|
| Coating (Int):<br>Coating (Ext): | Seam Up: Flat<br>Seam Dn: Flat | Wall Thickness: 6" | Height (Ext): 3" | Weight (Net): 224 lb<br>Volume (Net): 0.06cu.yd |
|----------------------------------|--------------------------------|--------------------|------------------|-------------------------------------------------|
