

Job Name: 25-2952 - KYTC Jefferson Co Call 106 (251315)

Job Location: Indiana, KY

Contractor: Louisville Paving and Construction

Plant: 100

6/17/2026 4:44:40 PM

Tech: J. Horsley - A

PC: J. Jarvis



Structure ID: 57

P2 BX2430-08R30

BOX RISER 8inW F/G

P3) 24" x 30" - P.I.P. - BY OTHERS - 8"

P2) 24" x 30" - BOX RISER 8inW F/G - 30"

P1) 24" x 30" - BOX BASE 8inW, 8inF, Variable Ht T/n - 31"

2) 24" x 30" - Conseal CS-102 1.00"

2) Hole - 24

1) Hole - 16

2) Hole - 4

0 lb

2668 lb

3693 lb

0 lb

0 lb

0 lb

0 lb

Structure Total: 6361 lb

Structure Notes:

** KYTC STATE PROJECT **

1. PER KYTC DBI TYPE 16G / ASTM C-913 SPECS

2. CONCRETE: 4,000 PSI AT 28 DAYS

3. REINFORCEMENT: #5 BAR @ 12" C.C. E.W. (GRADE 60) - 2" MIN. REBAR CLEARANCE (TYP)

4. HOE KY-230G FRAME & GRATE SUPPLIED BY OTHERS - POURED IN PLACE BY OTHERS

5. WET STICK #5 BAR @ 12" C.C. (GRADE 60) 12" OUT TOP OF RISER WALLS FOR FIELD POUR TIE-IN - 4" MIN. PENETRATION INTO WALLS

Rim: 551.84'

Rim to Invert: 5.75'


Slack: 0"

Sump: 0"


Step Position:

Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1										
Invert 2										
Invert 3	549.67'	180°	20"	12" CMP	13"	Hole 16	16"	16"	8"	0"
Invert 4	550.51'	90°	23"	4" WEEP HOLE	4"	Hole 4	4"	4"	20"	0"
Invert 5	550.51'	270°	23"	4" WEEP HOLE	4"	Hole 4	4"	4"	20"	0"
Invert 6										
Invert 7										
Invert 8										


WET STICK 16" LONG #5 BAR @ 12" C.C. E.W. (GRADE 60) 12" OUT TOP OF RISER WALLS FOR FIELD POUR TIE-IN - 4" MIN. PENETRATION INTO WALLS

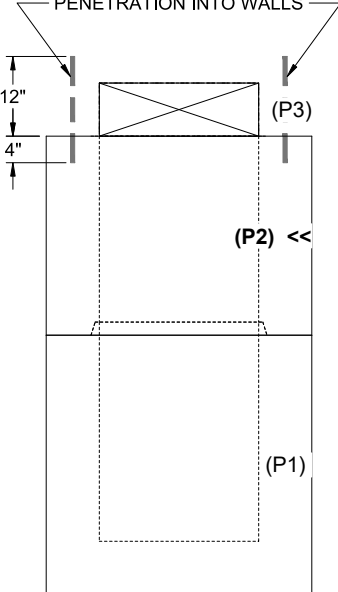

RIGHT-SIDE UP VIEW (int. dimensions)

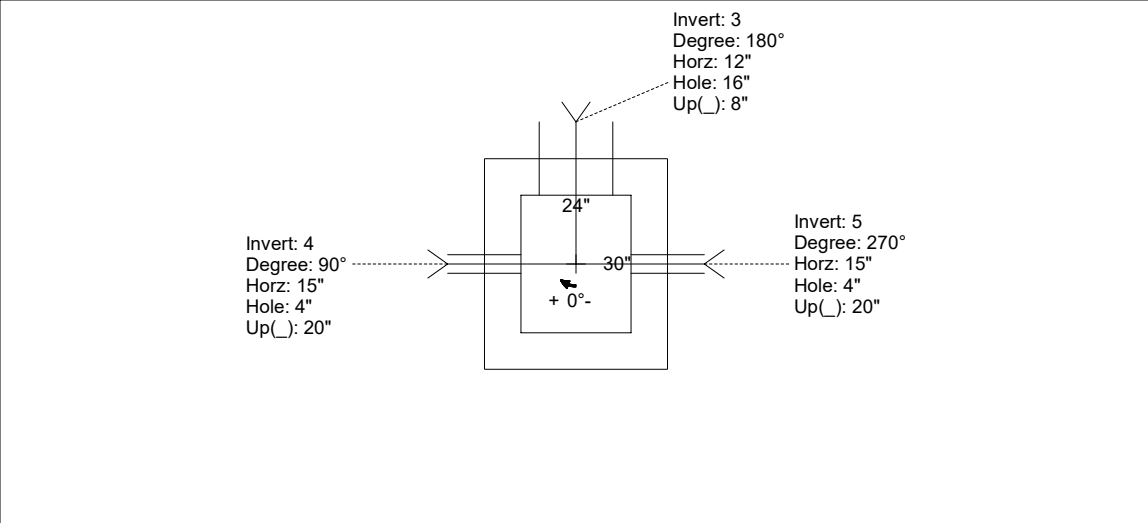

INSIDE WALL DIMENSIONS

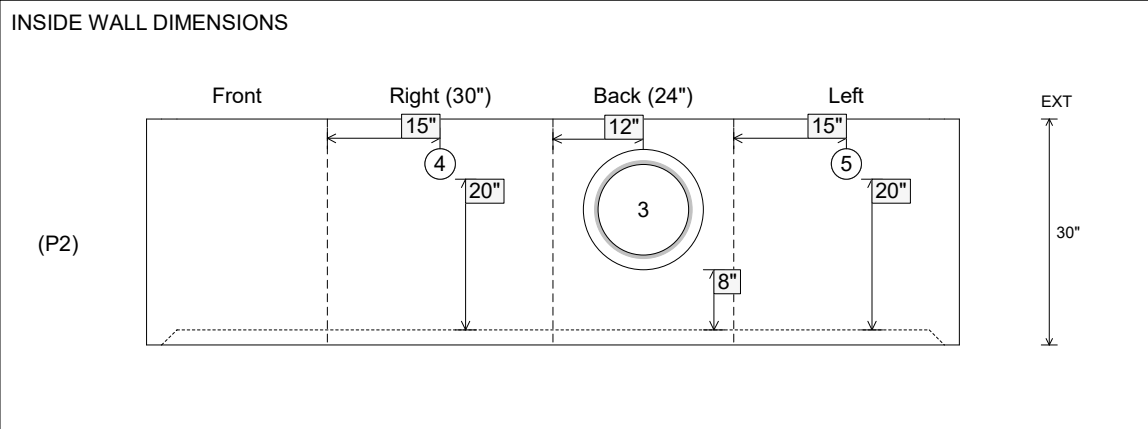

Coating (Int):

Coating (Ext):

Seam Up: Flat

Seam Dn: Groove

Wall Thickness: 8"

Floor Height: 0"

Height (Int): 30"

Height (Ext): 30"

Weight (Net): 2668 lb

Volume (Net): 0.68cu.yd
