

Job Name: 25-2977 KYTC Hopkins CO Call 105 (255382)
 Job Location:
 Contractor: Scotty's Contracting & Stone, LLC

Plant: Beaver Dam

1/12/2026 1:59:13 PM

Tech: J. Coppage

PC: Celina Goff



Structure ID: 1978R

P1 BX3636-08BAVF

BOX BASE 8inW, 8inF, Variable Ht

- P3) 36" x 36" - P.I.P. - BY OTHERS - 8"
- P2) 36" x 36" - BOX RISER 8inW - 42"
- P1) 36" x 36" - BOX BASE 8inW, 8inF, Variable Ht - 59"
- 2) 36" x 36" - Conseal CS-102 1.00"
- 1) Hole - 26

- Structure Notes:**
 KYTC STATE PROJECT
 1. JR HOE KY-316 PROVIDED BY ICAST.
 2. KYTC DBI TYPE 1 / ASTM C913 SPECIFICATIONS.
 3. CONCRETE = 4,000 PSI AT 28 DAYS.
 4. NO STEPS.
 5. REINFORCING PER ASTM A615 (GRADE 60).
 - WALLS (As .31) #5 BARS AT 12" C.C.E.W.
 - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.




Structure Total: 13392 lb

Rim: 381.91' Rim to Invert: 9.1' Slack: 0.2" Sump: 0" Step Position:


Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	372.81'	0°	26"	18" RCP B WALL	23"	Hole 26	26"	26"	-4"	0"
Invert 2										
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)

UPSIDE-DOWN VIEW (int. dimensions)

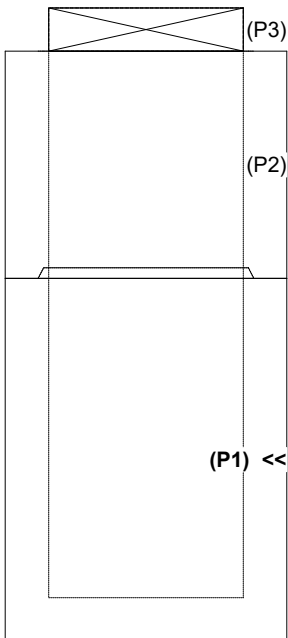

INSIDE WALL DIMENSIONS

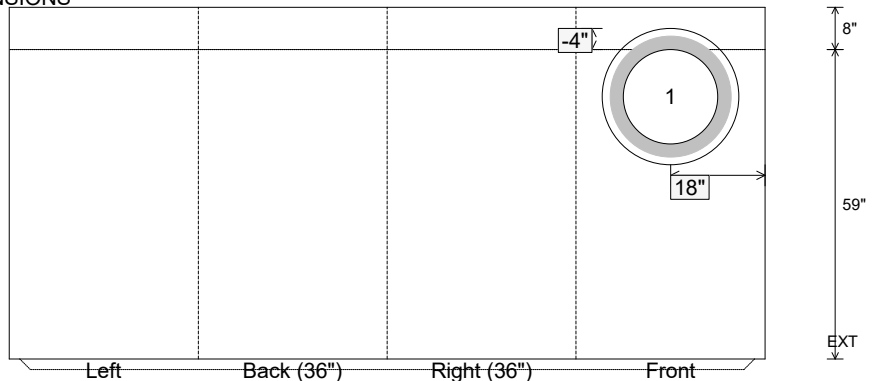

Coating (Int):
 Coating (Ext):

Seam Up: Tongue
 Seam Dn: n/a

Wall Thickness: 8"
 Floor Height: 8"

Height (Int): 59"
 Height (Ext): 67"

Weight (Net): 8430 lb
 Volume (Net): 2.15cu.yd
