



Job Name: 25-3040B - Stonedale Farms Job Location: Nicholasville, KY Contractor: Weddle Enterprises, Inc					Plant: 100 8/27/2026 1:50:17 PM		Tech: Jared - F PC: T. Ryan					
Structure ID: DMH3												
P2		MH048RS60SCDARED										
MH RISER w/DROP/ConBlock-CDA Red T/G												
P4) 24" - CASTING HEIGHT - 7" P3) 48" - ECC CONE w/ 24" HOLE, w/ConBlock-CDA Red F/G - 24" P2) 48" - MH RISER w/DROP/ConBlock-CDA Red T/G - 60" P1) 48" - MH BASE w/DROP/ConBlock-CDA Red T/n - 30" 2) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 2) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) ADMIXTURE CONBLOCK CDA RED 1) 48" - MH INVERT CHANNEL w/ConBlock-CDA Red - FULL HEIGHT 2) 48" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 1) PSX - 16M NYLO 1) Drop Tee - 12" PVC 1) Drop Elbow - 12" PVC 9) MH Step ML-10-TDS-NCR - 10"					0 lb 1738 lb 4140 lb 3288 lb 0 lb 0 lb 0 lb 1440 lb 0 lb 0 lb 8 lb 0 lb 0 lb 0 lb		Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. ADMIXTURE = CONBLOCK CDA RED. 4. CASTING SUPPLIED BY OTHERS (HOE MC-350 F/C SANITARY). 5. EXTERIOR DROP ASSEMBLY @ 180 DEGREES. REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.					
Rim: 999'					Rim to Invert: 10'		Slack: 1"		Sump: 2"		Step Position: 0°	
Structure Total: 10614 lb												
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset		
Invert 1												
Invert 2	994.67'	180°	91.125"	12" PVC SDR35	12.5"	Drop Tee 12" PVC	12.5"	12.646"	35.5"	0"		
Invert 3												
Invert 4												
Invert 5												
Invert 6												
Invert 7												
Invert 8												

RIGHT-SIDE UP VIEW (int. dimensions)

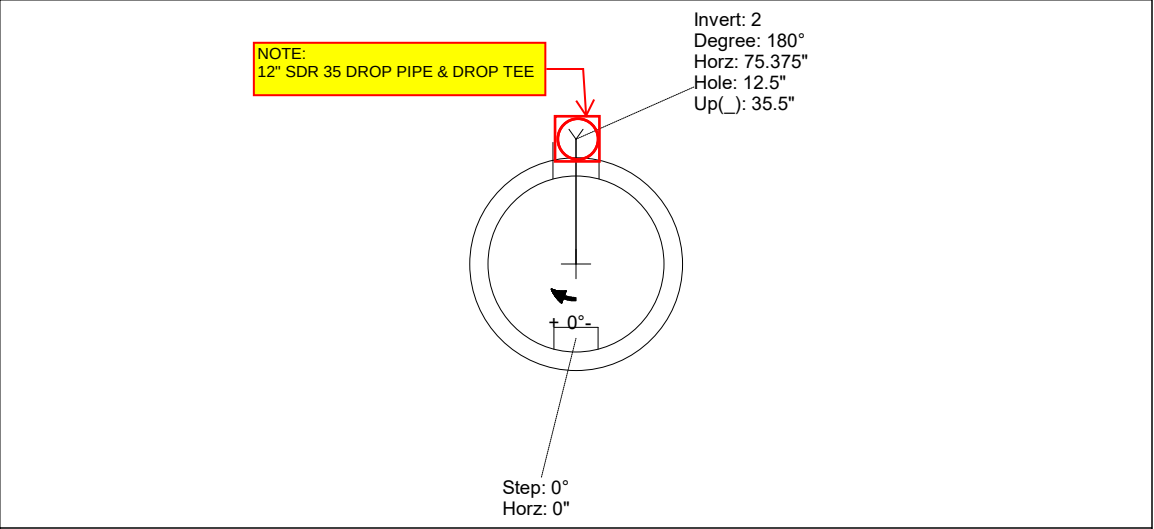

INSIDE WALL DIMENSIONS

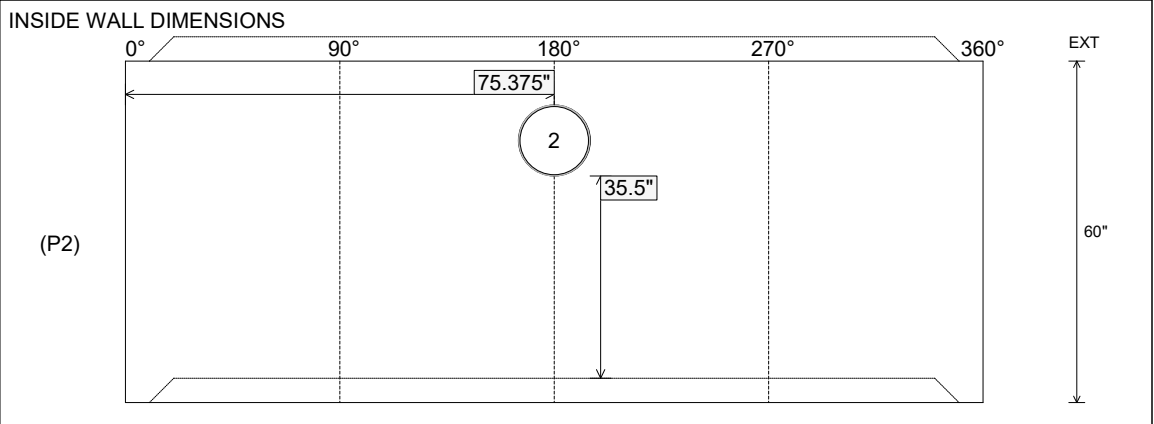

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: Groove	Wall Thickness: 5" Floor Height: 0"	Height (Int): 60" Height (Ext): 60"	Weight (Net): 4140 lb Volume (Net): 1.06cu.yd
----------------------------------	------------------------------------	--	--	--
