

Job Name: 25-3193 - KYTC Kenton Co Call 328 (251320)
Job Location: Independence, KY
Contractor: Eaton Asphalt

Plant: 100

Tech: Jared - A

7/1/2026 12:29:14 PM

PC: J. Jarvis



Structure ID: 477

P1 BX24300808VF

BOX BASE 8inW, 8inF, Variable Ht

P3) 15" x 27" - P.I.P. - BY OTHERS - 8"
P2) 24" x 30" - CB FLAT TOP 8"W w/15"x27" HOLE - 8"
P1) 24" x 30" - BOX BASE 8inW, 8inF, Variable Ht - 44"
1) CASTING - HOE KY-230-G F/G (GRADE)
1) 24" x 30" - Conseal CS-102 1.00"
1) 15" x 27" - Conseal CS-102 1.00"
1) Hole - 24
2) Hole - 4

0 lb
963 lb
5050 lb
237 lb
0 lb
0 lb
0 lb
0 lb

Structure Total: 6250 lb

Structure Notes:

****KYTC STATE PROJECT****

PLAN LABEL: 477

1. HOE KY-230-G F/G (GRADE) PROVIDED BY ICAST.
2. KYTC DBI TYPE 13G / ASTM C-913 SPEC'S.
3. CONCRETE = 4,000 PSI AT 28 DAYS.
4. REINFORCING PER ASTM A615 (GRADE 60).
 - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.
 - WALLS (As .31) #5 BARS AT 12" C.C.E.W..
 - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.
5. STUB #5 BARS 12" OUT OF THE TOP OF THE SLAB



(SPACED AT 12" CC) AROUND THE 15" X 27" HOLE

Rim: 890.77' Rim to Invert: 5' Slack: 0" Sump: 0" Step Position:


Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	885.77'	270°	23"	18" ADS N-12	22"	Hole 24	24"	24"	-3"	0"
Invert 2	888.57'	90°	23"	4" WEEP HOLE	4"	Hole 4	4"	4"	33.6"	0"
Invert 3	888.57'	270°	23"	4" WEEP HOLE	4"	Hole 4	4"	4"	33.6"	0"
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)

UPSIDE-DOWN VIEW (int. dimensions)

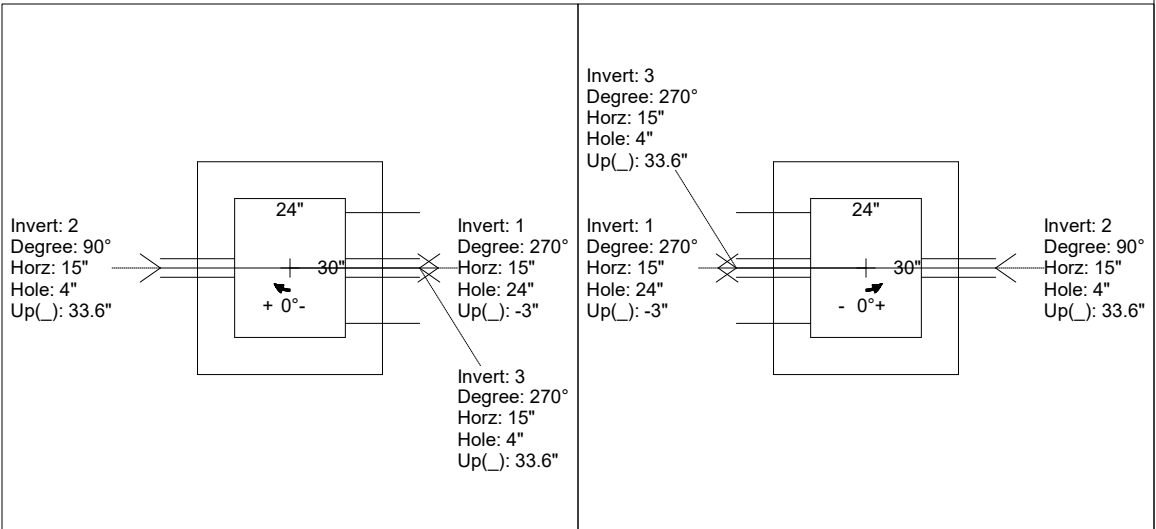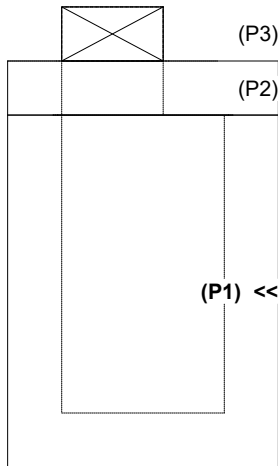

INSIDE WALL DIMENSIONS

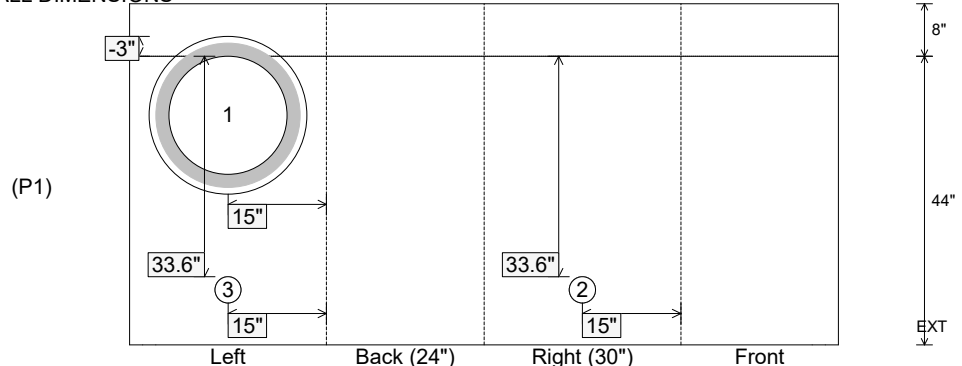

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: n/a

Wall Thickness: 8"
Floor Height: 8"

Height (Int): 44"
Height (Ext): 52"

Weight (Net): 5050 lb
Volume (Net): 1.29cu.yd
