

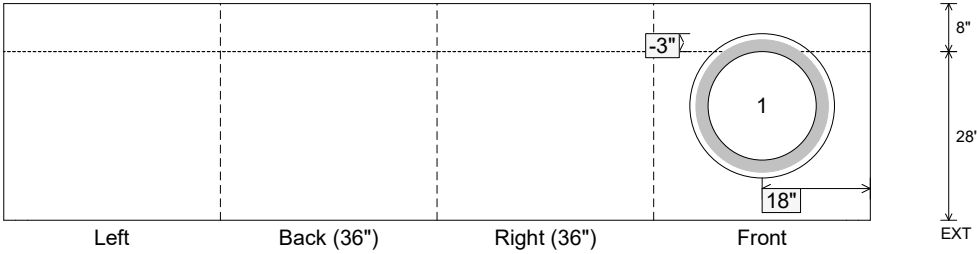


Job Name: 25-3193 - KYTC Kenton Co Call 328 (251320) Job Location: Independence, KY Contractor: Eaton Asphalt				Plant: 100 6/5/2026 9:50:10 AM		Tech: Jared - A PC: J. Jarvis					
Structure ID: 500											
P1 BX3636-08BAVF				BOX BASE 8inW, 8inF, Variable Ht F/n							
P2) 36" x 36" - P.I.P. - BY OTHERS - 8" P1) 36" x 36" - BOX BASE 8inW, 8inF, Variable Ht F/n - 28" 1) CASTING - HOE KY-316 SET (DBI 1) 1) 36" x 36" - Conseal CS-102 1.00" 1) Hole - 24				0 lb 4820 lb 317 lb 0 lb 0 lb Structure Total: 5137 lb		Structure Notes: ** KYTC STATE PROJECT ** 1. PER KYTC DBI TY 1 / ASTM C-913 SPECS 2. CONCRETE: 4,000 PSI AT 28 DAYS 3. REINFORCEMENT: #5 BAR @ 12" C.C. E.W. (GRADE 60) - 2" MIN. REBAR CLEARANCE (TYP) 4. NO STORM INVERT 5. NO STEPS 6. KY-316 FRAME & GRATES SUPPLIED BY ICAST - FRAME TO BE POURED IN PLACE BY OTHERS 7. STUB #5 BAR @ 12" C.C. (GRADE 60) 20" OUT TOP OF WALLS FOR FIELD POUR TIE-IN - MIN. 4" PENETRATION INTO WALLS					
Rim: 892' Rim to Invert: 3' Slack: 0" Sump: 0" Step Position:											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	889'	0°	26"	18" ADS N-12	22"	Hole 24	24"	24"	-3"	0"	
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											
RIGHT-SIDE UP VIEW (int. dimensions)  UPSIDE-DOWN VIEW (int. dimensions)  INSIDE WALL DIMENSIONS 											
Coating (Int): Coating (Ext):				Seam Up: Flat Seam Dn: n/a		Wall Thickness: 8" Floor Height: 8"		Height (Int): 28" Height (Ext): 36"		Weight (Net): 4820 lb Volume (Net): 1.23cu.yd	
