

Job Name: 25-4288 - Project Wave

Job Location: Franklin, KY 42134

Contractor: Cumberland Pipeline LLC

Plant: 100

7/10/2026 8:14:29 AM

Tech: Jared - A

PC: Erica Bradley




Structure ID: A13

P3 MH048RS48X

MH RISER w/XYPEX

P6) 24" - CASTING HEIGHT - 7"	0 lb	Structure Notes: 1. PER ASTM C-478 SPECIFICATIONS 2. CONCRETE: 4,000 PSI AT 28 DAYS 3. REINFORCEMENT: PER ASTM A615 4. INVERT CHANNEL REQUIRED 5. STEPS AT 0 DEGREES 6. JBS 1150 FRAME & COVER "SANITARY" SUPPLIED BY ICAST
P5) 24" - XYPEX GRADE RING - 4"	270 lb	
P4) 48" - ECC XYPEX CONE w/ 24" HOLE - 36"	2251 lb	
P3) 48" - MH RISER w/XYPEX - 48"	3353 lb	
P2) 48" - MH RISER w/XYPEX - 48"	3353 lb	
P1) 48" - MH BASE w/XYPEX - 24"	2863 lb	
1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212	0 lb	
1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.)	0 lb	
1) 48" - MH INVERT CHANNEL w/XYPEX - FULL HEIGHT	1440 lb	
1) CASTING - JBS 1150 F/C SANITARY	250 lb	
3) 48" - Conseal CS-102 1.00" (Double)	0 lb	
2) 24" - Conseal CS-102 1.00" (Double)	0 lb	
3) PSX - 12-08 NYLO	24 lb	
13) MH Step ML-10-TDS-NCR - 10"	0 lb	
Structure Total:		13805 lb
Rim: 728.52' Rim to Invert: 13.78' Slack: 0.36" Sump: 2" Step Position: 0°		

Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset
Invert 1										
Invert 2										
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

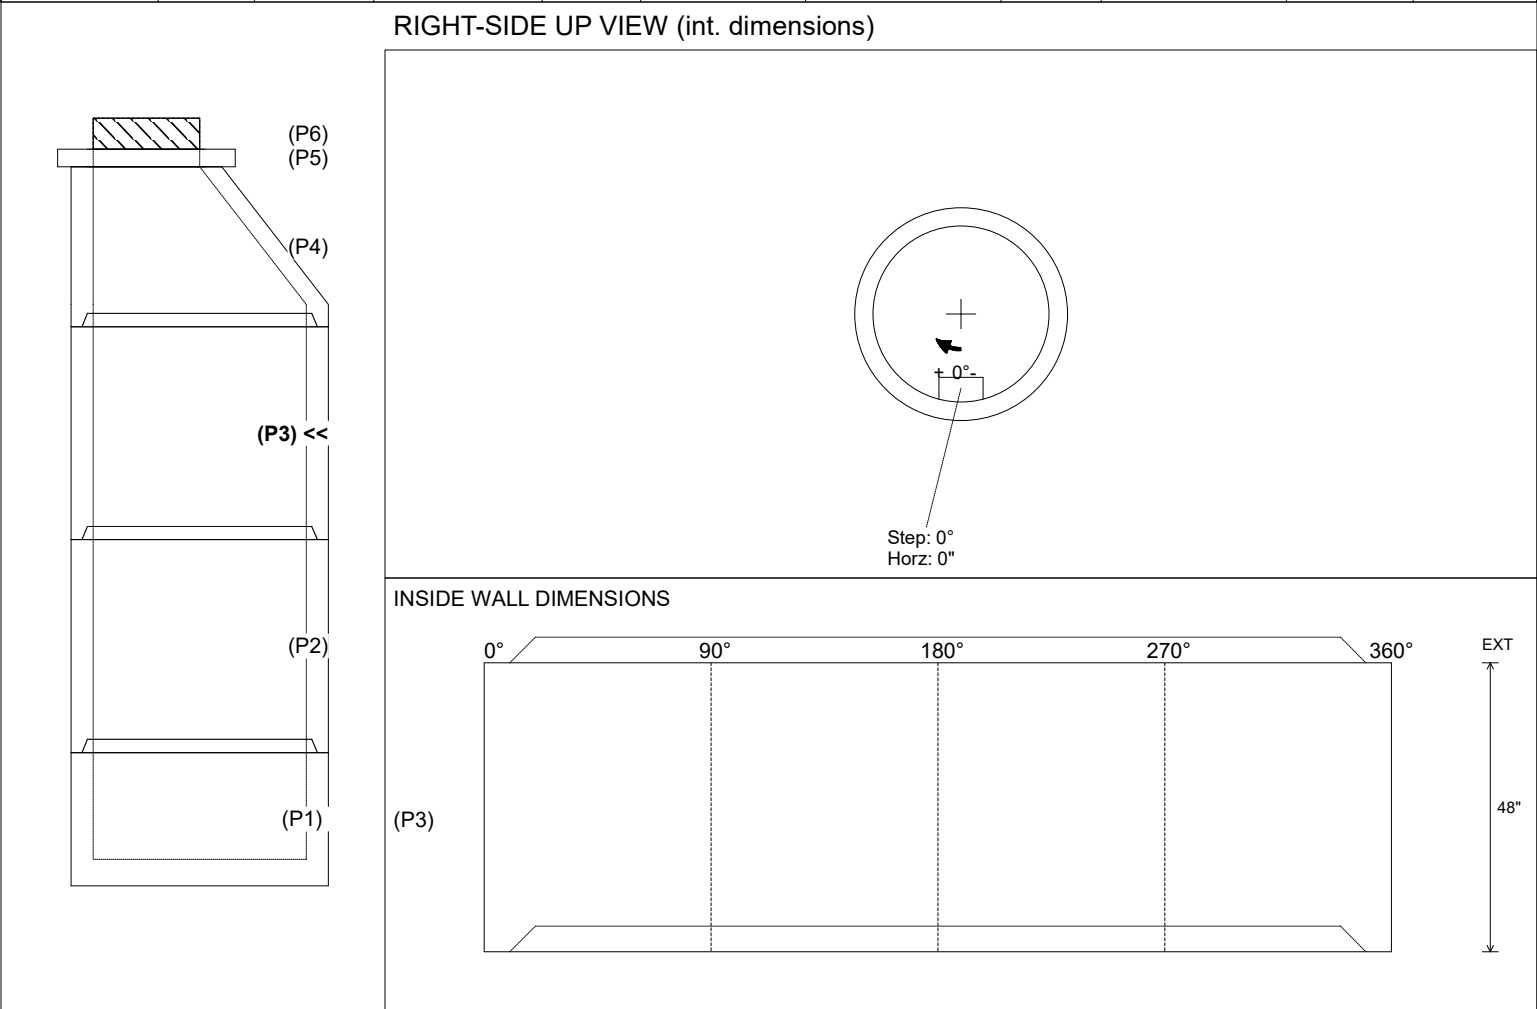

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: Groove	Wall Thickness: 5" Floor Height: 0"	Height (Int): 48" Height (Ext): 48"	Weight (Net): 3353 lb Volume (Net): 0.86cu.yd
----------------------------------	------------------------------------	--	--	--
