

Job Name: 25-4430 KYTC Daviess Co Call 104 (2511035)  
 Job Location: Owensboro, KY  
 Contractor: Ragle, Inc.

Plant: 100

3/11/2026 2:15:03 PM

Tech: Jared - A

PC: Andy Chambers



**Structure ID: 4940 (20)**

**P2 BX3636-08R24**

**BOX RISER 8inW**

- P4) 15" x 27" - P.I.P. - BY OTHERS - 8"
- P3) 36" x 36" - CB FLAT TOP 8"W w/15"x27" HOLE - 8"
- P2) 36" x 36" - BOX RISER 8inW - 24"
- P1) 36" x 36" - BOX BASE 8inW, 8inF, Variable Ht - 38"
- 1) CASTING - HOE KY-230-G F/G (GRADE)
- 2) 36" x 36" - Conseal CS-102 1.00"
- 1) 15" x 27" - Conseal CS-102 1.00"
- 1) Hole - 30
- 2) Hole - 24
- 2) Hole - 4



0 lb  
 1543 lb  
 2819 lb  
 5107 lb  
 237 lb  
 0 lb  
 0 lb  
 0 lb  
 0 lb  
 0 lb  
 0 lb  
 Structure Total: 9706 lb

**Structure Notes:**  
 (1) JBS 3413 F&G's (BY CONTR)  
 \*\*KYTC STATE PROJECT\*\*  
 1. HOE KY-230-G F/G (GRADE) PROVIDED BY ICAST.  
 2. KYTC DBI TYPE 13G / ASTM C-913 SPEC'S.  
 3. CONCRETE = 4,000 PSI AT 28 DAYS.  
 4. REINFORCING PER ASTM A615 (GRADE 60).  
 - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.  
 - RISER/WALLS (As .31) #5 BARS AT 12" C.C.E.W..  
 - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.  
 5. STUB #5 BARS 12" OUT OF THE TOP OF THE SLAB (SPACED AT 12" C.C.).


Rim: 450.54' Rim to Invert: 6.67' Slack: 2.04" Sump: 0" Step Position:

Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ( )	Offset
Invert 1										
Invert 2										
Invert 3										
Invert 4	448.37'	90°	26"	4" WEEP HOLE	4"	Hole 4	4"	4"	14"	0"
Invert 5	448.37'	270°	26"	4" WEEP HOLE	4"	Hole 4	4"	4"	14"	0"
Invert 6										
Invert 7										
Invert 8										

**RIGHT-SIDE UP VIEW (int. dimensions)**

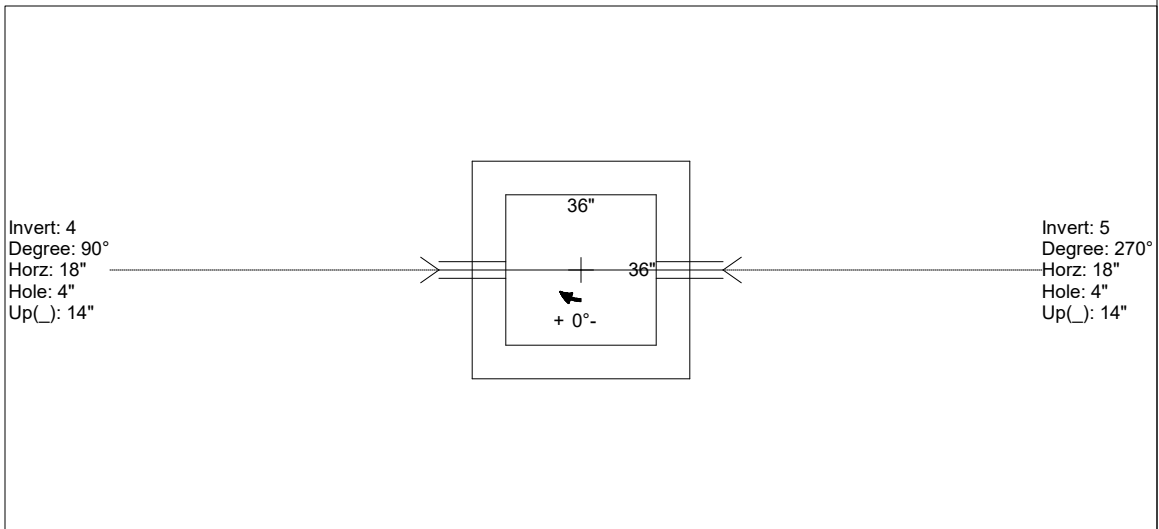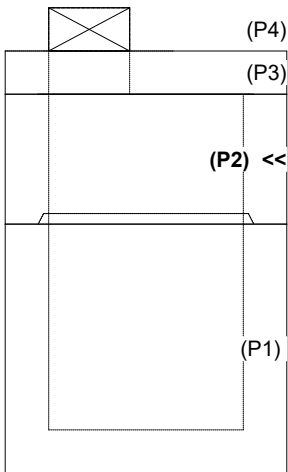

**INSIDE WALL DIMENSIONS**

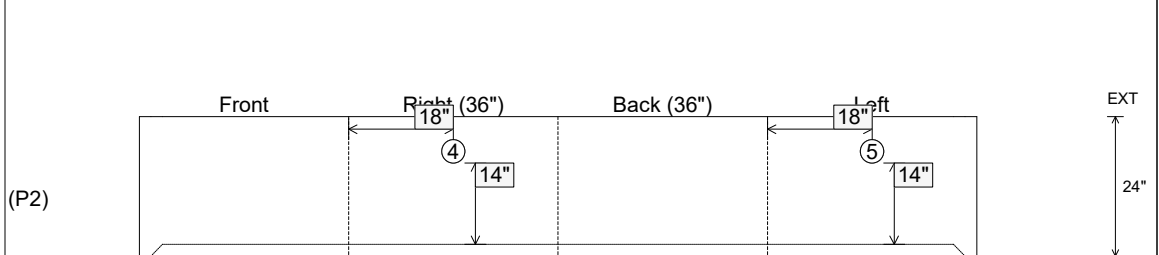

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: Groove	Wall Thickness: 8" Floor Height: 0"	Height (Int): 24" Height (Ext): 24"	Weight (Net): 2819 lb Volume (Net): 0.72cu.yd
----------------------------------	----------------------------------	--	--	--
