



Job Name: 25-4547 - WWTP Improvements & Hydraulic Expansion Job Location: Shepherdsville, KY Contractor: Pace Contracting, LLC					Plant: 100 6/4/2026 5:54:35 PM		Tech: Jared - F PC: J Jarvis				
Structure ID: METER VAULT 1											
P2 MH060RS60			MH RISER T/G								
P4) 36" x 36" - CASTING HEIGHT - 0" P3) 60" - MH FLAT TOP w/36"x36" Hatch F/G - 13" P2) 60" - MH RISER T/G - 60" P1) 60" - MH BASE Custom Ht T/n - 47" 1) HATCH (Alum.) - HALLIDAY W1S 36"x36" 2) 60" - Conseal CS-102 1.00" (Double) 1) 36" x 36" - Conseal CS-102 1.00" (Double) 2) PSX - 8QRS DD					0 lb 2132 lb 6213 lb 7640 lb 78 lb 0 lb 0 lb 13 lb ----- 16075 lb		Structure Notes: . 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. HATCH SUPPLIED BY I-CAST (HALLIDAY W1S 36"X36") . REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W. - RISER/WALLS (As .18) - FLOOR (As .47) #5 BARS AT 12" C.C.E.W.				
Rim: 454' Rim to Invert: 5.06' Slack: -0.002" Sump: 59.28" Step Position:											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	448.94'	0°	0"	4" DI	4.75"	PSX 8QRS DD	8"	8.024"	5.5"	0"	
Invert 2	448.94'	180°	113.125"	4" DI	4.75"	PSX 8QRS DD	8"	8.024"	5.5"	0"	
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											

RIGHT-SIDE UP VIEW (int. dimensions)

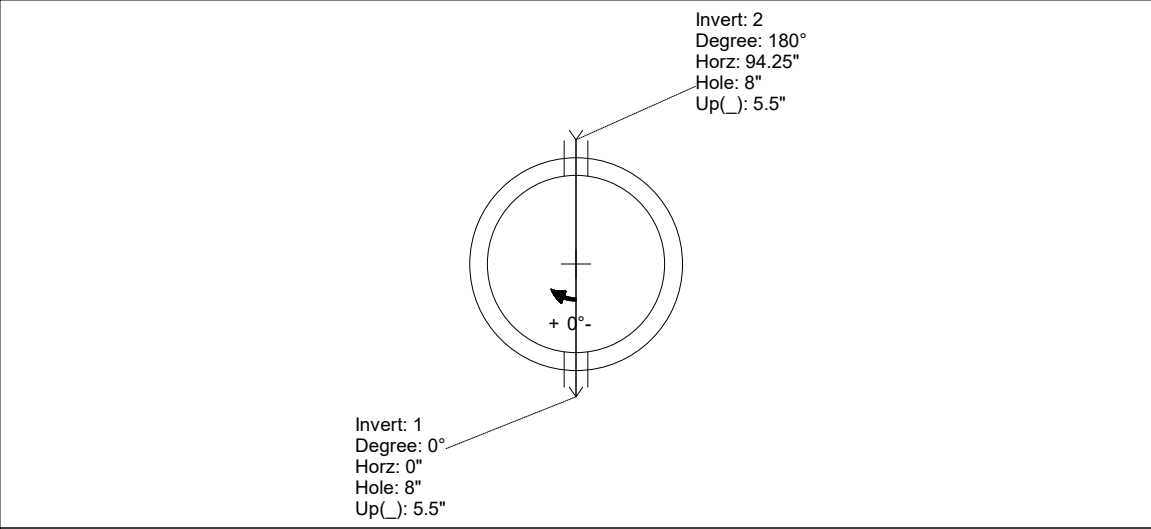

INSIDE WALL DIMENSIONS

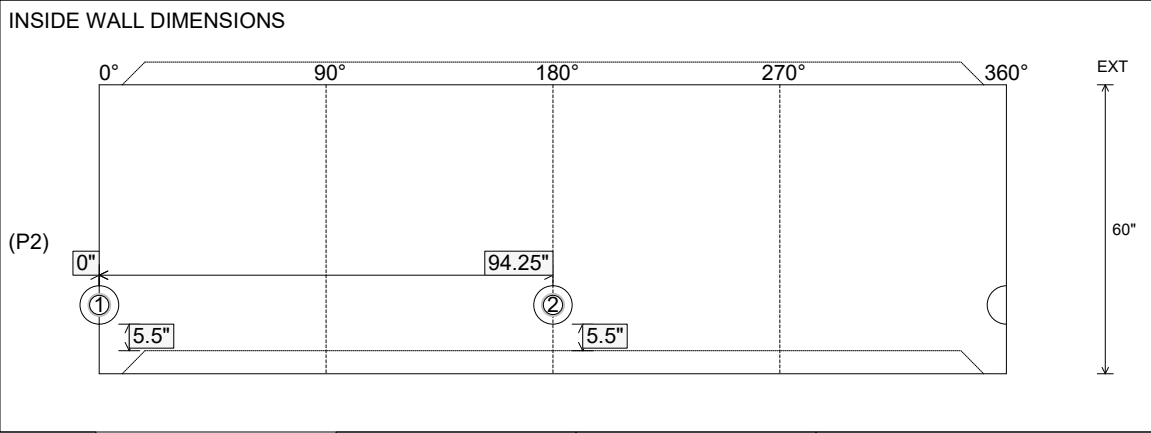

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: Groove	Wall Thickness: 6" Floor Height: 0"	Height (Int): 60" Height (Ext): 60"	Weight (Net): 6213 lb Volume (Net): 1.59cu.yd
----------------------------------	------------------------------------	--	--	--
