

Contractor: Pace Contracting, LLC

TECH: Jared - F

Plant: 100



Size: 60"

Rim to Invert: 11.45'

Floor Height: 8"



Slack: 0.4"

- FLOOR (As .37) #5 BARS AT 10" C.C.E.W.

11) MH Step ML-10-TDS-NCR - 10"


0 lb

Structure Total: 18788 lb

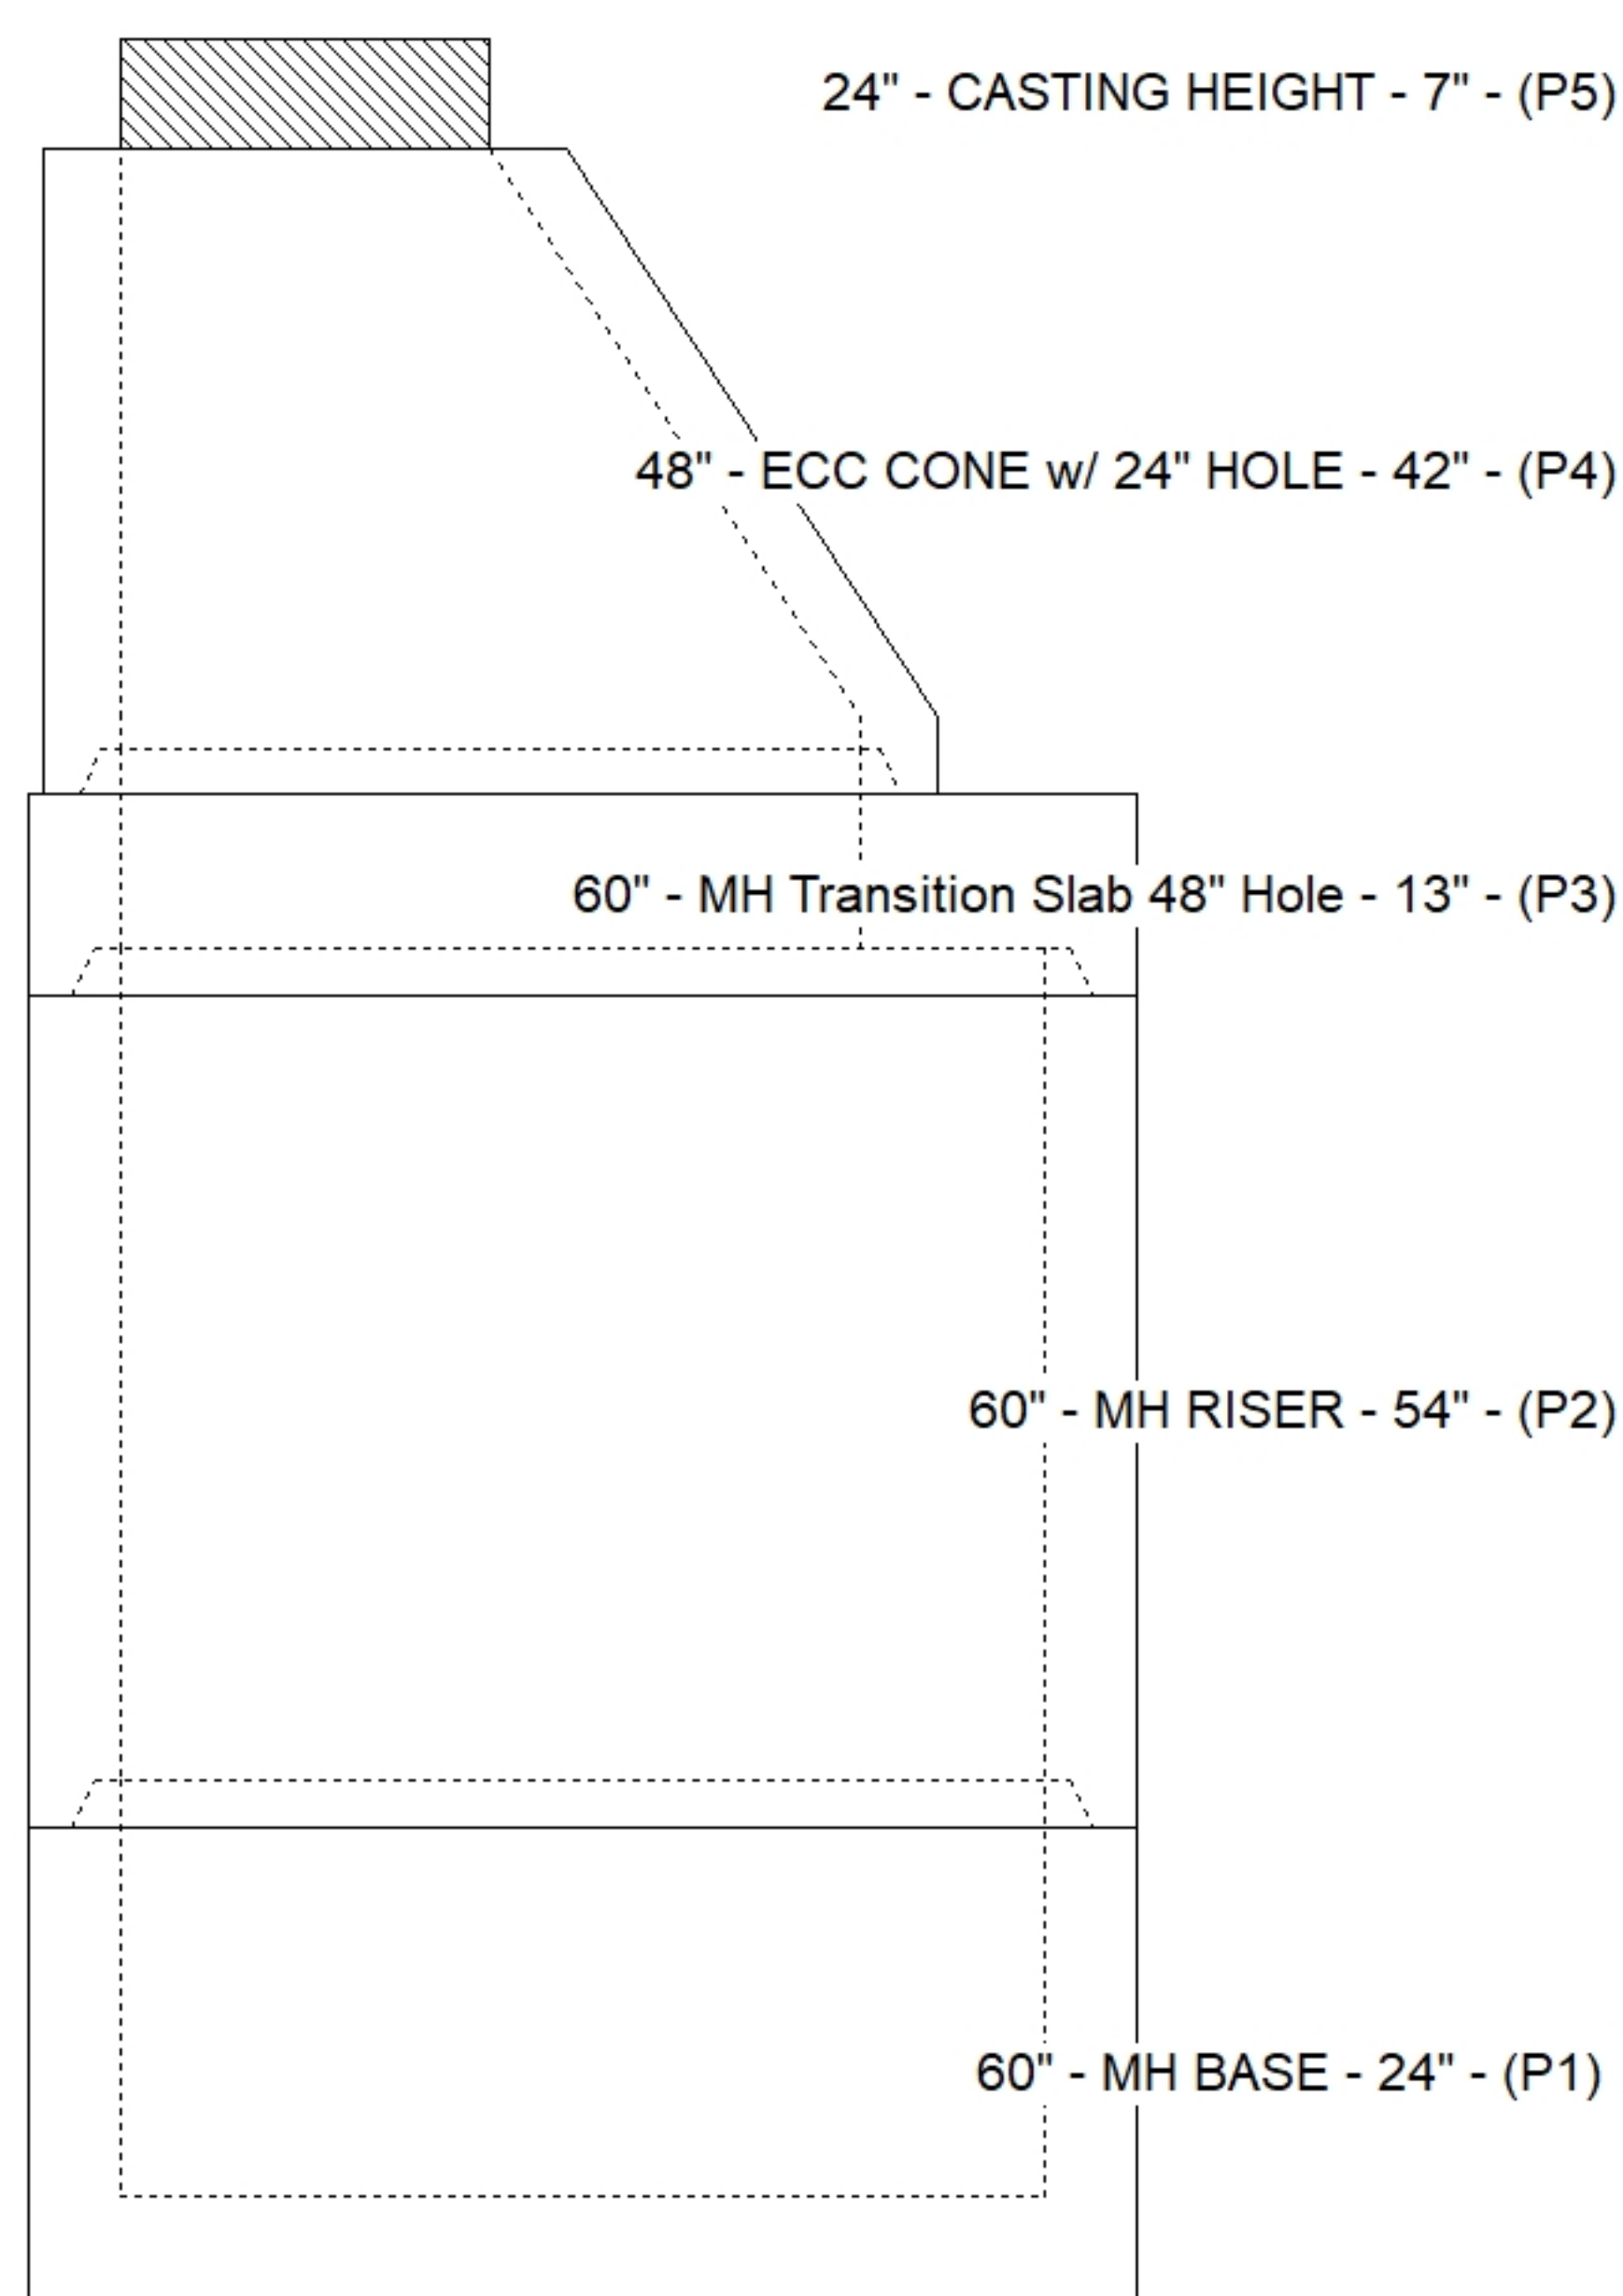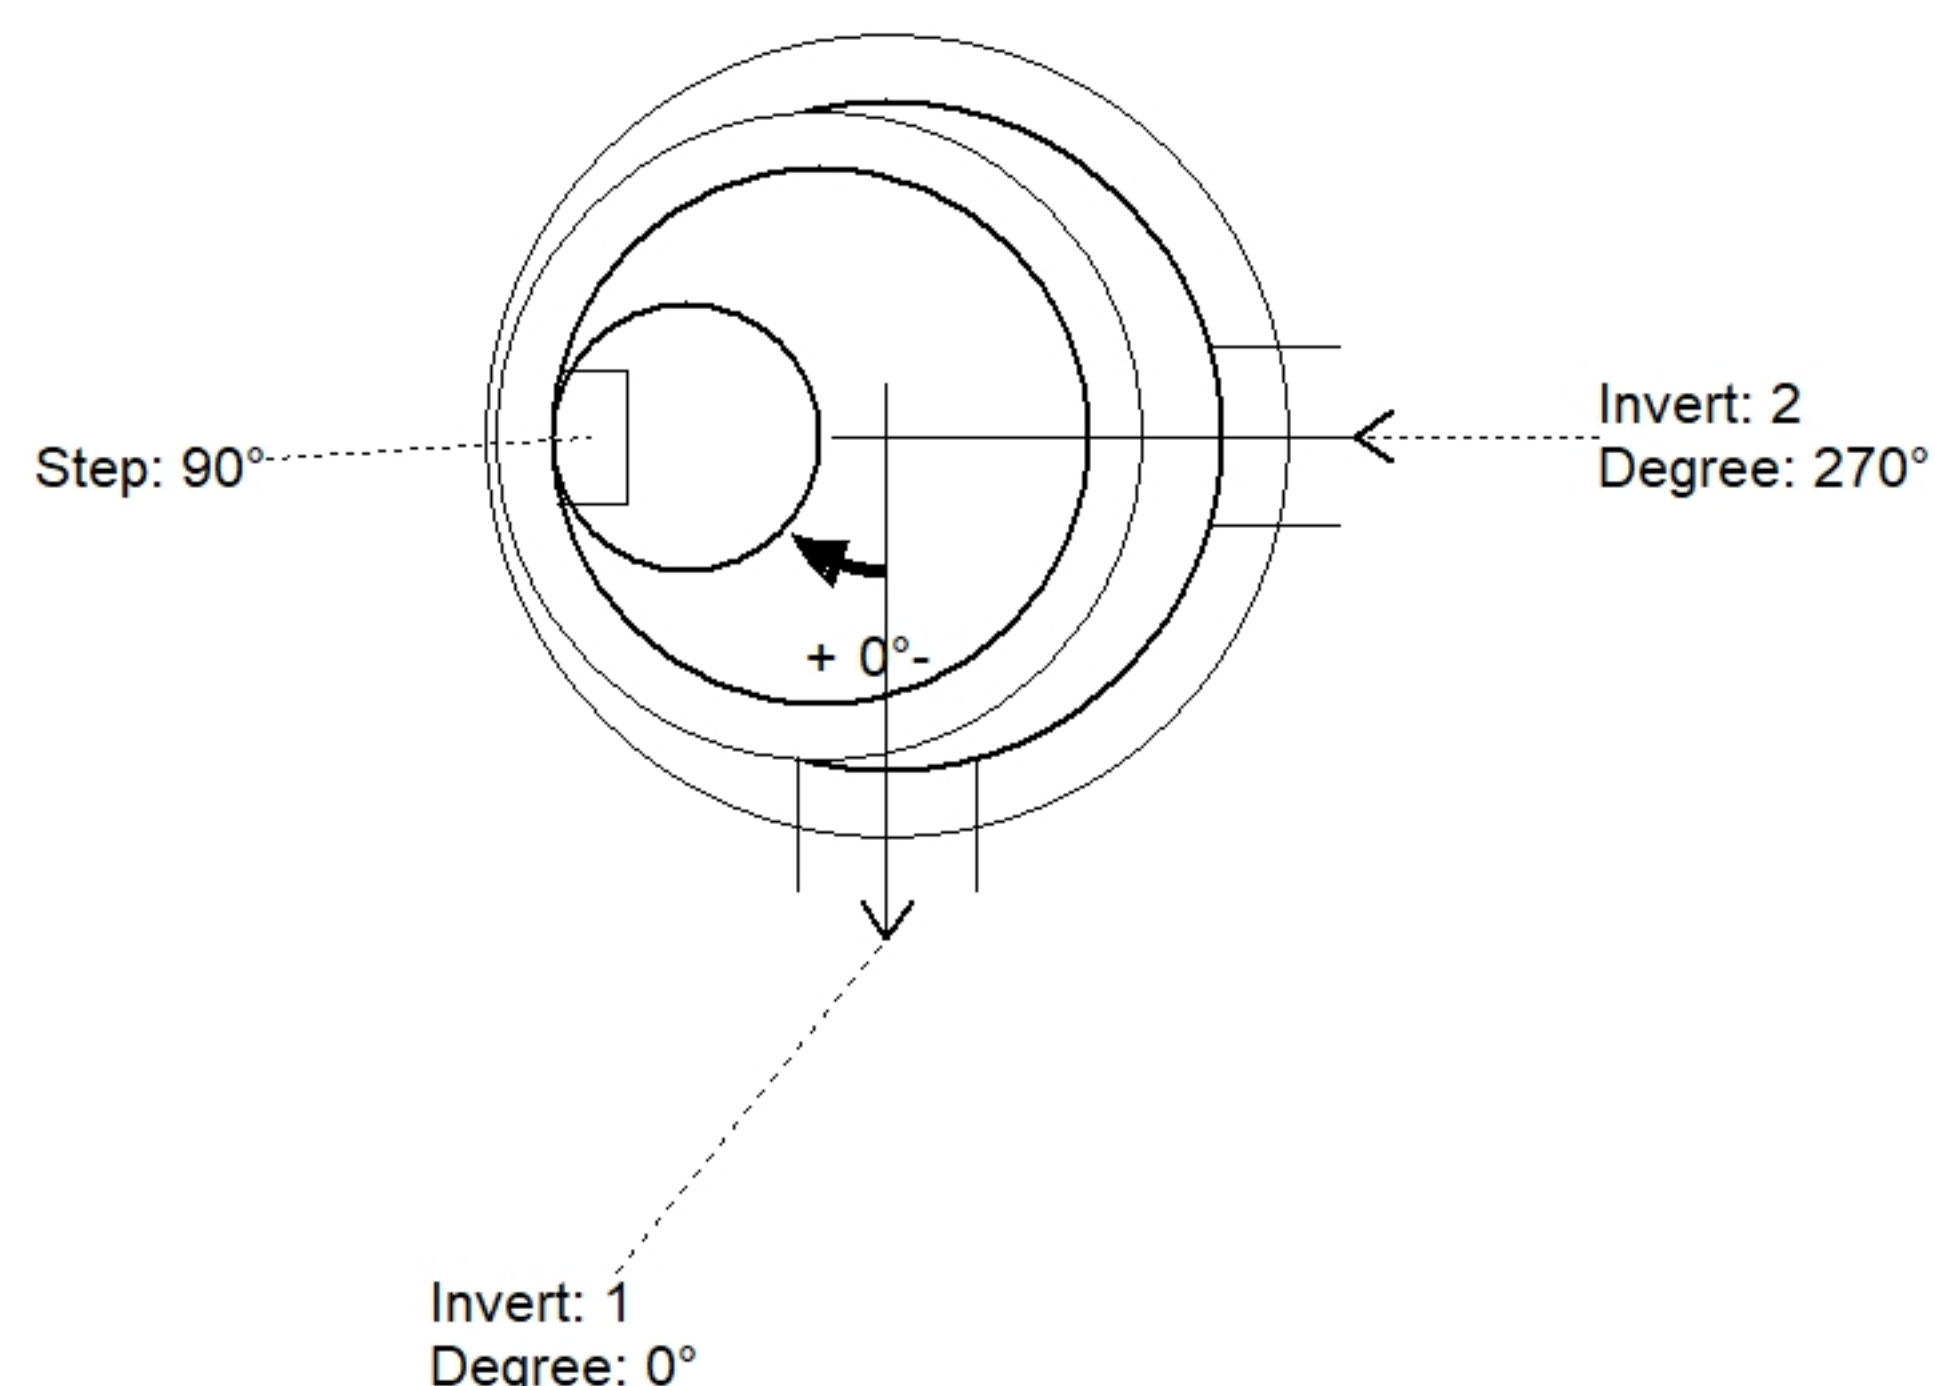

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up ()	Ref
Rim	449'							
Reducer	443.8'							
Invert 1	437.55'	0°	10" DI	11.1"	16"	PSX 16Y NYLO	0"	P1
Invert 2	437.65'	270°	10" DI	11.1"	16"	PSX 16Y NYLO	1.2"	P1
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

Default - Interior Dimensions

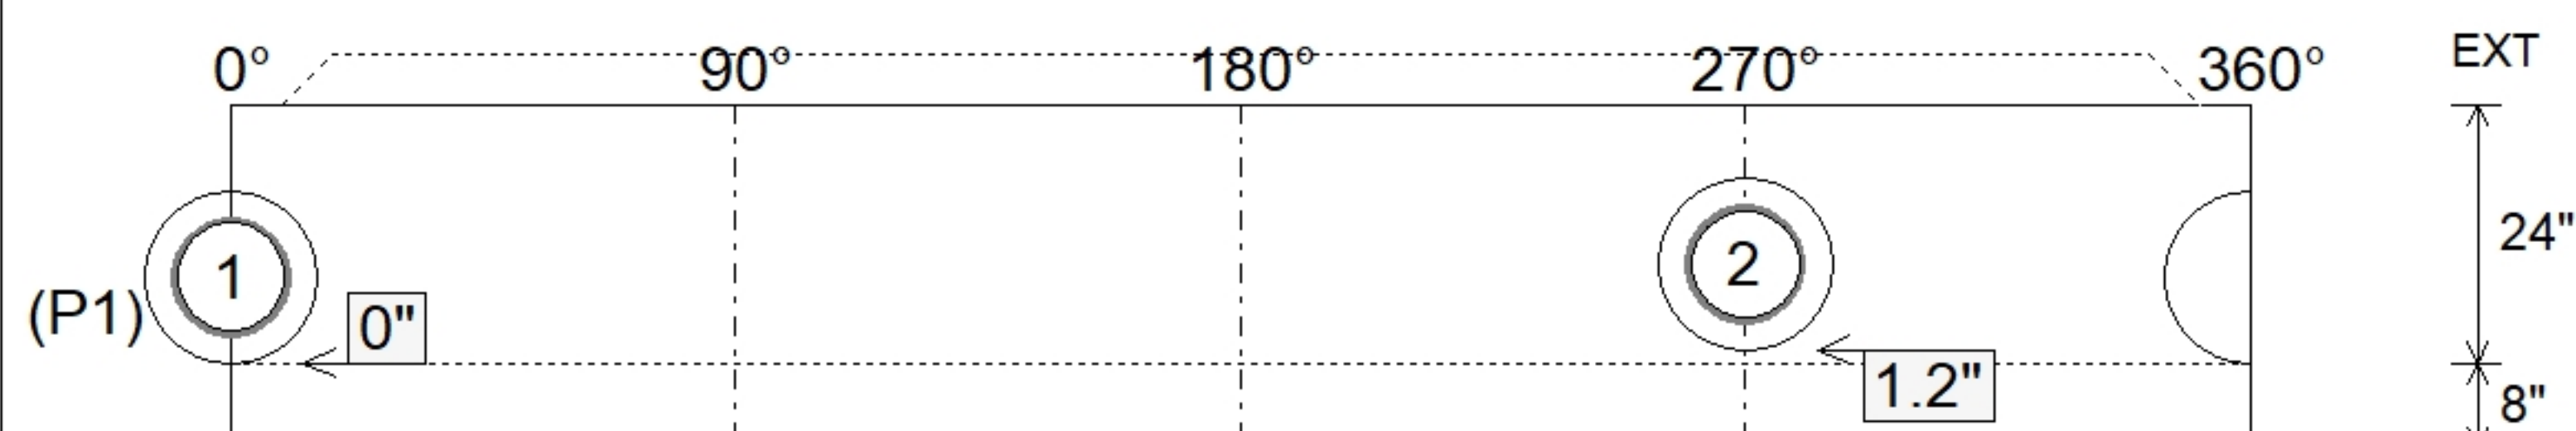

Submittal Drawing
6/8/2026 10:33:40 AM

SUBMITTAL
APPROVED BY:
