

Job Name: 26-1545 - KYTC Boone Co. Camp Ernst Roundabout (ID 3002312)
Job Location: Burlington, KY
Contractor: Lawrence Construction & Leasing, Inc.

Plant: 100

5/13/2026 2:22:11 PM

Tech: J.Horsley

PC: J. Jarvis



Structure ID: D3-7 DBI14

P2 BX024024-08LD08-14


CB FLAT TOP 8"W (HOE KY-210) F/F

P2) 24" x 24" - CB FLAT TOP 8"W (HOE KY-210) F/F - 8"
P1) 24" x 24" - BOX BASE 8inW, 8inF, Variable Ht F/n - 40"
1) CASTING - HOE KY-210 F/G (DBI 14)
1) 24" x 24" - Conseal CS-102 1.00"
1) Hole - 20

770 lb
4300 lb
178 lb
0 lb
0 lb
Structure Total: 5249 lb

Structure Notes: ** KYTC STATE PROJECT**
1. KYTC DBI TYPE 14 / ASTM C913 SPECIFICATIONS
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. NO INVERT CHANNEL.
4. DBI-14 F/G CAST INTO TOP SLAB (HOE KY-210 F/G).
REINFORCING PER ASTM A615 (GRADE 60).
- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.
- WALLS (As .31) #5 BARS AT 12" C.C.E.W.
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

KYTC STATE PROJECT

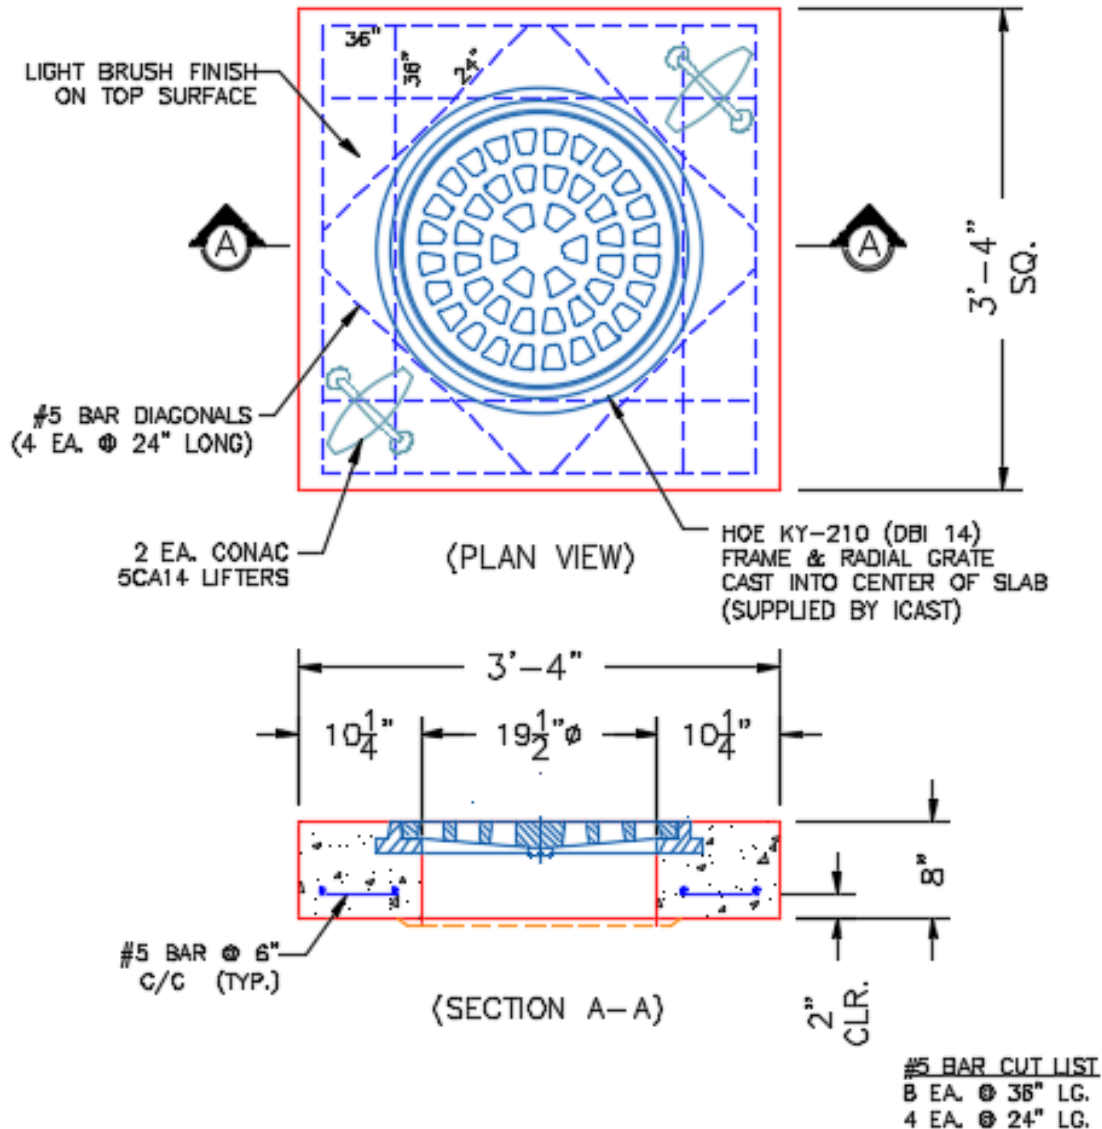

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Flat

Wall Thickness: 8"

Height (Ext): 8"

Weight (Net): 770 lb
Volume (Net): 0.2cu.yd
