

Job Name: 26-1635 - KYTC Oldham Co (261505)
Job Location: Pee wee Valley, KY
Contractor: Cleary Construction, Inc.

Plant: 100

7/22/2026 12:46:53 PM

Tech: Jared - F

PC: T. Ryan



Structure ID: 37887-142 SBIA

P2 BX048048-08LD12S

BX FLAT LID 8inW SOLID F/F

- P2) 48" x 48" - BX FLAT LID 8inW SOLID F/F - 12"
P1) 48" x 48" - BX BASE w/FLANGE 08W/12F/14EF F/n - 32"
1) 48" x 48" - Conseal CS-102 1.00"
1) Hole - 16
3) Hole - 8

4124 lb
13098 lb
0 lb
0 lb
0 lb

Structure Total: 17223 lb

Structure Notes:

****KYTC STATE PROJECT****

1. PER KYTC SPRING BOX INLET A / ASTM C478 SPEC'S.

2. CONCRETE = 4,000 PSI AT 28 DAYS.


3. SOLID TOP SLAB - NO CASTING.

REINFORCING PER ASTM A615 (GRADE 60.)


- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.

- WALLS (As .12) #5 BARS AT 12" C.C.E.W.

- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

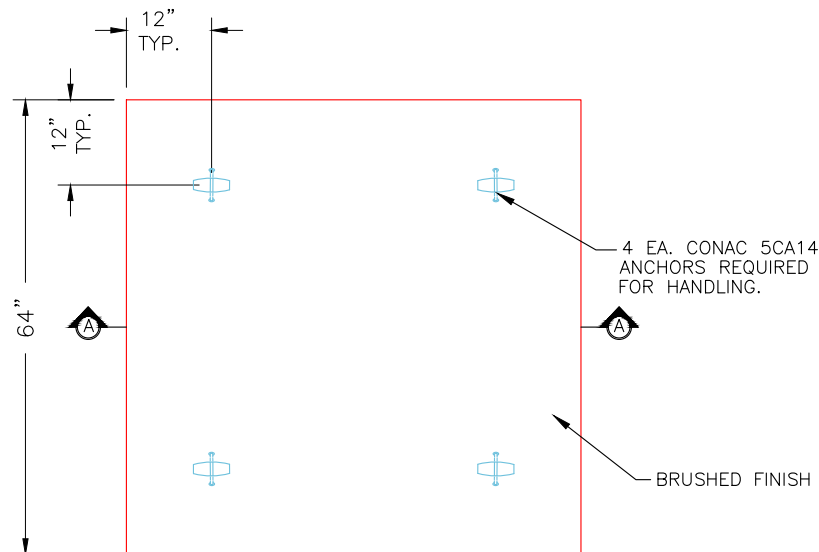

PLAN VIEW

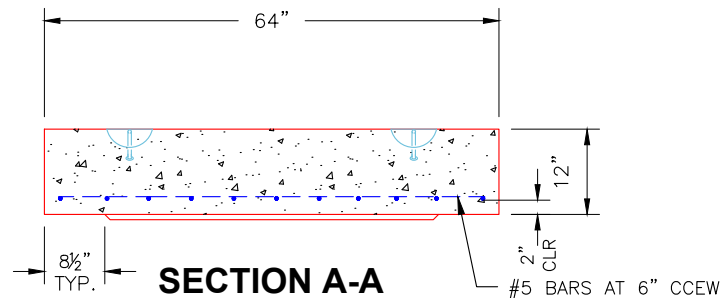

SECTION A-A

NOTES:

1. MANUFACTURED TO ASTM C-913 (LATEST REVISION).
2. CONCRETE: 4,000 PSI AT 28 DAYS.
3. REINFORCING: #5 BAR @ 6" O.C. E.W. (GRADE 60).

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Flat

Wall Thickness: 8"

Height (Ext): 12"

Weight (Net): 4124 lb
Volume (Net): 1.05cu.yd
