

**Contractor: Cleary Construction, Inc.**

TECH: Jared - F

Plant: 100




Slack: 3.2"

- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.


0 lb

Structure Total: 12856 lb

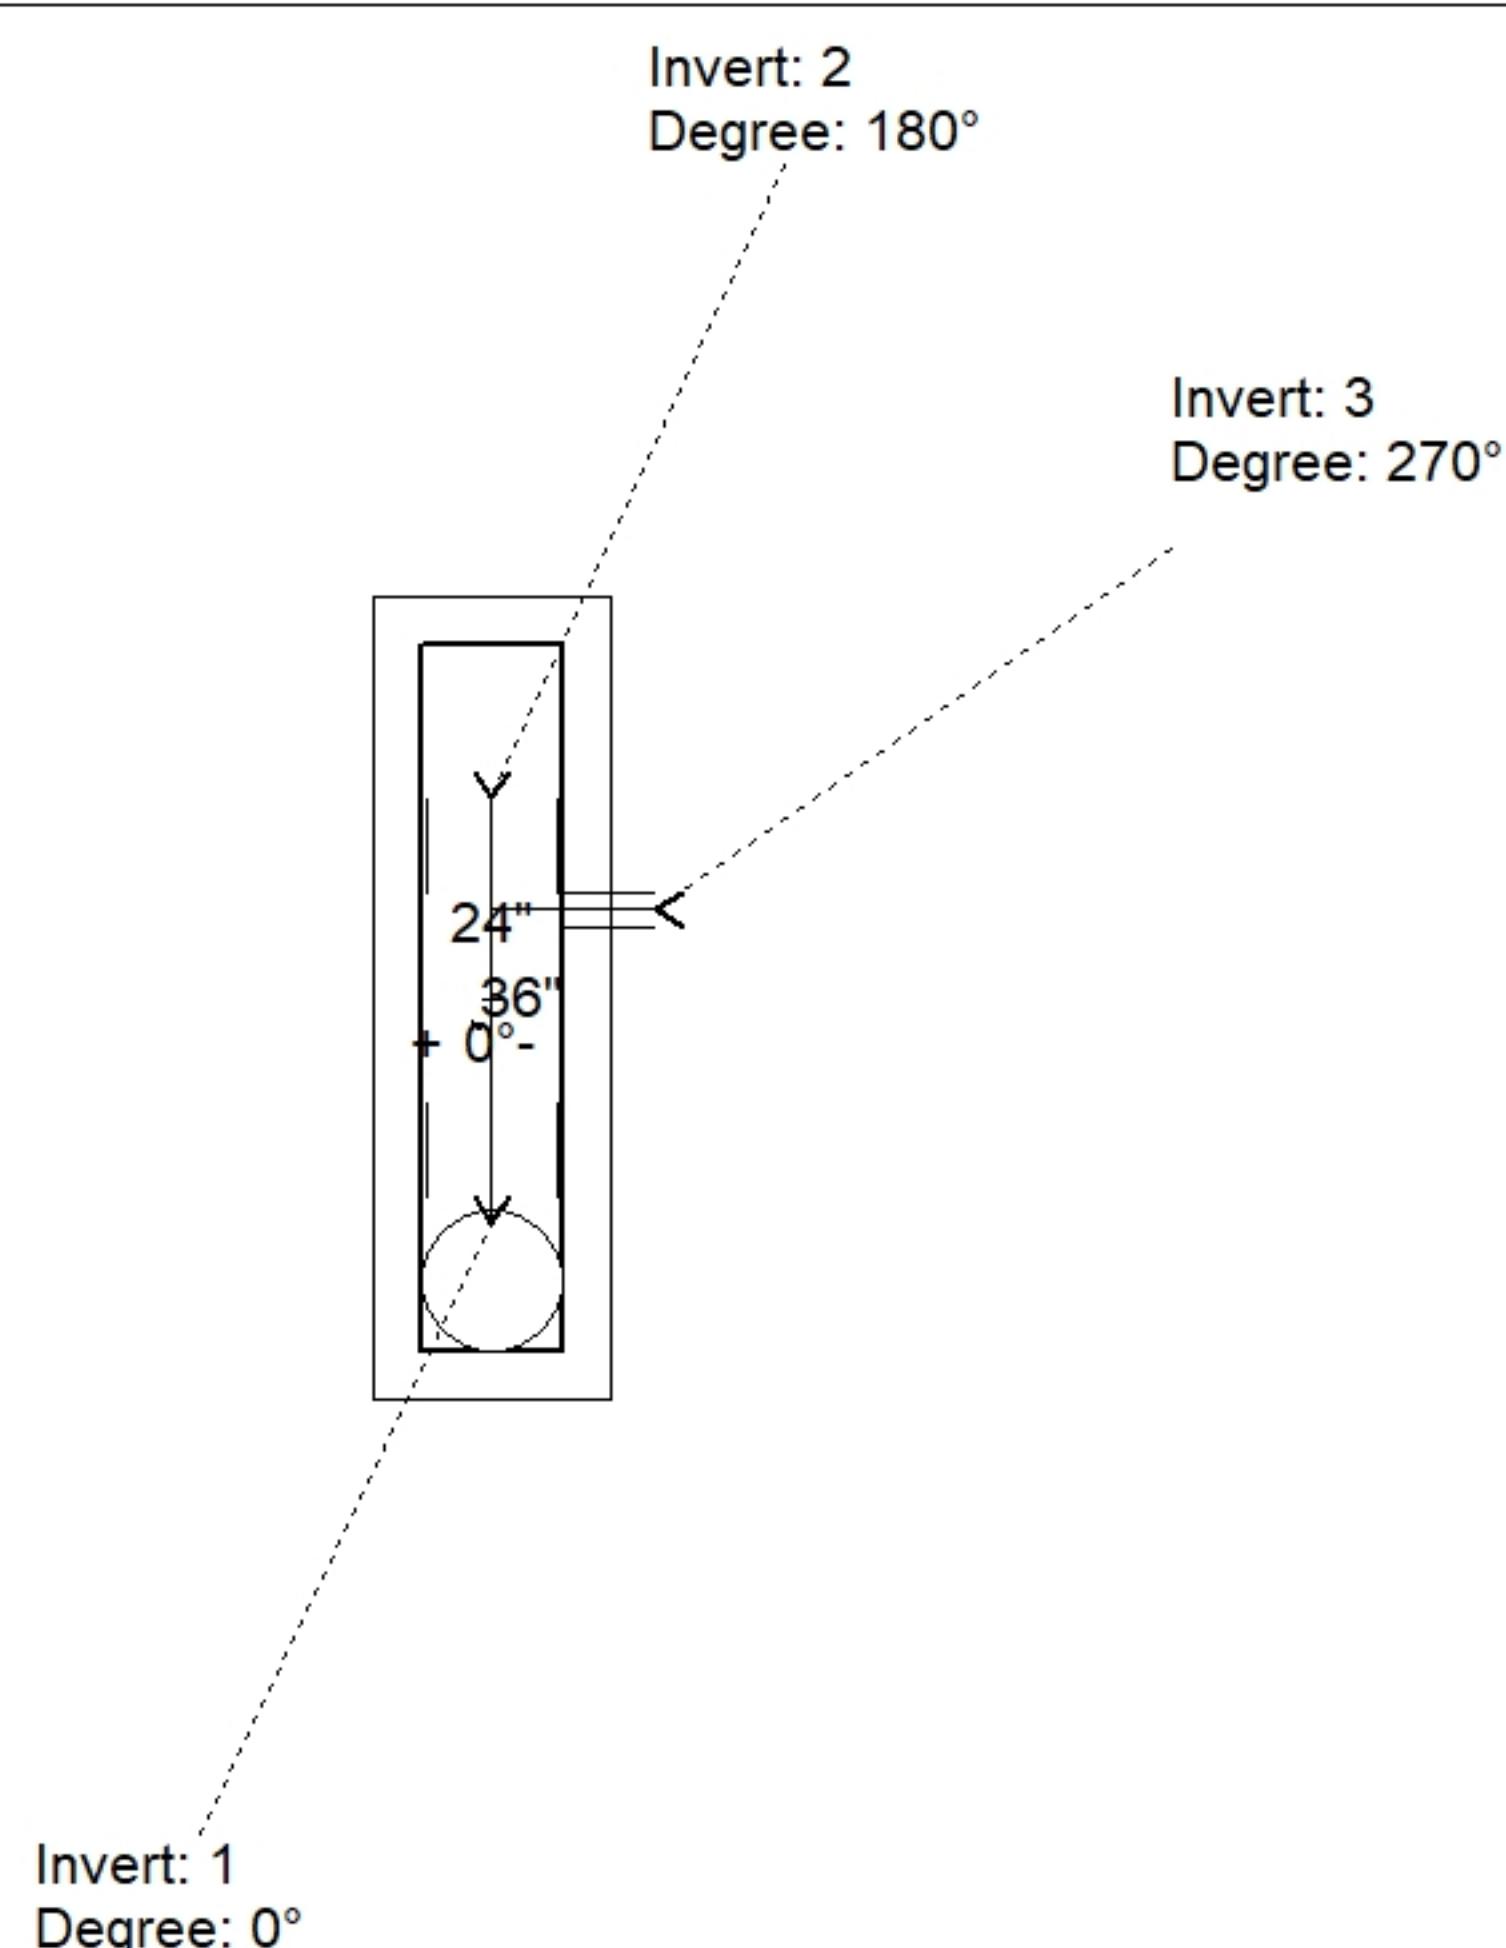

| Position | Elev    | Angle | Pipe                | Pipe OD | Hole | Connector | Up (↓) | Ref |
|----------|---------|-------|---------------------|---------|------|-----------|--------|-----|
| Rim      | 789.29' |       |                     |         |      |           |        |     |
| Reducer  |         |       |                     |         |      |           |        |     |
| Invert 1 | 784.19' | 0°    | 18" CMP             | 19"     | 22"  | Hole 22   | -2"    | P1  |
| Invert 2 | 784.27' | 180°  | 18" CMP             | 19"     | 22"  | Hole 22   | -1.04" | P1  |
| Invert 3 | 785.94' | 270°  | 4" HDPE (perf pipe) | 4.8"    | 6"   | Hole 6    | 20"    | P1  |
| Invert 4 |         |       |                     |         |      |           |        |     |
| Invert 5 |         |       |                     |         |      |           |        |     |
| Invert 6 |         |       |                     |         |      |           |        |     |
| Invert 7 |         |       |                     |         |      |           |        |     |
| Invert 8 |         |       |                     |         |      |           |        |     |

### Default - Interior Dimensions

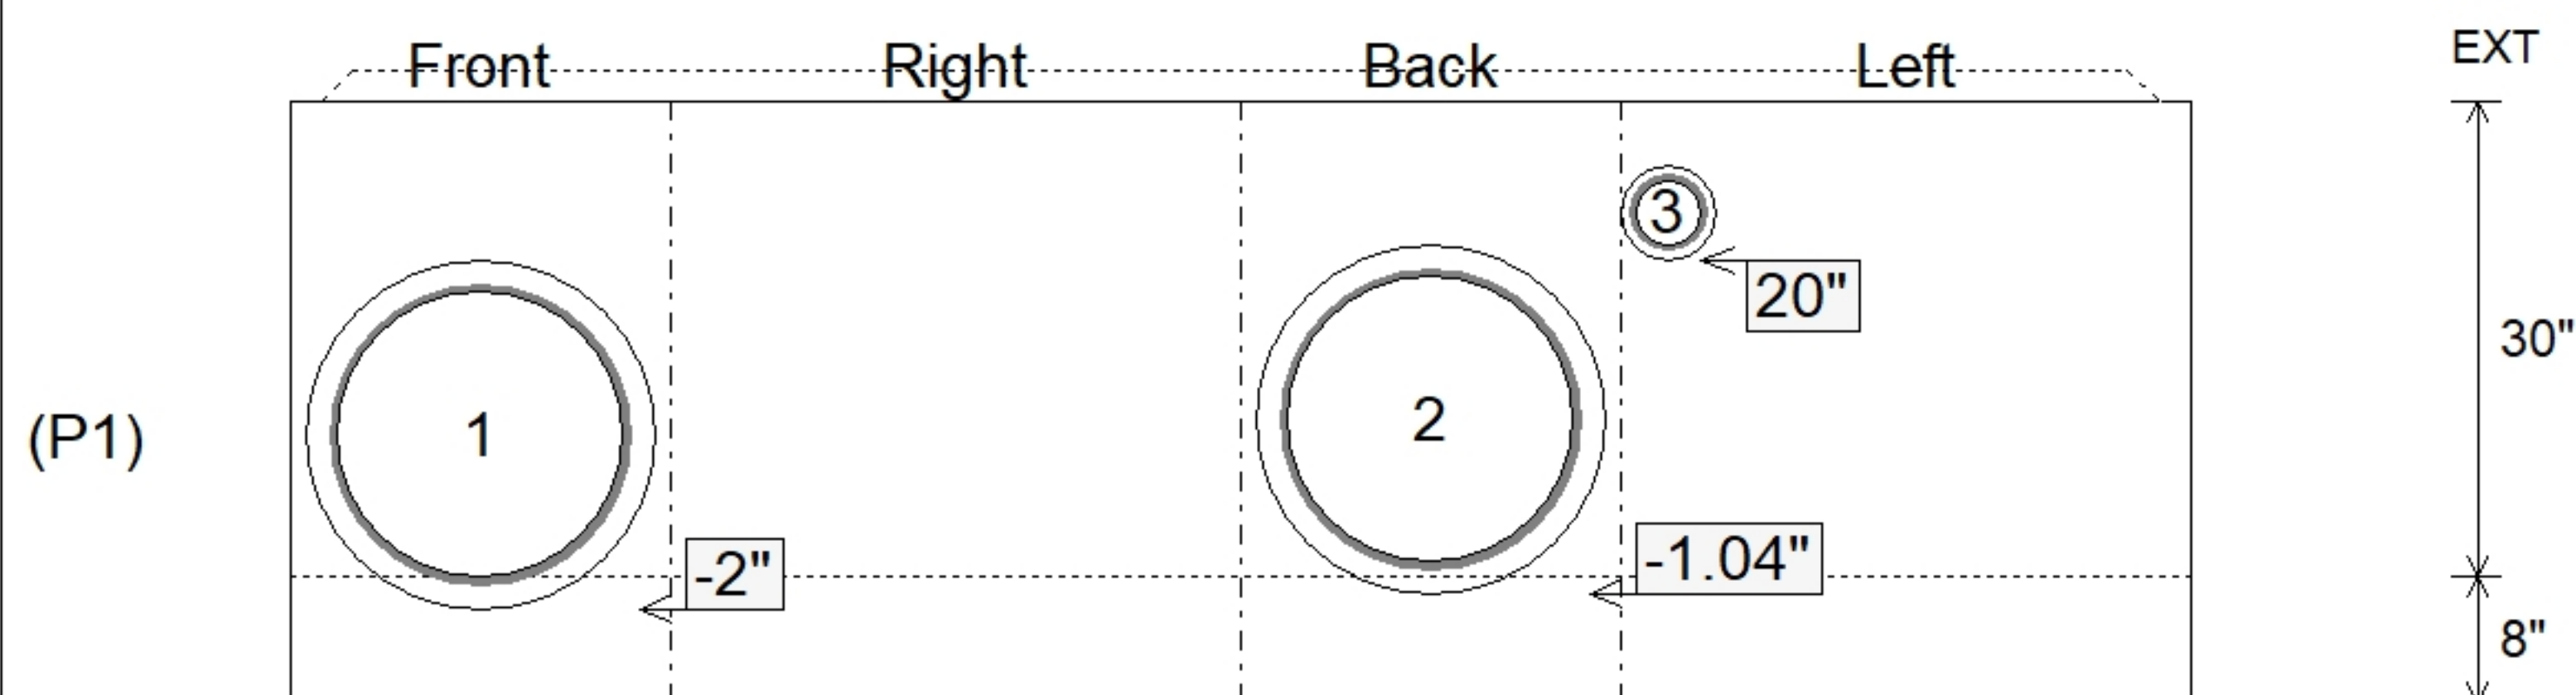

Submittal Drawing  
7/28/2026 3:10:55 PM

SUBMITTAL  
APPROVED BY:
