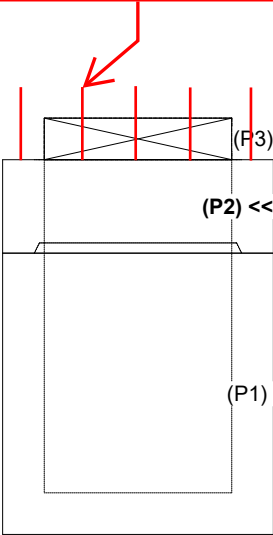




Job Name: 26-1635 - KYTC Oldham Co (261505) Job Location: Pee wee Valley, KY Contractor: Cleary Construction, Inc.					Plant: 100 7/27/2026 11:40:09 AM		Tech: Jared - F PC: T. Ryan				
Structure ID: 17100-129 DBI4 - 37A											
P2 BX3648-08R18			BOX RISER 8inW F/G								
P3) 36" x 48" - P.I.P. - BY OTHERS - 8" P2) 36" x 48" - BOX RISER 8inW F/G - 18" P1) 36" x 48" - BOX BASE 8inW, 8inF, Variable Ht T/n - 46" 2) 36" x 48" - Conseal CS-102 1.00" 1) Hole - 34						0 lb 2417 lb 7801 lb 0 lb 0 lb ----- 10217 lb		Structure Notes: . **KYTC STATE PROJECT** 1. KYTC DBI TYPE 4 / ASTM C913 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. STUB #5 BARS 20" OUT TOP OF WALLS (SPA@12"C/C) 4. CASTING SUPPLIED BY OTHERS (HOE KY-410 (DBI4)). REINFORCING PER ASTM A615 (GRADE 60). - WALLS (As .31) #5 BARS AT 12" C.C.E.W. - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.			
Rim: 839.97' Rim to Invert: 6' Slack: 0" Sump: 0" Step Position:											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset	
Invert 1											
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											
RIGHT-SIDE UP VIEW (int. dimensions)											
#5 DOWELS @ 12" O.C. STUBBED 20" OUT THE TOP OF THE WALLS 											
INSIDE WALL DIMENSIONS											
(P2)											
Coating (Int): Coating (Ext):				Seam Up: Flat Seam Dn: Groove		Wall Thickness: 8" Floor Height: 0"		Height (Int): 18" Height (Ext): 18"		Weight (Net): 2417 lb Volume (Net): 0.62cu.yd	
