



Job Name: 26-1635 - KYTC Oldham Co (261505) Job Location: Peewee Valley, KY Contractor: Cleary Construction, Inc.					Plant: 100 7/27/2026 11:36:03 AM		Tech: Jared - F PC: T. Ryan			
Structure ID: 49892L-81 CBIA										
P1 BX2436-08BA42			BOX BASE 8inW, 8inF T/n							
P3) 24" x 120" - CB INLET KY A 10' TOP SAG F/G - 10" P2) 24" x 120" - CB INLET KY A 10' BOTTOM SAG T/G - 18" P1) 24" x 36" - BOX BASE 8inW, 8inF T/n - 42" 1) CASTING - HOE KY-206 F/C (KY CBI A) 1) 24" x 36" - Conseal CS-102 1.00" 2) Hole - 28 2) Hole - 18					3398 lb 5270 lb 4606 lb 206 lb 0 lb 0 lb 0 lb ----- Structure Total: 13480 lb		Structure Notes: ** KYTC STATE PROJECT ** 1. PER KYTC CBI TYPE A / ASTM C913 SPEC'S. 2. CONCRETE = 4,000 PI AT 28 DAYS. 3. CASTING BY ICAST (HOE KY-206 F/C (KY CBI A)). REINFORCING PER ASTM A615 (GRADE 60). - TOP PHASE (As .62) #5 BARS AT 6" C.C.E.W. - WALLS (As .31) #5 BARS AT 12" C.C.E.W. - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.			
Rim: 800.64' Rim to Invert: 6.07' Slack: 2.84" Sump: 0" Step Position:										
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	794.57'	90°	26"	24" CMP	25"	Hole 28	28"	28"	-2"	0"
Invert 2	794.57'	180°	20"	24" CMP	25"	Hole 28	28"	26"	-2"	0"
Invert 3	794.57'	270°	26"	15" CMP	16"	Hole 18	18"	18"	-1.5"	0"
Invert 4	794.57'	340°	16.875"	15" CMP	16"	Hole 18	18"	19.155"	-1.5"	6"
Invert 5										
Invert 6										
Invert 7										
Invert 8										


RIGHT-SIDE UP VIEW (int. dimensions)

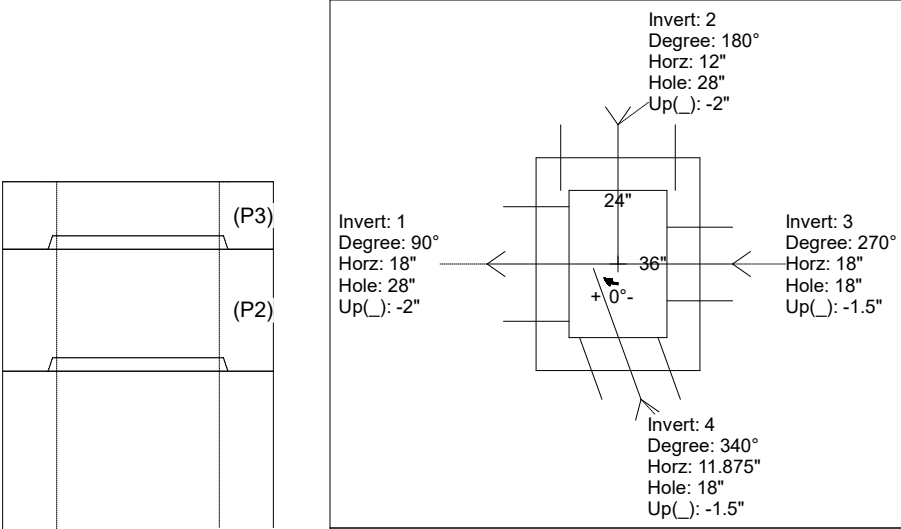

UPSIDE-DOWN VIEW (int. dimensions)

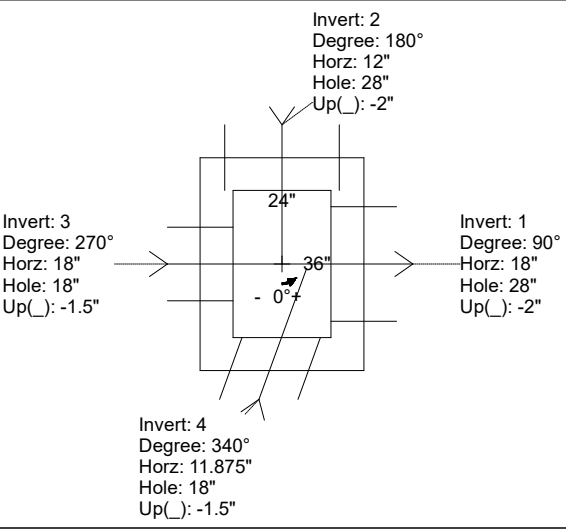

INSIDE WALL DIMENSIONS

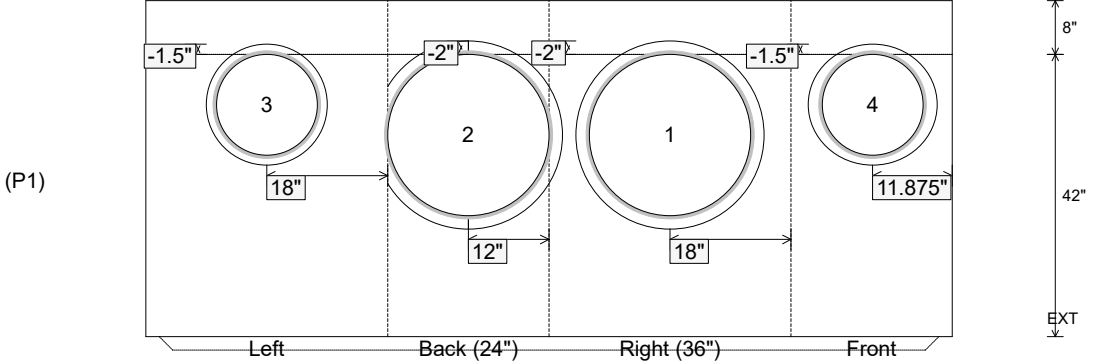

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 8" Floor Height: 8"	Height (Int): 42" Height (Ext): 50"	Weight (Net): 4606 lb Volume (Net): 1.18cu.yd
----------------------------------	---------------------------------	--	--	--
