

Job Name: 26-1635 - KYTC Oldham Co (261505)
Job Location: Pee wee Valley, KY
Contractor: Cleary Construction, Inc.

Plant: 100

8/14/2026 1:21:09 PM

Tech: Jared - F

PC: T. Ryan



Structure ID: 38900-133 DBI13G

P3 BX024030-08LD08-15X27

CB FLAT TOP 8"W w/15"x27" HOLE F/F

P4) 15" x 27" - P.I.P. - BY OTHERS - 8"
P3) 24" x 30" - CB FLAT TOP 8"W w/15"x27" HOLE F/F - 8"
P2) 24" x 30" - BOX RISER 8inW F/G - 18"
P1) 24" x 30" - BOX BASE 8inW, 8inF, Variable Ht T/n - 38"
2) 24" x 30" - Conseal CS-102 1.00"
1) 15" x 27" - Conseal CS-102 1.00"
1) Hole - 22
1) Hole - 20
2) Hole - 4

0 lb
963 lb
1675 lb
4340 lb
0 lb
0 lb
0 lb
0 lb
0 lb
0 lb

Structure Total: 6979 lb

Structure Notes:

****KYTC STATE PROJECT****


1. KYTC DBI TYPE 13G / ASTM C-913 SPEC'S.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. STUB #5 BARS 6" OUT TOP OF SLAB (SPA@12"C/C).
4. CASTING SUPPLIED BY OTHERS (HOE KY-230-G F/G (GRADE)).

REINFORCING PER ASTM A615 (GRADE 60).


- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W. (DOUBLE MAT)

- WALLS (As .31) #5 BARS AT 12" C.C.E.W..

- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

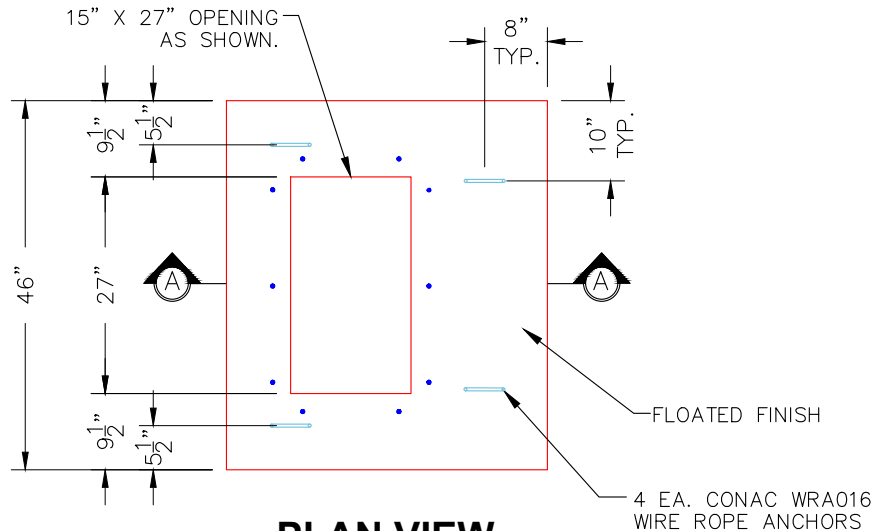

PLAN VIEW

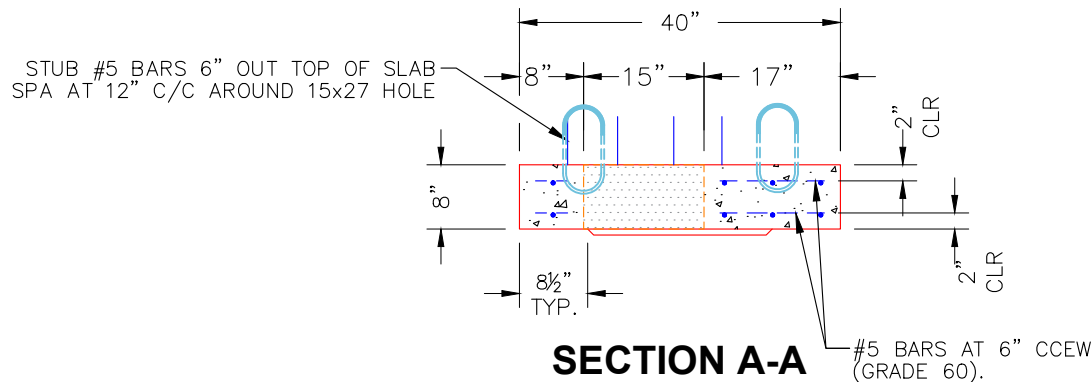

SECTION A-A

NOTES:

1. MANUFACTURED TO ASTM C-913 (LATEST REVISION).
2. CONCRETE: 4,000 PSI AT 28 DAYS.
3. REINFORCING: #5 BAR @ 6" O.C. E.W. (DOUBLE MAT) (GRADE 60).

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Flat

Wall Thickness: 8"

Height (Ext): 8"

Weight (Net): 963 lb
Volume (Net): 0.25cu.yd
