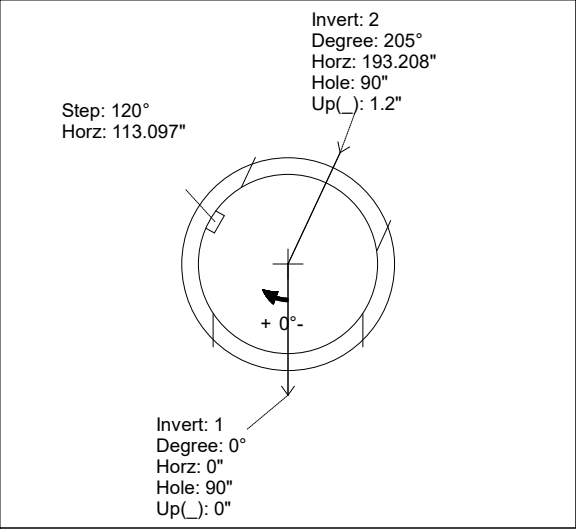
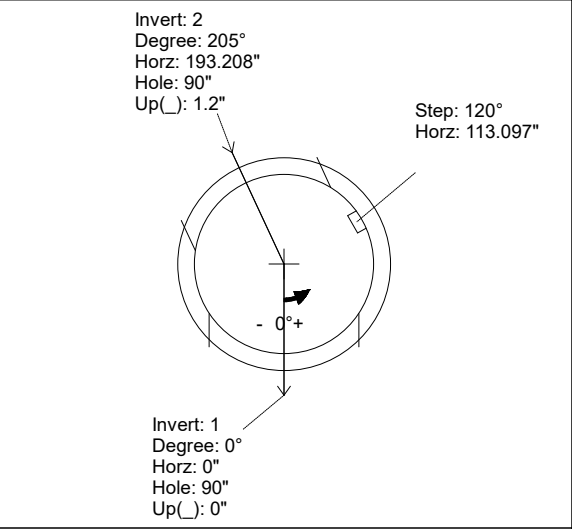
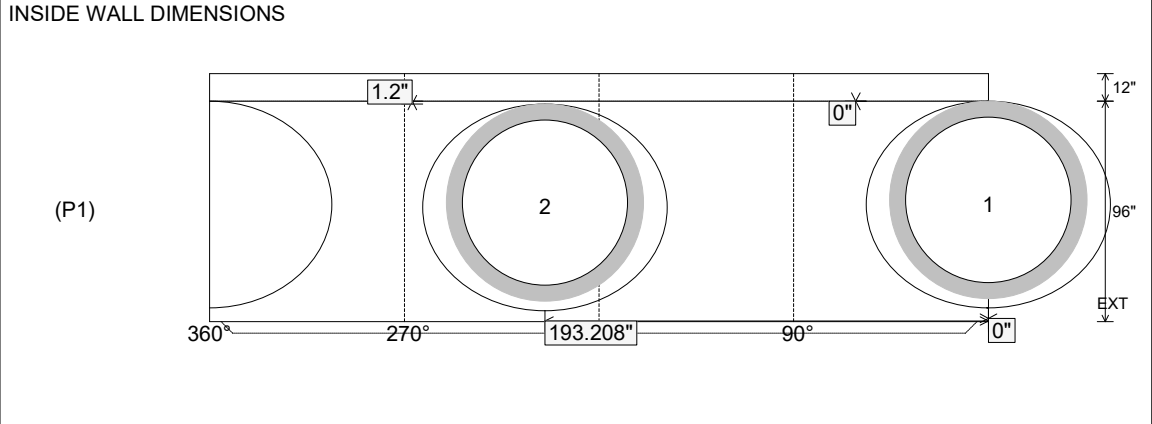


Job Name: 26-1987P6 - Project Nova Job Location: Sullivan, IN 47882 Contractor: McCreary Concrete Products, Inc.					Plant: Beaver Dam 9/3/2026 3:12:41 PM		Tech: J. Coppage PC: M. Sullivan						
Structure ID: 1414													
P1		MH108BA96										MH BASE	
P6) 24" x 36" - CASTING HEIGHT - 6" P5) 24" x 36" - GRADE RING - 4" P4) 108" - MH FLAT TOP w/24in X 36in ECC Hole - 17" P3) 108" - MH RISER - 78" P2) 108" - MH RISER - 96" P1) 108" - MH BASE - 96" 3) 108" - Conseal CS-102 1.00" 2) 24" x 36" - Conseal CS-102 1.00" 2) Hole - 90 4) Hole - 6 22) MH Step ML-10-TDS-NCR - 10"						0 lb 408 lb 12900 lb 24168 lb 29863 lb 30589 lb 0 lb 0 lb 0 lb 0 lb 0 lb 0 lb Structure Total: 97928 lb		Structure Notes: 1. (CASTING PROVIDED BY OTHERS) 2. PER ASTM C478 SPECIFICATIONS. 3. CONCRETE = 4,000 PSI AT 28 DAYS. 4. REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.. - RISER/WALLS (As .36) - FLOOR (As .47) #5 BARS AT 8" C.C.E.W. 4 EA - 8CA18 A-Anchors In The Floor For Handling					
Rim: 511.95'		Rim to Invert: 24.24'		Slack: 0.88"		Sump: 7"		Step Position: 120					
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset			
Invert 1	487.71'	0°	0"	72" RCP B WALL	86"	Hole 90	90"	106.392"	0"	0"			
Invert 2	487.81'	205°	228.987"	72" RCP B WALL	86"	Hole 90	90"	106.392"	1.2"	0"			
Invert 3													
Invert 4													
Invert 5													
Invert 6													
Invert 7													
Invert 8													
RIGHT-SIDE UP VIEW (int. dimensions)  UPSIDE-DOWN VIEW (int. dimensions) 													
INSIDE WALL DIMENSIONS 													
Coating (Int): Coating (Ext):			Seam Up: Tongue Seam Dn: n/a		Wall Thickness: 10" Floor Height: 12"		Height (Int): 96" Height (Ext): 108"		Weight (Net): 30589 lb Volume (Net): 7.81cu.yd				
