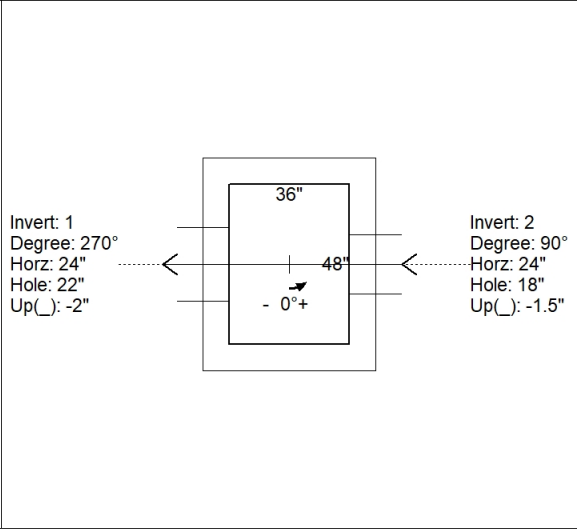
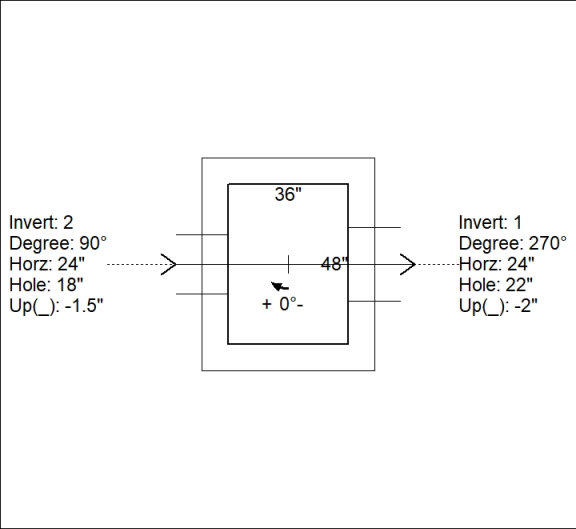
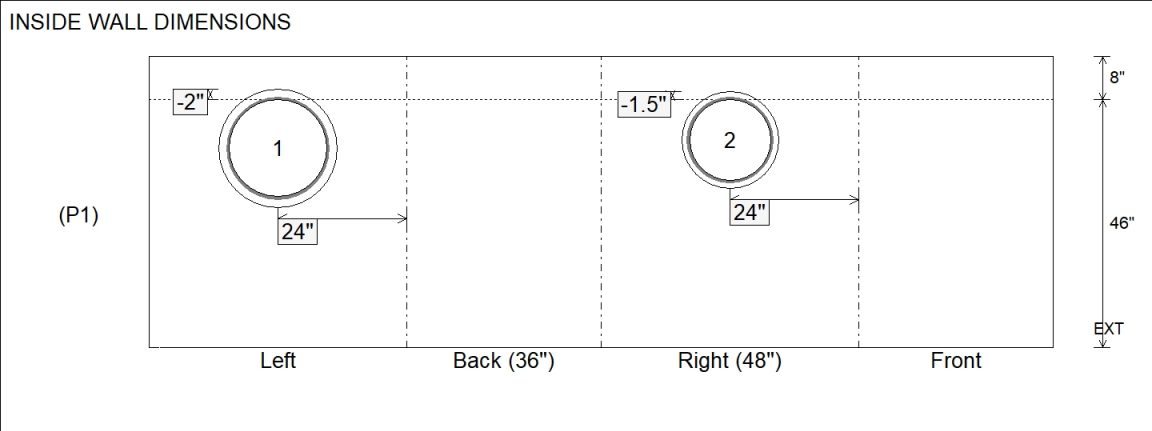


Job Name: 26-2030 - KYTC McCracken Co. Call 111 (ID 264505) Job Location: Paducah, KY Contractor: Jim Smith Contracting Co, LLC					Plant: 100 6/12/2026 7:49:32 AM		Tech: J. Horsley PC: J. Jarvis				
Structure ID: 144+26 S1 DBI-5D											
P1		BX3648-08BAVF		BOX BASE 8inW, 8inF, Variable Ht F/n							
P2) 36" x 48" - P.I.P. - BY OTHERS - 8" P1) 36" x 48" - BOX BASE 8inW, 8inF, Variable Ht F/n - 46" 1) CASTING - HOE KY-460 SET (DBI 5D) 1) 36" x 48" - Conseal CS-102 1.00" 1) Hole - 22 1) Hole - 18					0 lb 7984 lb 460 lb 0 lb 0 lb 0 lb ----- Structure Total: 8444 lb		Structure Notes: **KYTC STATE PROJECT** 1. KYTC DBI TYPE 5 / ASTM C913 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY ICAST (HOE KY-460 (DBI 5D). 4. STUB #5 BARS 20" OUT TOP OF WALLS (SPA@12"C/C) REINFORCING PER ASTM A615 (GRADE 60). - WALLS (As .31) #5 BARS AT 12" C.C.E.W. - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.				
Rim: 370.46' Rim to Invert: 4.54' Slack: 0.48" Sump: 0" Step Position:											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	365.92'	270°	32"	18" CMP	19"	Hole 22	22"	22"	-2"	0"	
Invert 2	365.92'	90°	32"	15" CMP	16"	Hole 18	18"	18"	-1.5"	0"	
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											
RIGHT-SIDE UP VIEW (int. dimensions) UPSIDE-DOWN VIEW (int. dimenions)											
											
INSIDE WALL DIMENSIONS											
											
Coating (Int): Coating (Ext):			Seam Up: Flat Seam Dn: n/a		Wall Thickness: 8" Floor Height: 8"		Height (Int): 46" Height (Ext): 54"		Weight (Net): 7984 lb Volume (Net): 2.04cu.yd		
