

Job Name: 26-2119 512 W Kingston Ave MSD
Job Location: Louisville, KY
Contractor: TRC, LLC

Plant: Beaver Dam
7/16/2026 3:43:12 PM

Tech: S. Felletter
PC: T. Lewis



Structure ID: QL1 CB1

P2 MH048LD12S

MH FLAT TOP w/34"x34" Hole F/G


P3) 34" x 34" - CASTING HEIGHT - 3"
P2) 48" - MH FLAT TOP w/34"x34" Hole F/G - 12"
P1) 48" - KO MH 48"Dia X 36" Tall 3 Panel - STOCK T/n - 36"
1) CASTING - HOE 595 F/G
1) SNOUT - BMP SNOUT 18R w/ KIT
1) 48" - Conseal CS-102 1.00"

0 lb
1194 lb
2564 lb
376 lb
25 lb
0 lb

Structure Total: 4159 lb


Structure Notes:
1. PER ASTM C913 SPECIFICATIONS.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. NO INVERT CHANNEL.
4. CASTING BY ICAST (HOE 595 F/G).

REINFORCING PER ASTM A615 (GRADE 60).
- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.
- WALLS (As .12) #5 BARS AT 12" C.C.E.W.
- FLOOR (As .12) #5 BARS AT 12" C.C.E.W.

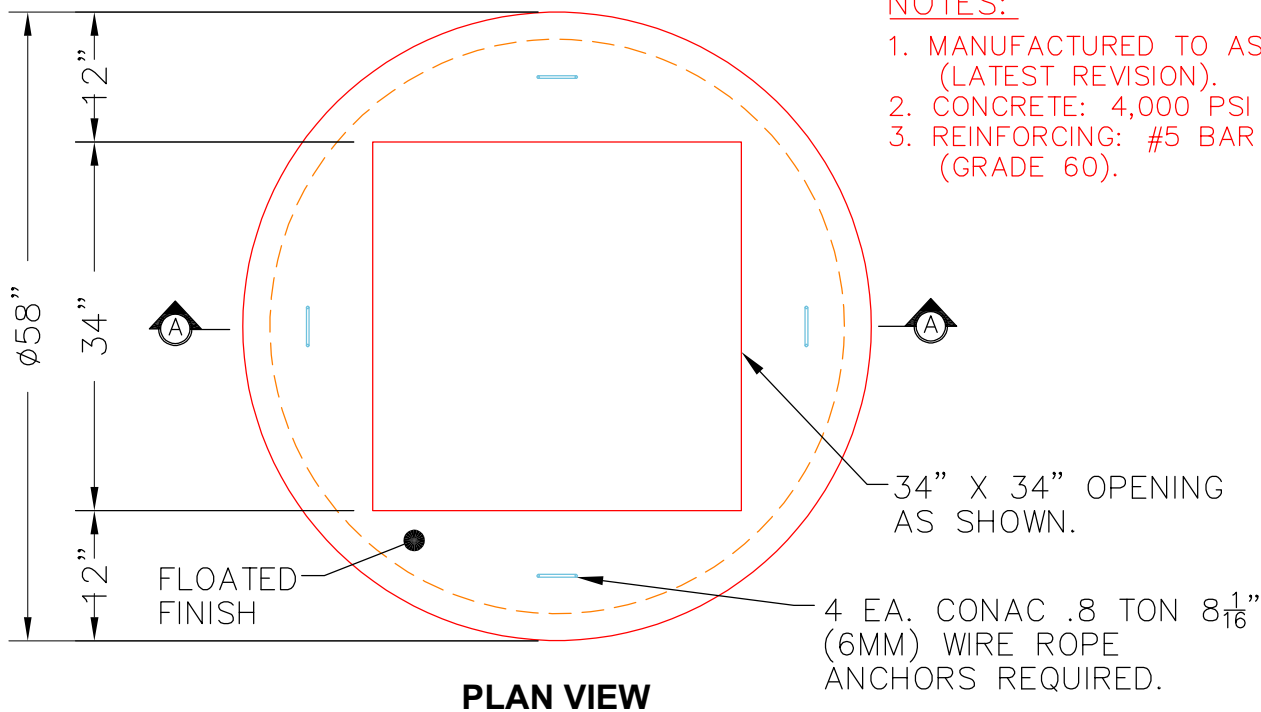

NOTES:

1. MANUFACTURED TO ASTM C-478 (LATEST REVISION).
2. CONCRETE: 4,000 PSI AT 28 DAYS.
3. REINFORCING: #5 BAR @ 6" C.C. E.W. (GRADE 60).

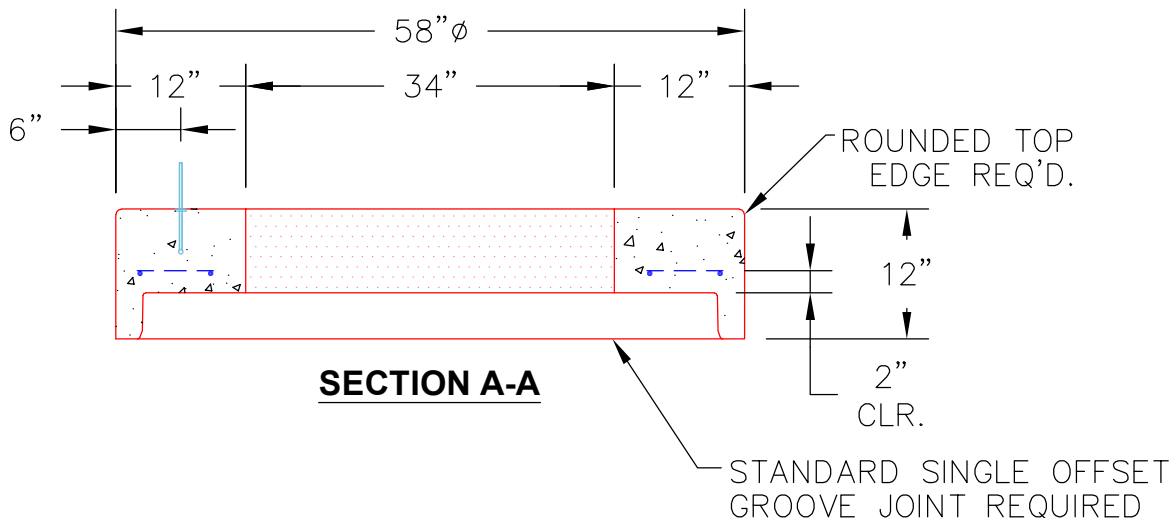

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Groove

Wall Thickness: 5"

Height (Ext): 12"

Weight (Net): 1194 lb
Volume (Net): 0.3cu.yd
