

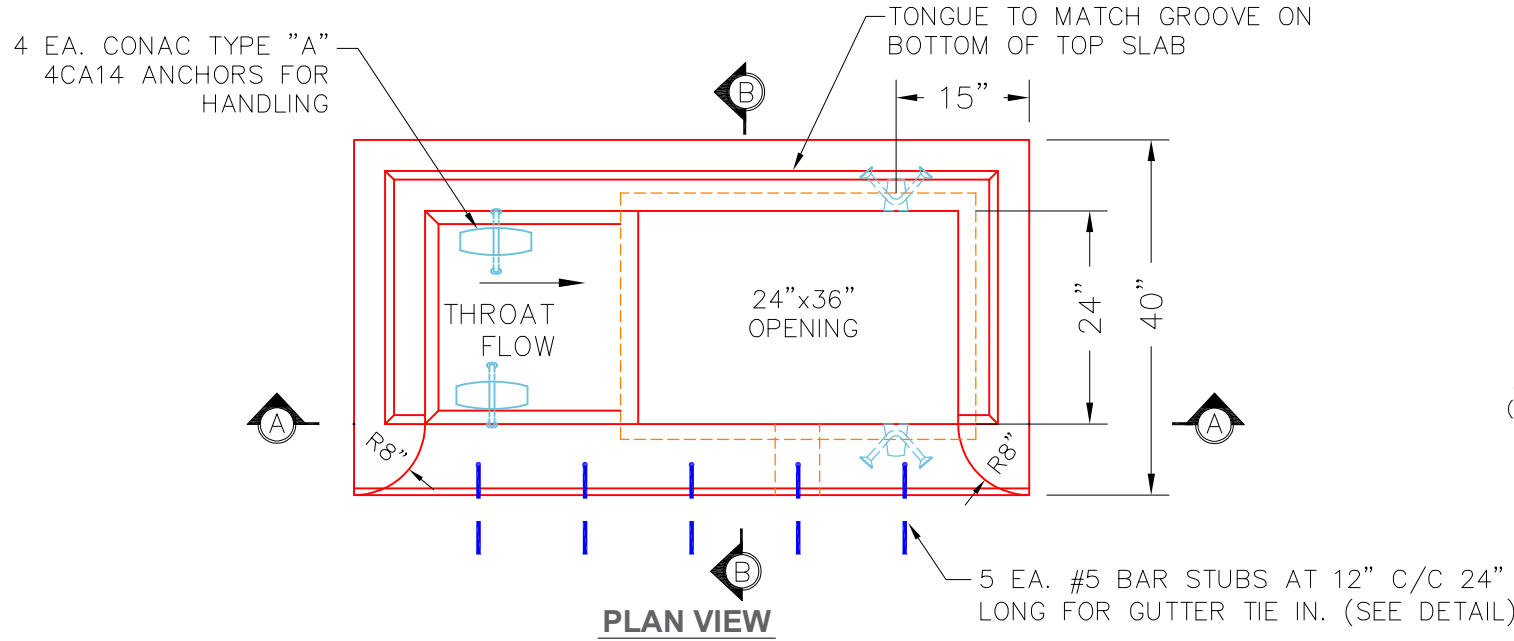


NOTES:



1. MANUFACTURED PER KYTC SPECIFICATIONS.
2. CONCRETE $f'_c = 4,500$ PSI AT 28 DAYS.
3. REINFORCING: #5 BAR @ 12" C/C E.W. (GRADE 60).

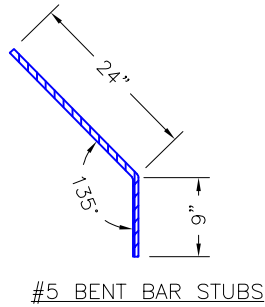

ISOMETRIC VIEW
(5' RIGHT HAND CONFIG.)

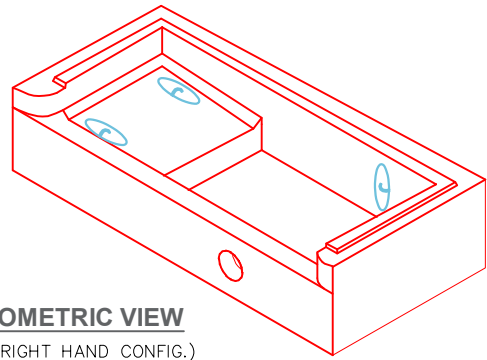

#5 BENT BAR STUBS

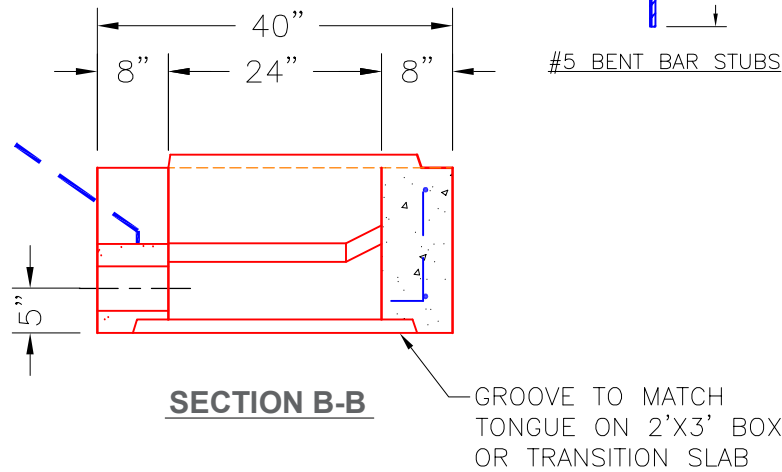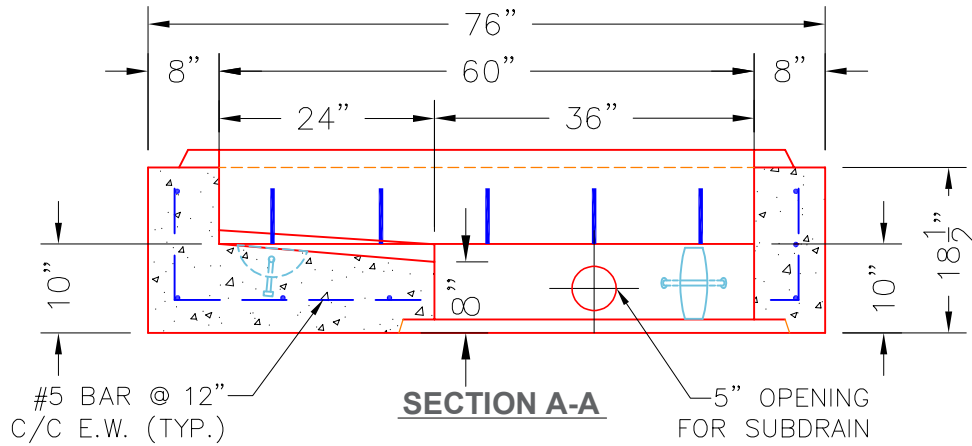

PRODUCTION WORK ORDER

PRODUCT I.D.: CBITA-5BR

DESCRIPTION: KYTC 5' CBI-TYPE A TOP PHASE BOTTOM (RIGHT)

QUALITY CONTROL CHECKLIST

- ☐ ALL DIMENSIONS CORRECT.
- ☐ LIFTERS INSTALLED.
- ☐ CASTING AT CORRECT LOCATION.
- ☐ REINFORCING CORRECT.
- ☐ EXTENDED REBAR INSTALLED.
- ☐ KYTC THROAT CORRECT.
- ☐ ALL PATCHWORK ACCEPTABLE.

PRODUCT VIEW: RIGHT SIDE UP

CUSTOMER: STOCK

PLANT: BEAVER DAM, KY.

PROJECT: STOCK

WEIGHT: 2,580 LBS.

STRUCTURE ID.: STOCK

TOP JOINT: SHIP-LAP TONGUE

SALES ORDER NO.: N/A

BOTTOM JOINT: N/A

CHK.: J.H. ROSS, PE

DRAWING: N. RICHARDS

QC CHECK INITIALS:

DATE: 04/18/24

SCALE: NTS

PG. 1 of 1

