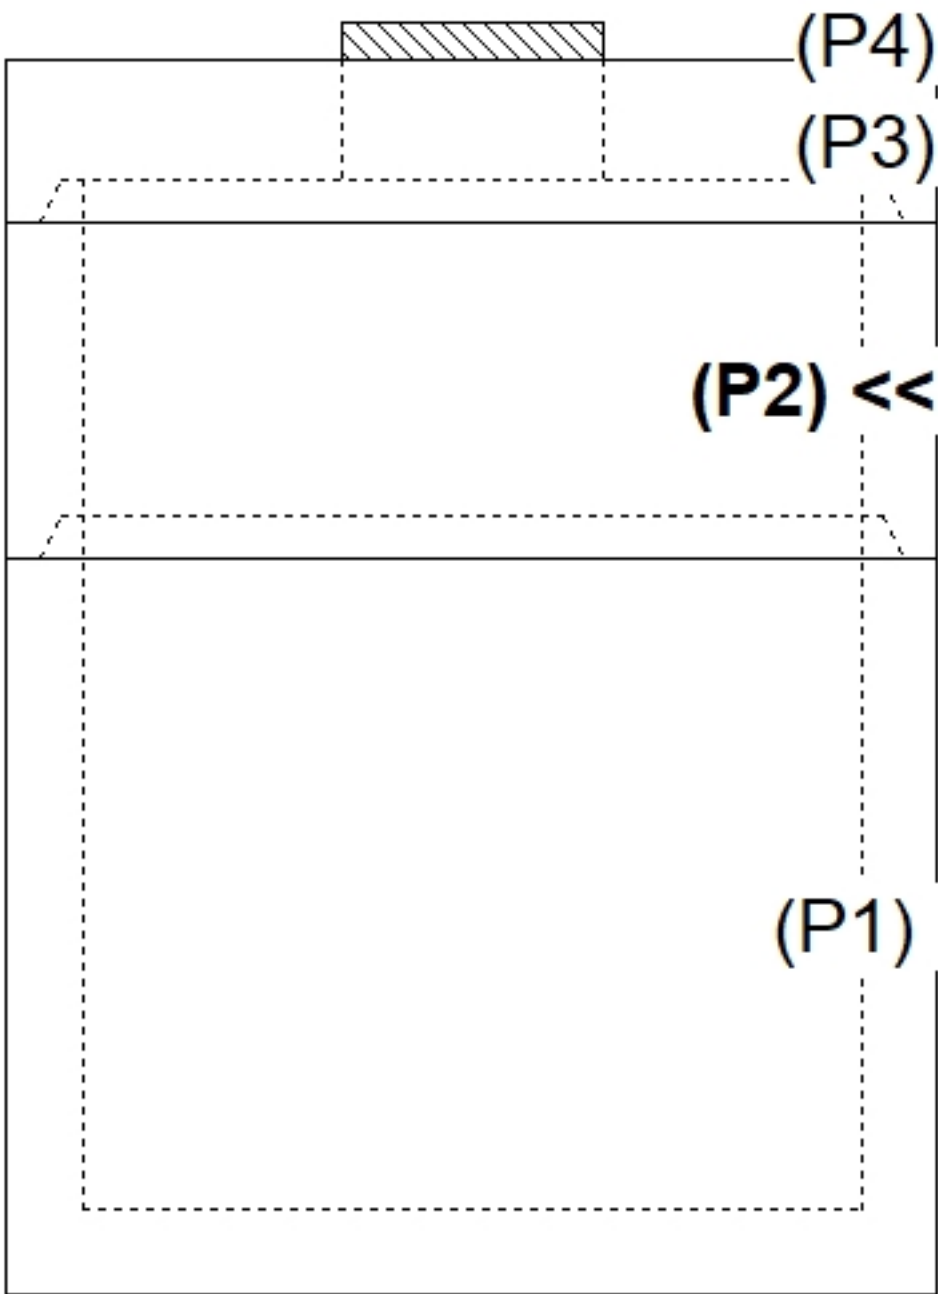
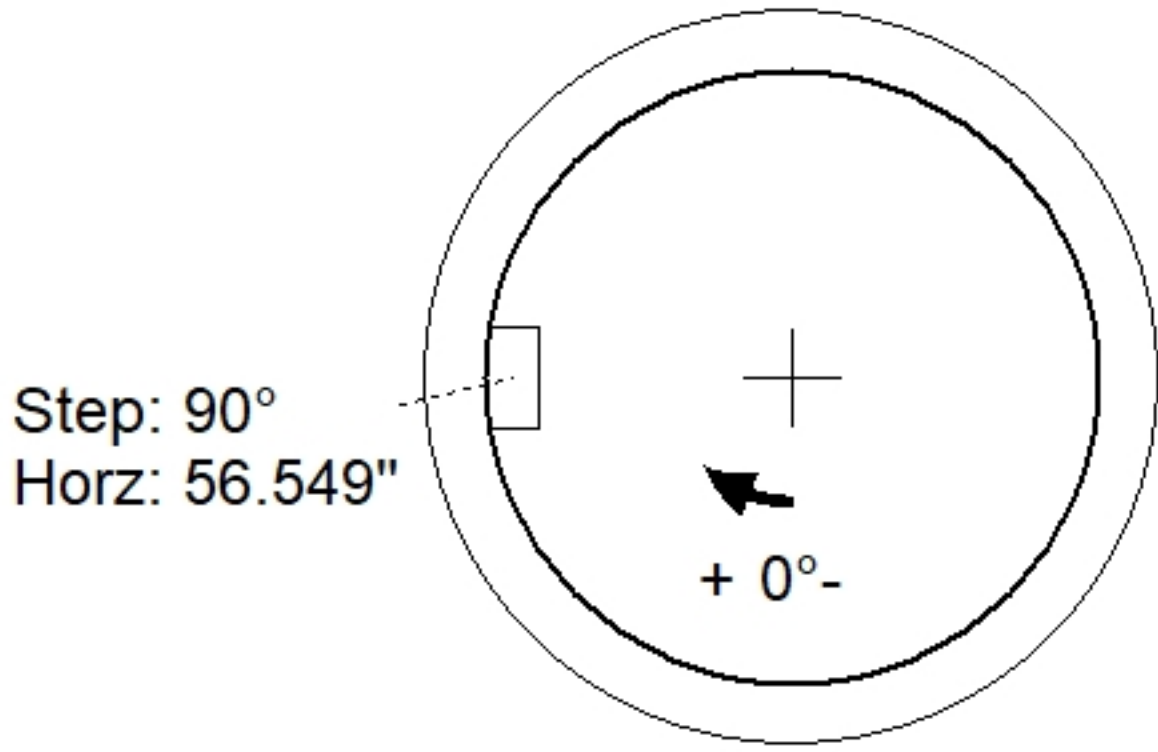
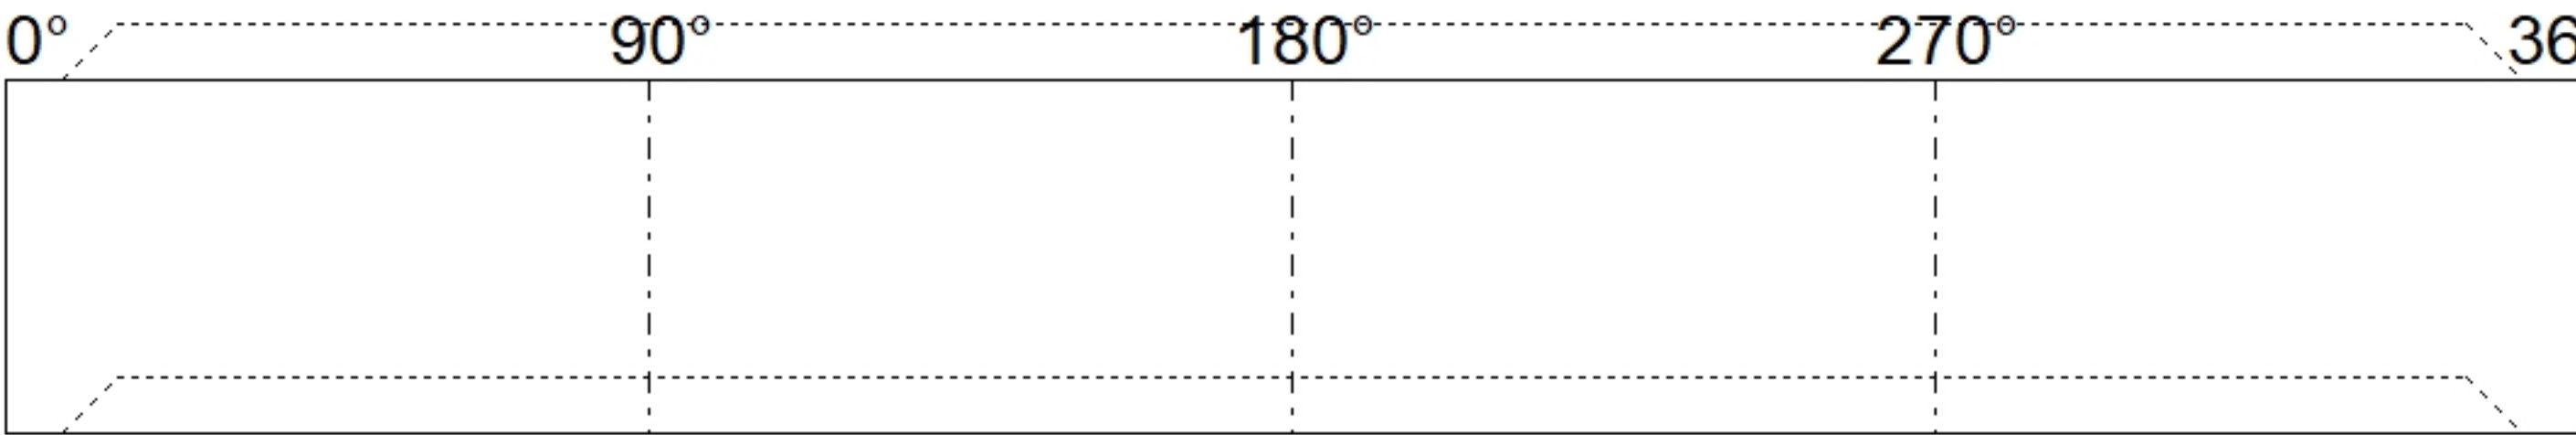


Job Name: 26-1000P2 Clark Distributing New HQ - Site Structures					Plant: Beaver Dam		Tech: S. Felletter				
Job Location: Bowling Green, KY					8/11/2026 9:22:30 AM		PC: M. Sullivan				
Contractor: Scotty's Contracting & Stone, LLC											
Structure ID: DBI-15											
P2		MH072RSVF		MH RISER Custom Ht T/G							
P4) 24" x 30" - CASTING HEIGHT - 3.50" P3) 72" - MH FLAT TOP w/24"x30" Hole LOU-MSD F/G - 15" P2) 72" - MH RISER Custom Ht T/G - 31" P1) 72" - MH BASE T/n - 60" 1) CASTING - HOE KY-460-11 F/G (DBI 11) 2) 72" - Conseal CS-102 1.00" 1) 24" x 30" - Conseal CS-102 1.00" 2) Hole - 50 1) Hole - 16 5) MH Step ML-10-TDS-NCR - 10"					0 lb 6405 lb 4519 lb 10022 lb 421 lb 0 lb 0 lb 0 lb 0 lb 0 lb ----- Structure Total: 21367 lb		Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY ICAST (HOE KY-460-11 F/G). . REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.. - RISER/WALLS (As .18) - FLOOR (As .37) #5 BARS AT 10" C.C.E.W.				
Rim: 589.34' Rim to Invert: 9.13' Slack: 0.06" Sump: 0" Step Position: 90°											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (┘)	Offset	
Invert 1											
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											
RIGHT-SIDE UP VIEW (int. dimensions)  											
INSIDE WALL DIMENSIONS  EXT 31"											
Coating (Int): Coating (Ext):			Seam Up: Tongue Seam Dn: Groove		Wall Thickness: 7" Floor Height: 0"		Height (Int): 31" Height (Ext): 31"		Weight (Net): 4519 lb Volume (Net): 1.15cu.yd		
