

Job Name: 26-1733 - Liberty Power Station
Job Location: Liberty, KY
Contractor: Weddle Enterprises, Inc

Plant: 100

7/20/2026 8:30:34 AM

Tech: Jared - F

PC: T. Ryan



Structure ID: CB-39

P2 MH072LD15-24CC

MH FLAT LID w/24" CC Hole

- P3) 24" - CASTING HEIGHT - 4"
P2) 72" - MH FLAT LID w/24" CC Hole - 15"
P1) 72" - MH BASE Custom Ht - 61"
1) 72" - Conseal CS-102 1.00"
1) 24" - Conseal CS-102 1.00"
2) Hole - 46
5) MH Step ML-10-TDS-NCR - 10"

Structure Total:


0 lb
5097 lb
10703 lb
0 lb
0 lb
0 lb
0 lb
15800 lb

Structure Notes:


1. PER ASTM C478 SPECIFICATIONS.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. NO INVERT CHANNEL.
4. CASTING SUPPLIED BY OTHERS.

REINFORCING PER ASTM A615 (GRADE 60).

- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W..
- RISER/WALLS (As .18)
- FLOOR (As .37) #5 BARS AT 10" C.C.E.W.

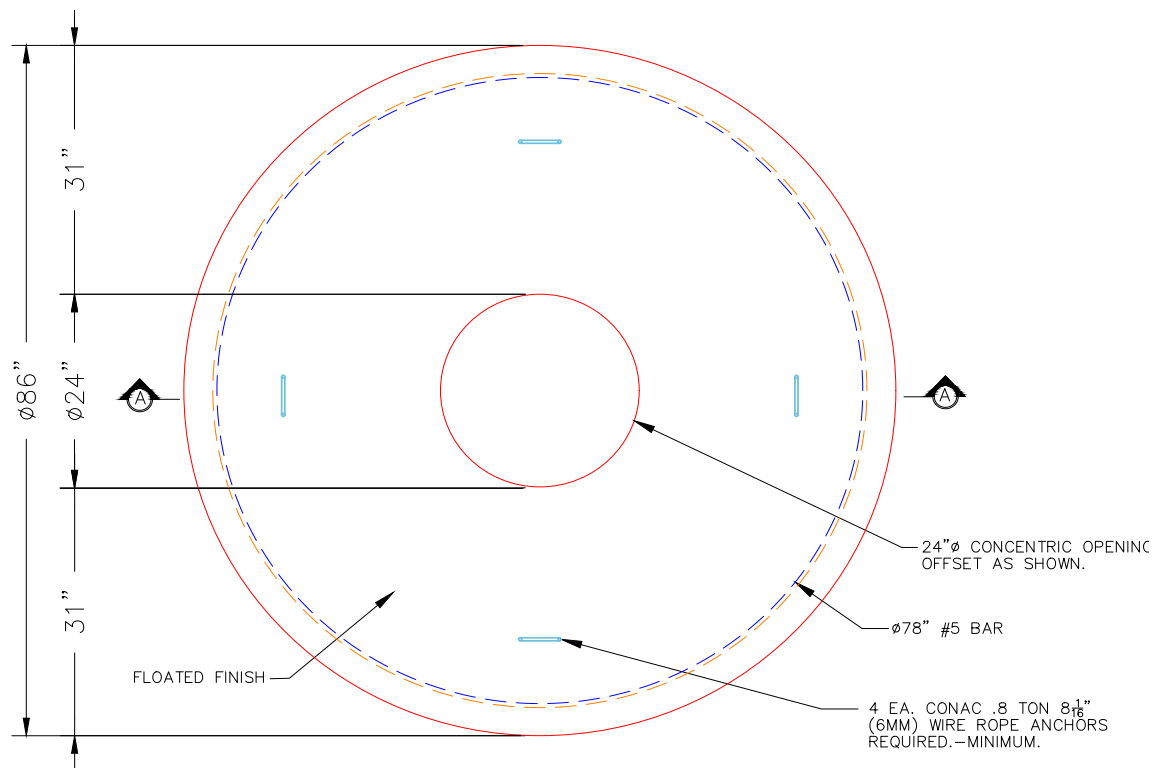

PLAN VIEW

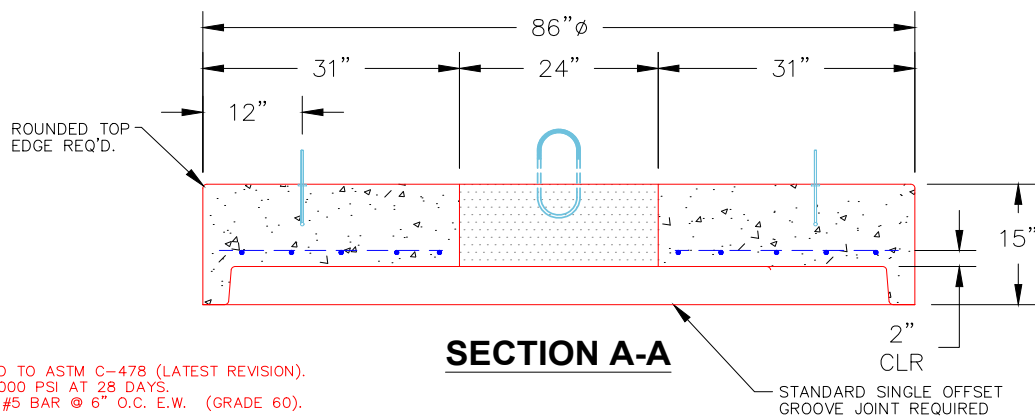

NOTES:

1. MANUFACTURED TO ASTM C-478 (LATEST REVISION).
2. CONCRETE: 4,000 PSI AT 28 DAYS.
3. REINFORCING: #5 BAR @ 6" O.C. E.W. (GRADE 60).

SECTION A-A

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Groove

Wall Thickness: 7"

Height (Ext): 15"

Weight (Net): 5097 lb
Volume (Net): 1.3cu.yd
