




Job Name: 26-1814 - Brownsville Sewer System Additions Job Location: Cave City, KY Contractor: Luttrell & Sons, LLC					Plant: 100 7/31/2026 1:28:15 PM		Tech: Jared - F PC: A. Chambers			
Structure ID: 108+25 ARV										
P1 MH048DHVF			MH DH RISER Custom Ht T/F							
P3) 24" - CASTING HEIGHT - 7" P2) 48" - MH FLAT TOP w/ 24" ECC Hole F/G - 12" P1) 48" - MH DH RISER Custom Ht T/F - 41" 1) CASTING - HOE MC-375 F/C Sanitary 1) 48" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 1) Hole - 0					0 lb 1561 lb 2864 lb 271 lb 0 lb 0 lb 0 lb ----- Structure Total: 4696 lb		Structure Notes: . 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. NO STEPS. 4. CASTING SUPPLIED BY ICAST (HOE MC-375 F/C "SANITARY") REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB = H20 LOADING. - RISER/WALLS (As .12)			
Rim: 5' Rim to Invert: 5' Slack: 0" Sump: 0" Step Position:										
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset
Invert 1	0'	0°	0"	0" No Hole	0.01"	Hole 0	0"	0"	0"	0"
Invert 2										
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

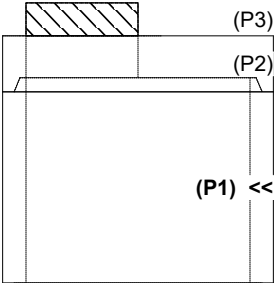


RIGHT-SIDE UP VIEW (int. dimensions)

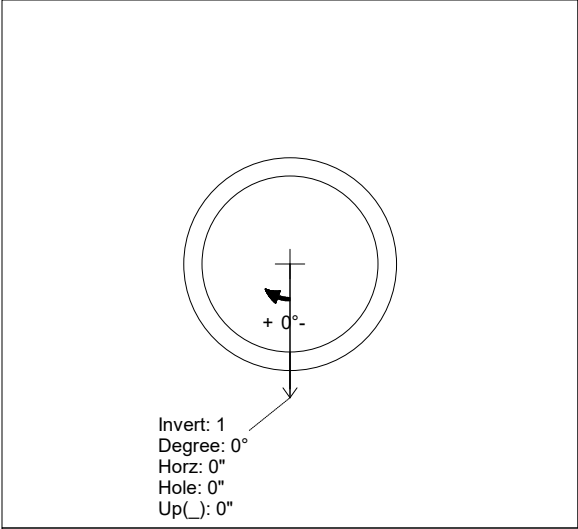

UPSIDE-DOWN VIEW (int. dimenions)



INSIDE WALL DIMENSIONS

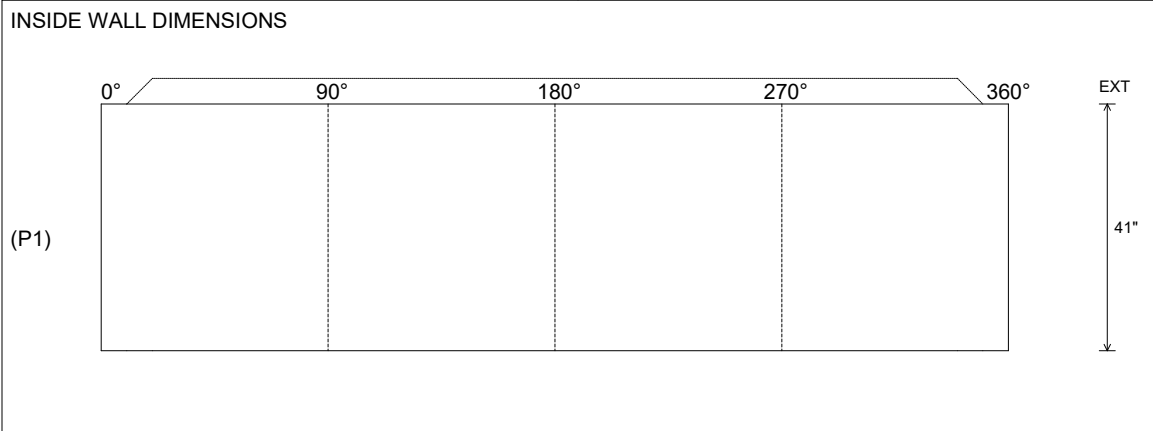

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: Flat	Wall Thickness: 5" Floor Height: 0"	Height (Int): 41" Height (Ext): 41"	Weight (Net): 2864 lb Volume (Net): 0.73cu.yd
----------------------------------	----------------------------------	--	--	--
