

Job Name: 26-2254 - Wilder Box Culvert
Job Location: Wilder, KY
Contractor: Eaton Asphalt



Plant: 100
7/6/2026 1:23:22 PM

Tech: Jared - A
PC: E. Bradley





Structure ID: Box Culvert
P21 BC168144-12W12T12F-12H BOX CULVERT (12W/12F/12T) T/G

- NOTES:
- 1. BOX CULVERT IS DESIGNED PER ATTACHED PE STAMPED DRAWINGS & CALCULATIONS.
 - 2. LOAD REQUIREMENTS PER KY-HL93 (KY TABLE 1)
 - 3. COVER DEPTH = 15' - 0"
 - 4. CONCRETE: 5,000 PSI AT 28 DAYS.
 - 5. REINFORCING: AS SHOWN BY MATT CHILDS ENGINEERING.
 - 6. BOX CULVERT TO BE SEALED WITH CS-102 ROLL BUTYL MASTIC & CS-212 12" WRAP. (SUPPLIED BY ICAST).
 - 7. WEIGHT: 48,363 LBS.

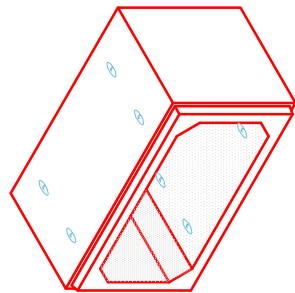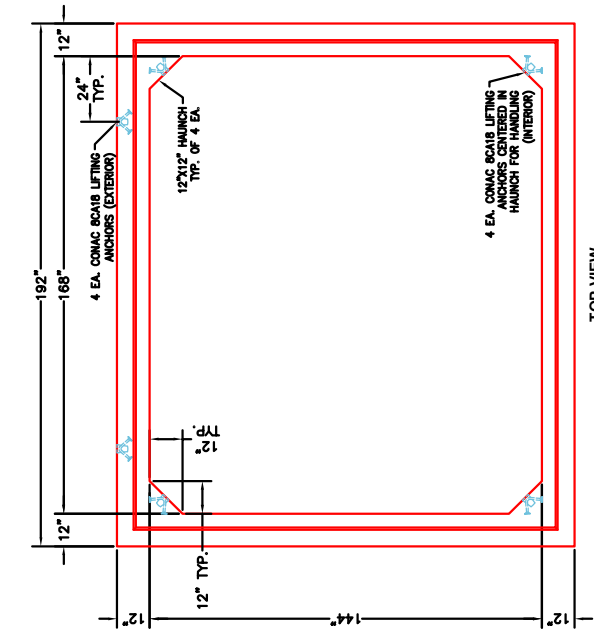


COMPONENT ISOMETRIC VIEW

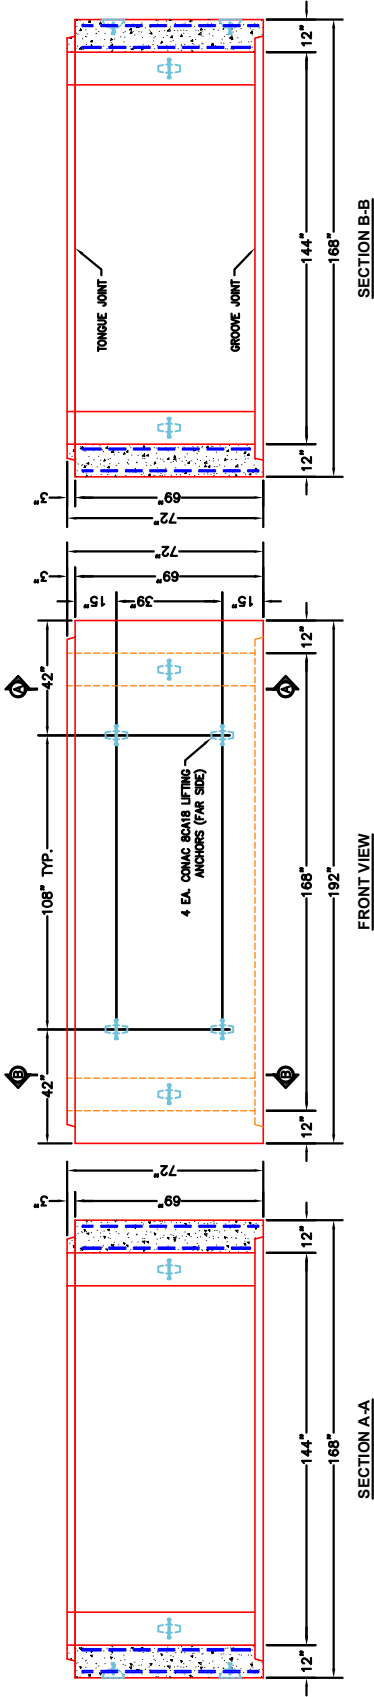

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: Groove	Wall Thickness: 12" Floor Height: 0"	Height (Int): 69" Height (Ext): 69"	Weight (Net): 48363 lb Volume (Net): 12.35cu.yd
----------------------------------	------------------------------------	---	--	--

Project: Mooch Road
Product: 14' x 12' Box Culvert
Job: 26-2254
Design No.:
Location: Wilder, KY
Reference #:



MATT CHILDS ENGINEERING, PLLC

Project : City of Wilder
Task : 14x12 15' Fill
Job No. :

Client: ICast
File: 20260605-ICast-CityofWilder-14x12(15'Fill).etcx

Sht ____ of ____
By:MBJ
Ck:
6/5/2026 4:35:08 PM
p. 1 of 2

Spec.: LRFD 9th ed.
Type of Culvert: Precast

Physical Dimensions

Clear Span:	14'-0"
Clear Height:	12'-0"
Top Slab:	1'-0"
Bottom Slab:	1'-0"
Ext. Wall:	1'-0"
Fill Depth:	15.00 ft
Length:	4'-0"
Skew Angle:	0.00 deg
Bottom Slab Support:	Full Slab
Top Haunch, Width:	1'-0"
Top Haunch, Height:	1'-0"
Bottom Haunch, Width:	1'-0"
Bottom Haunch, Height:	1'-0"

Material Properties

Concrete
Strength, f_c: 5.000 ksi
Density: 0.150 kcf
Elasticity, E_c: 3834 ksi
Type: Normal wt

Steel
Yield, f_y: 65 ksi
Allow Stress: 39 ksi
Elasticity, E_s: 29000 ksi

Soil
Density: 0.120 kcf

Exposure Factor
Class 2 Exposure
Reinforcement Covers
Ext. Cover Top Slab: 1"
Ext. Cover Bottom Slab: 1"
Ext. Cover Walls: 1"
Int. Cover Walls: 1"
Int. Cover Top Slab: 1"
Int. Cover Bottom Slab: 1"

Controlling Ratings

Inventory Rating: 5.85
Operating Rating: 7.59



Loads

Live Load
Vehicle Names: HL-93
Traffic Direction: Parallel
Eq. Height of Soil: 2.00 ft (Calc'd)

Dead Load
Future Wearing Surface: 0.000 klf
Additional Dead Load: 0.000 klf
Concentrated Loads: none

Lateral Soil Loads
Eq. Fluid Press. Max: 60.00 pcf
Eq. Fluid Press. Min: 30.00 pcf

Interior Water Pressure: yes, head pressure = 0 ft
Exterior Water Pressure: no

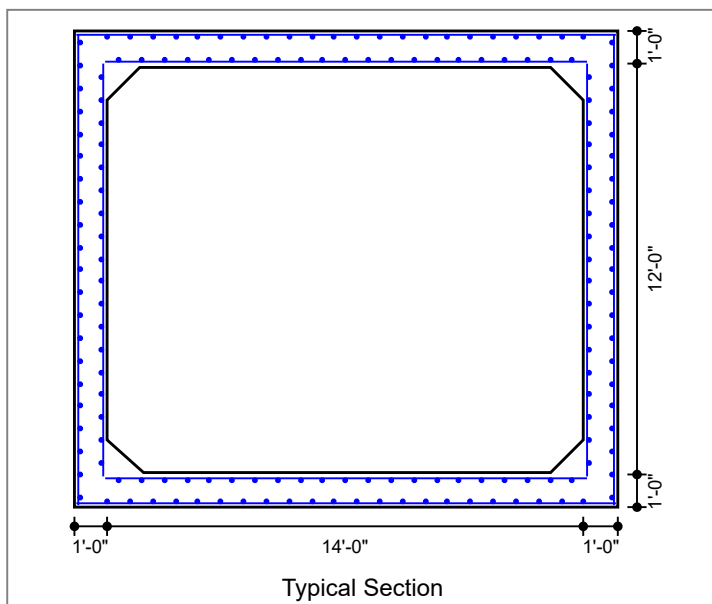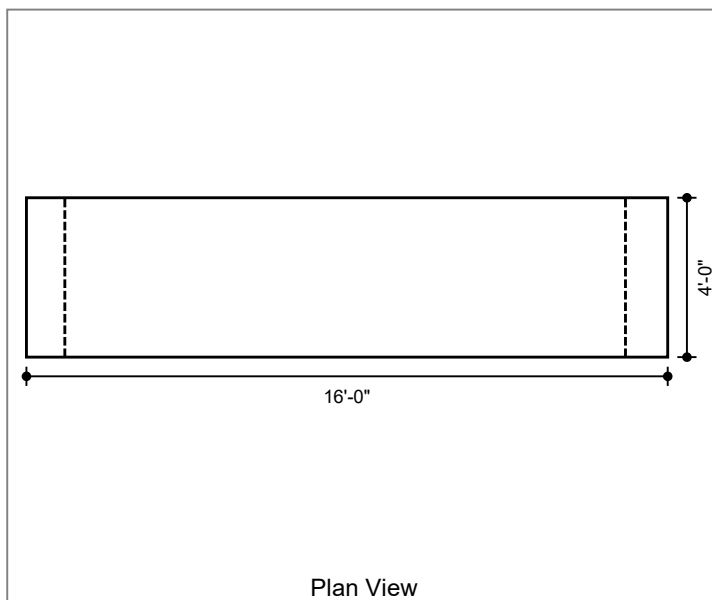

MATT CHILDS ENGINEERING, PLLC

Project : City of Wilder

Task : 14x12 15' Fill

Job No. :

Client: ICast

File: 20260605-ICast-CityofWilder-14x12(15'Fill).etcx

Sht ____ of ____

By:MBJ

Ck: _____

6/5/2026 4:35:09 PM

p. 2 of 2

Concrete Summary

Volume of Concrete: 2.148 cy/ft Total Volume of Concrete: 8.593 cy

Reinforcing Steel Bar Schedule (lb)

Location	Mark	Sheets Included	As Provided
Top Slab(Int)	A100 (AS2)	Top	1.200
Bot Slab(Int)	A200 (AS3)	Bot	1.290
Top Slab(Ext)	A300 (AS7)	Top	0.300
Bot Slab(Ext)	A400 (AS8)	Bot	0.300
Corner(Top)	A1 (AS1)	Top	0.780
Corner(Bot)	A2 (AS1)	Bot	0.780
Wall(Int)	B1 (AS4)	L&R	0.300
Wall(Ext)	B2 (AS1)	L&R	0.780
Longit. Top (Int)	C100 (AS5)	Top	0.150
Longit. Bot (Int)	C200	Bot	0.150
Longit. Top (Ext)	C1 (AS6)	Top	0.150
Longit. Bot (Ext)	C1 (AS6)	Bot	0.150
Longit. Wall (Ext)	C1 (AS6)	L&R	0.150
Longit. Wall (Int)	C1 (AS6)	L&R	0.150
