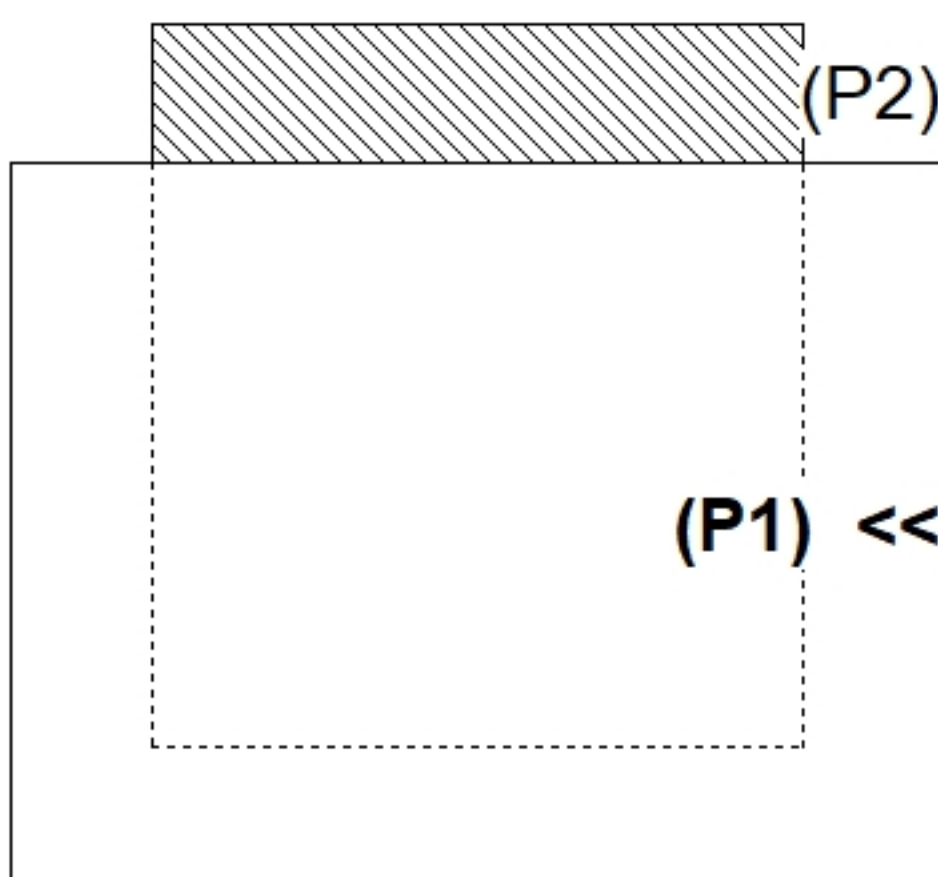
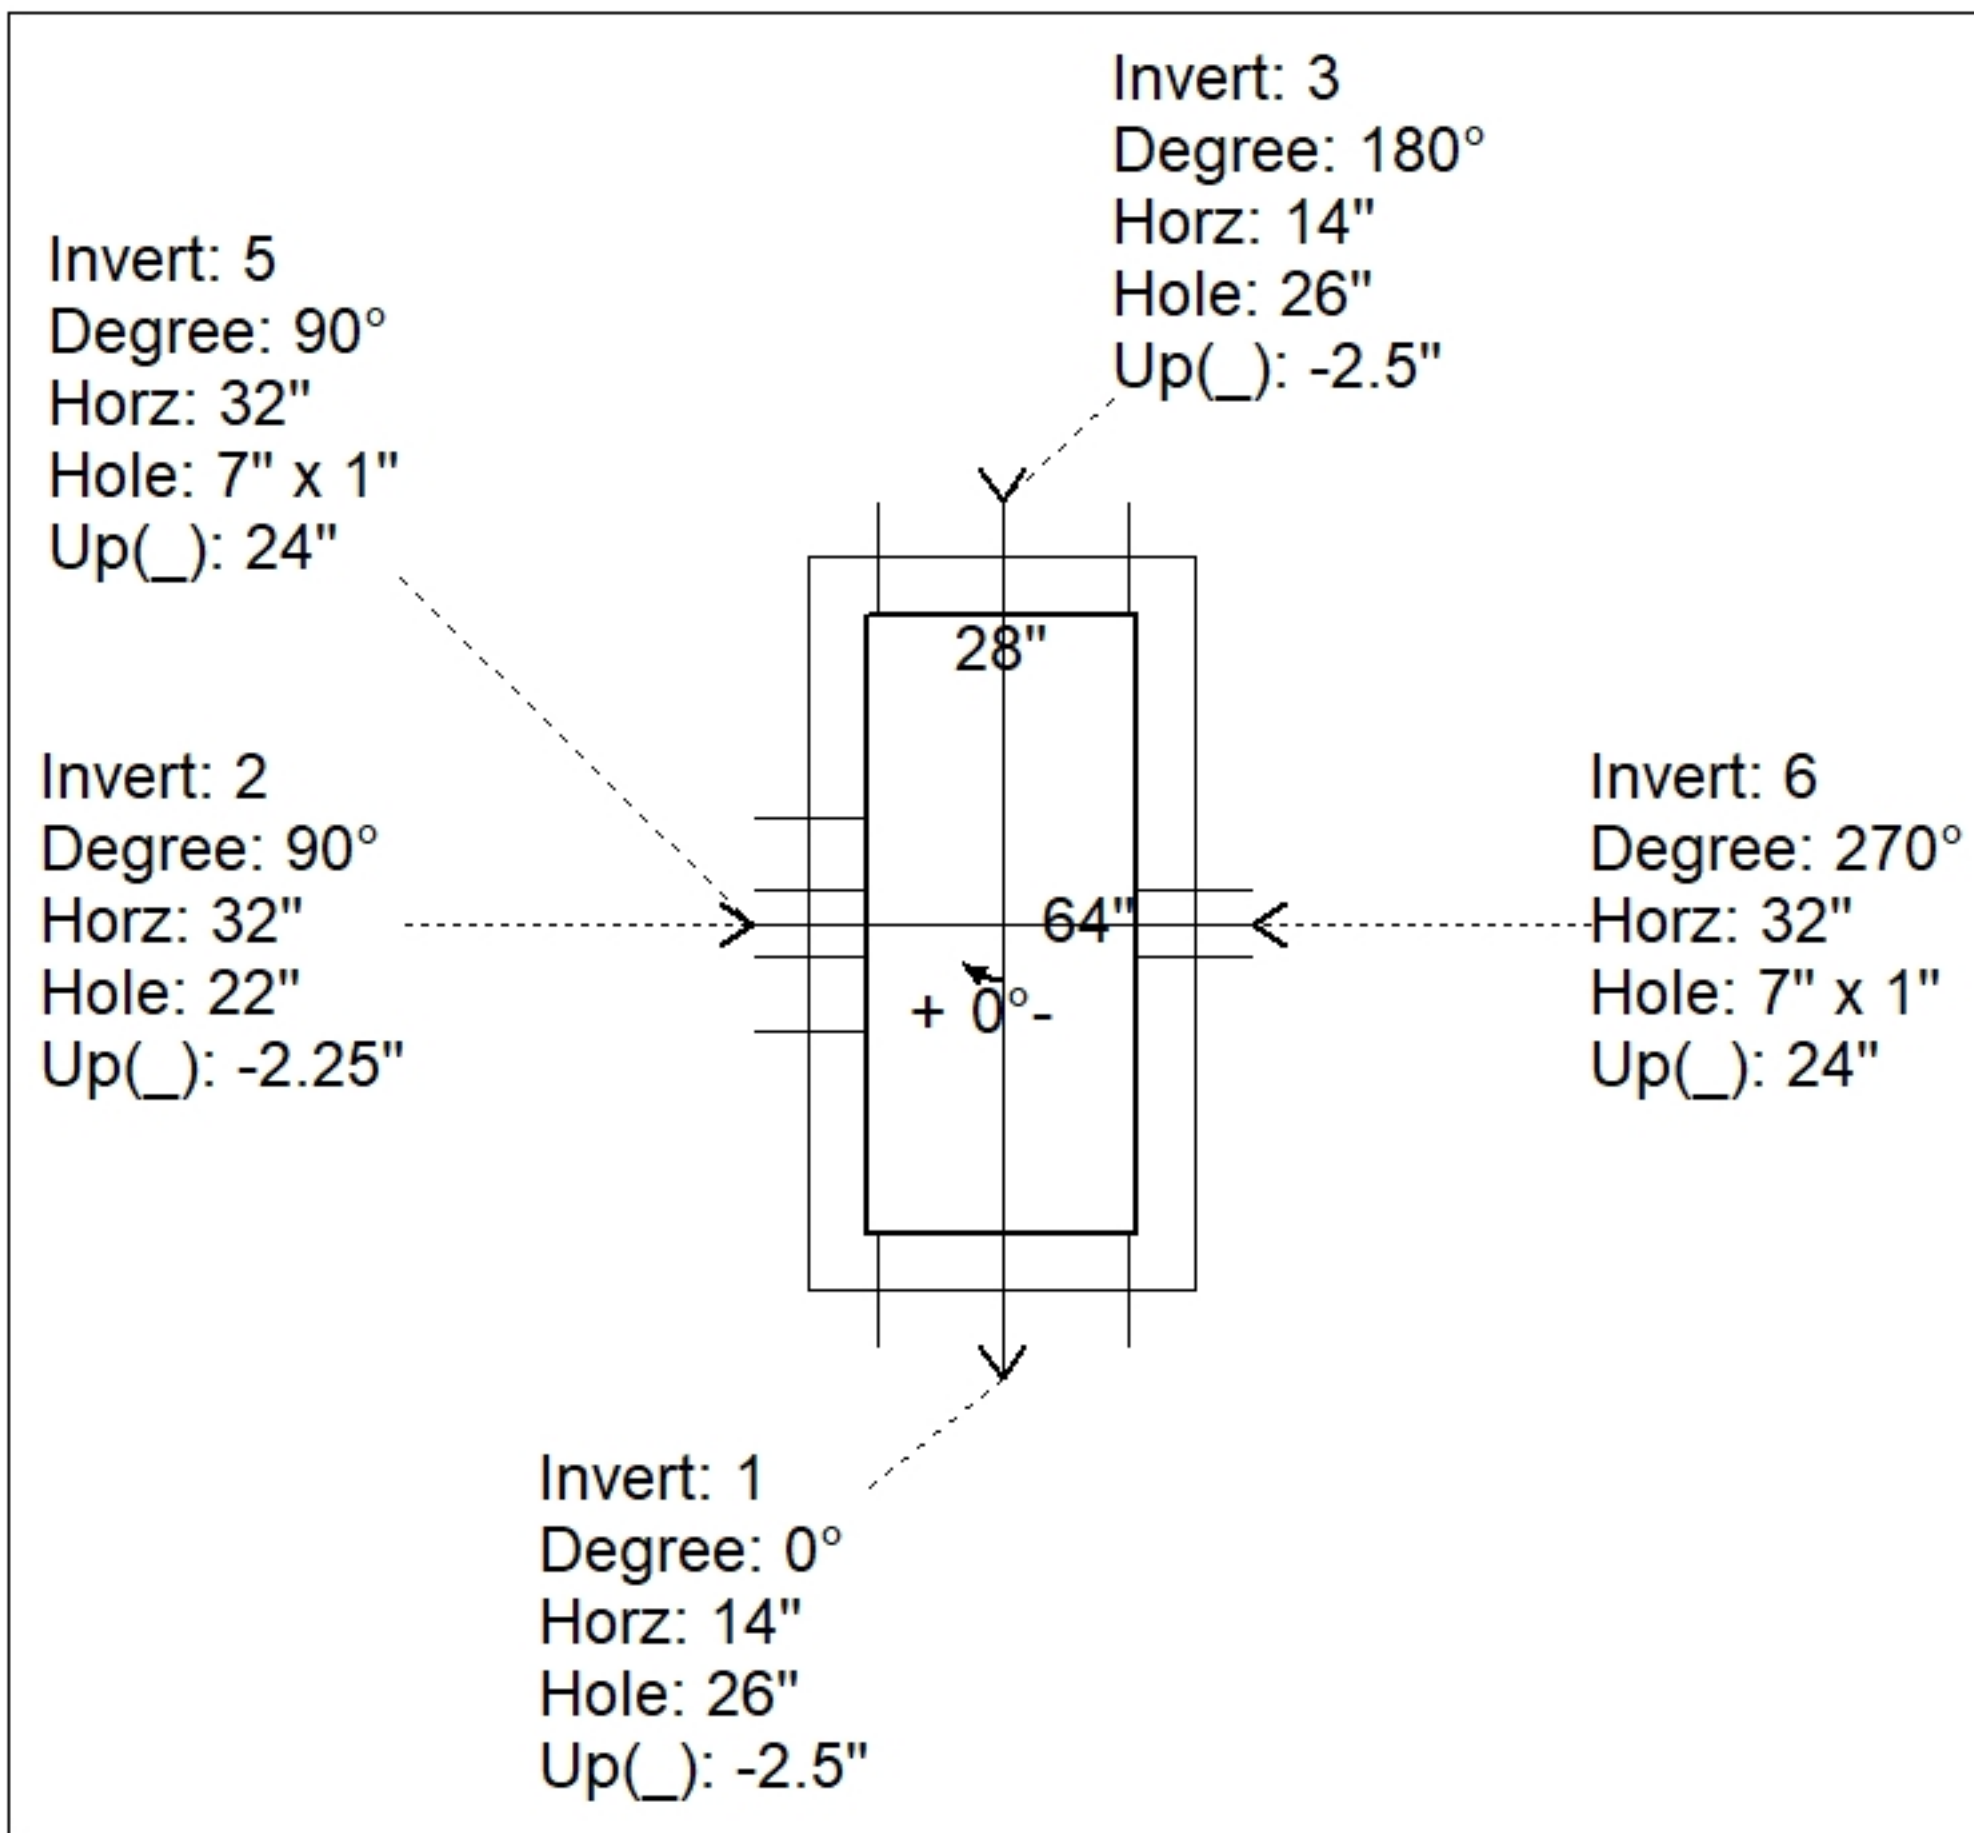
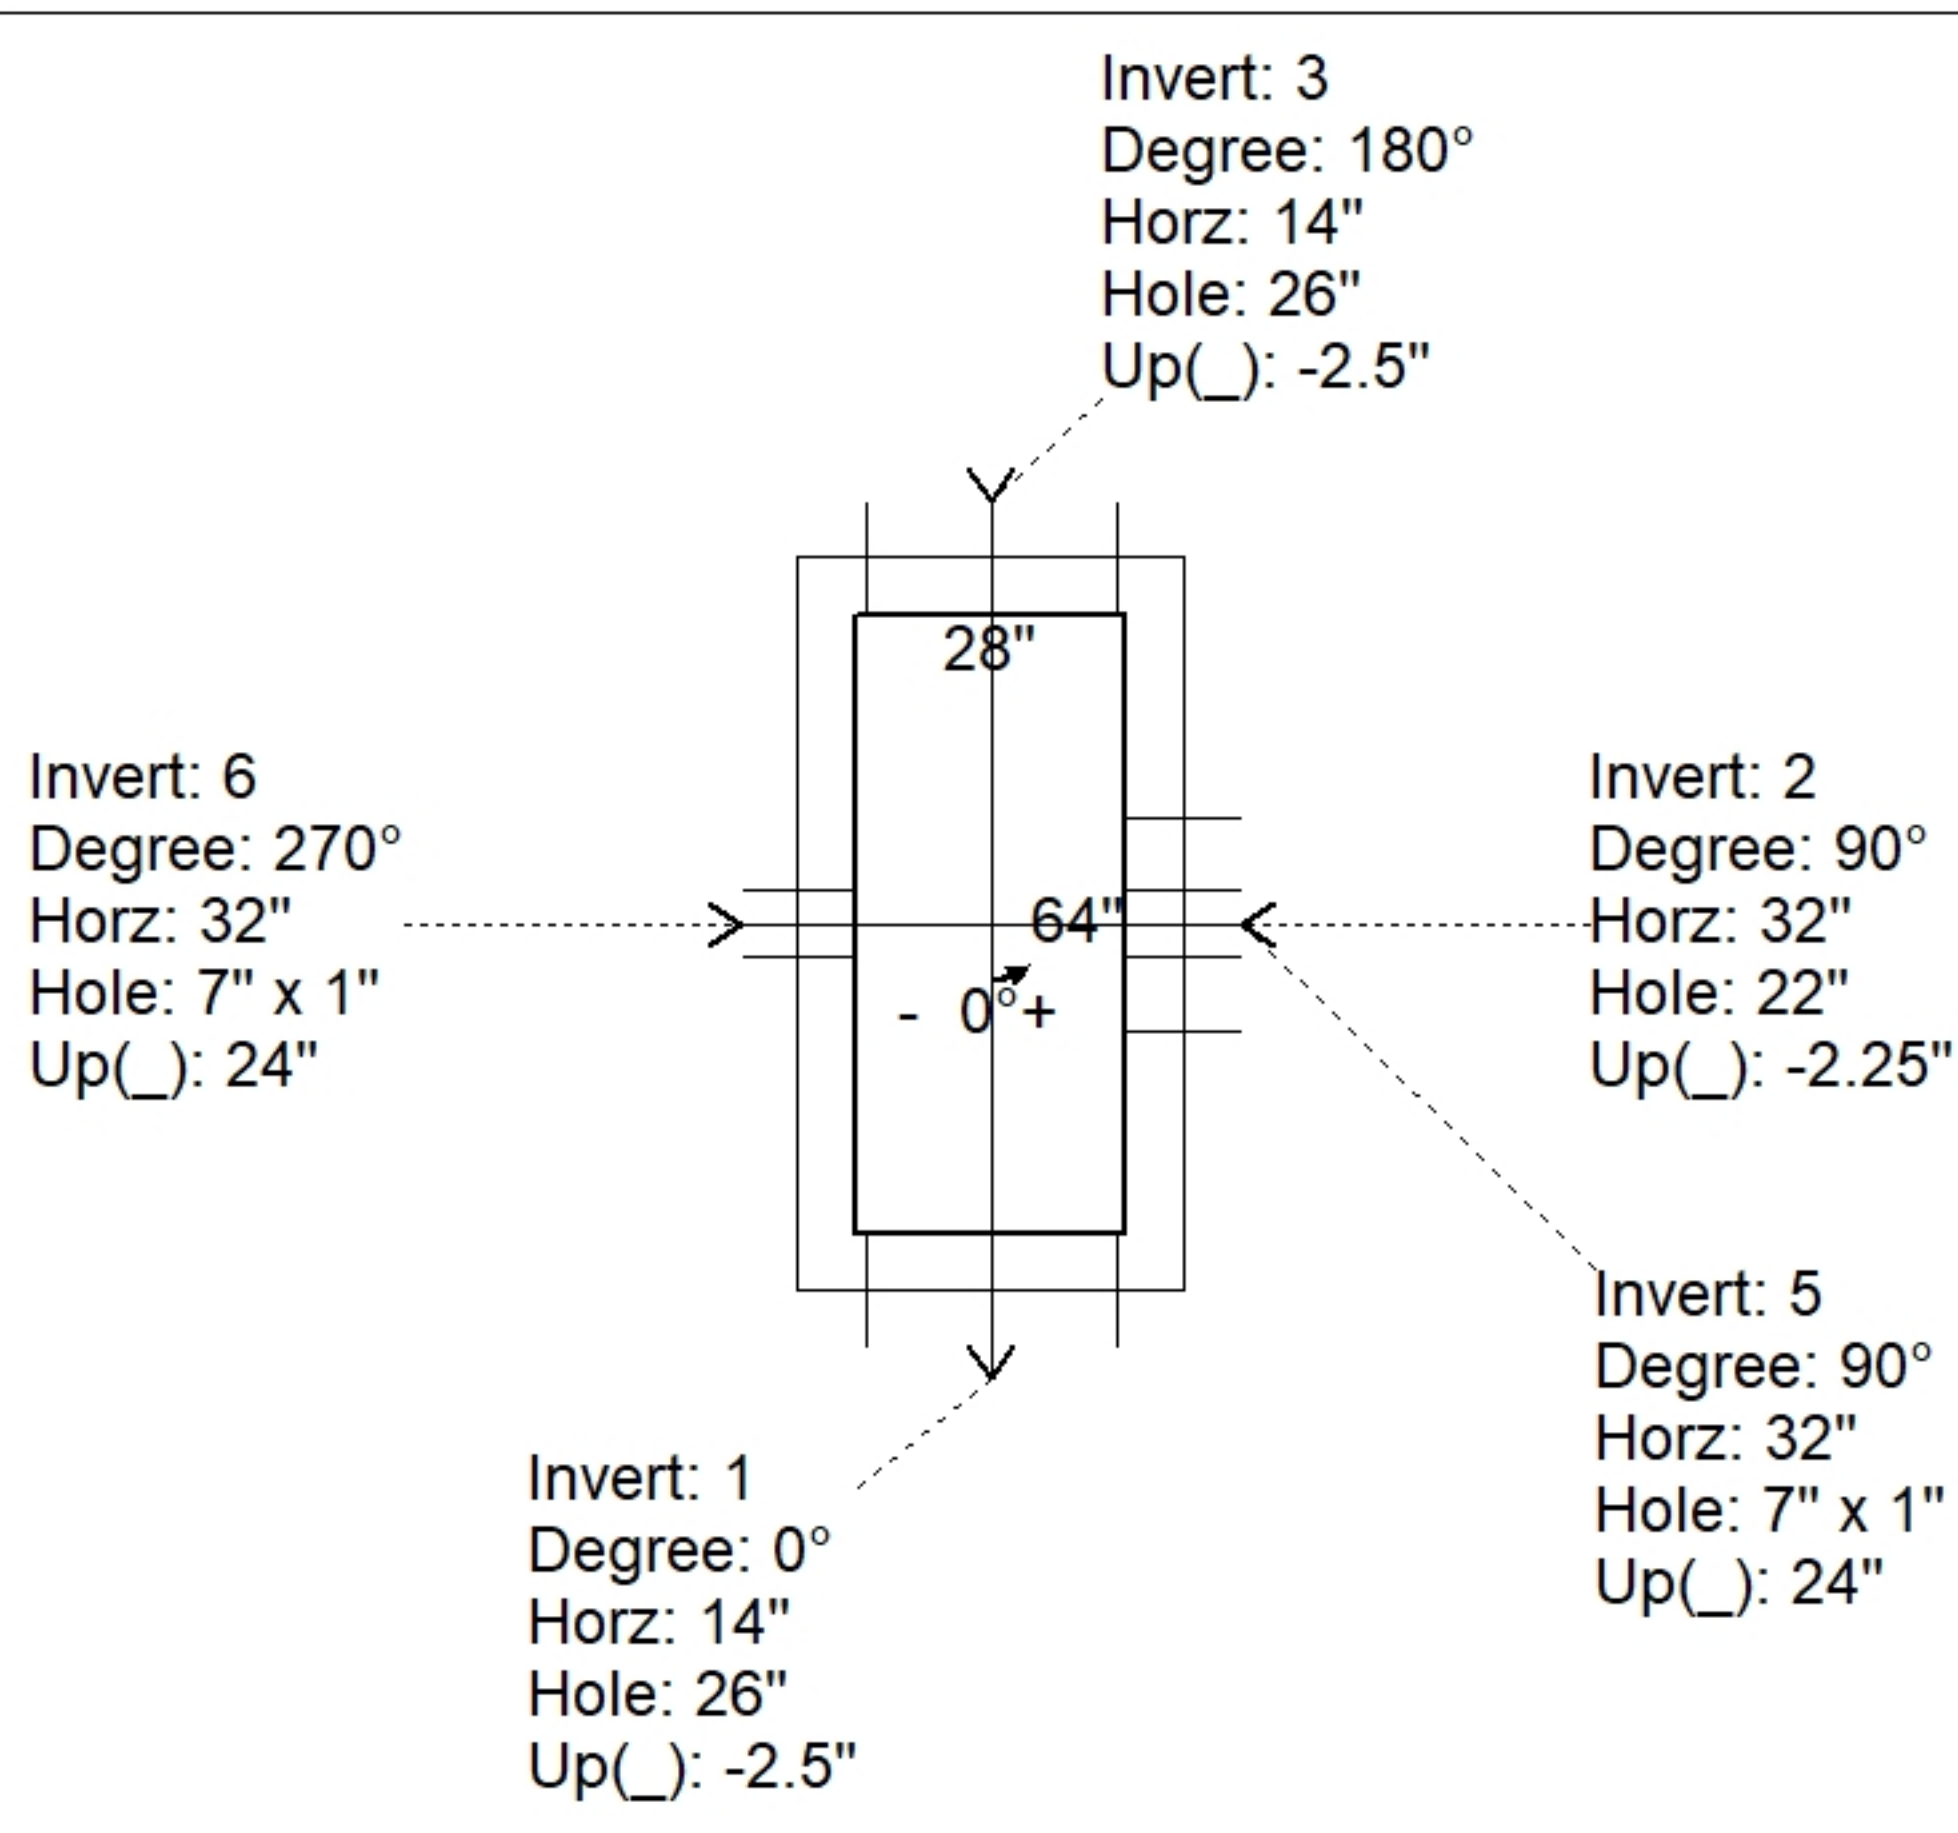
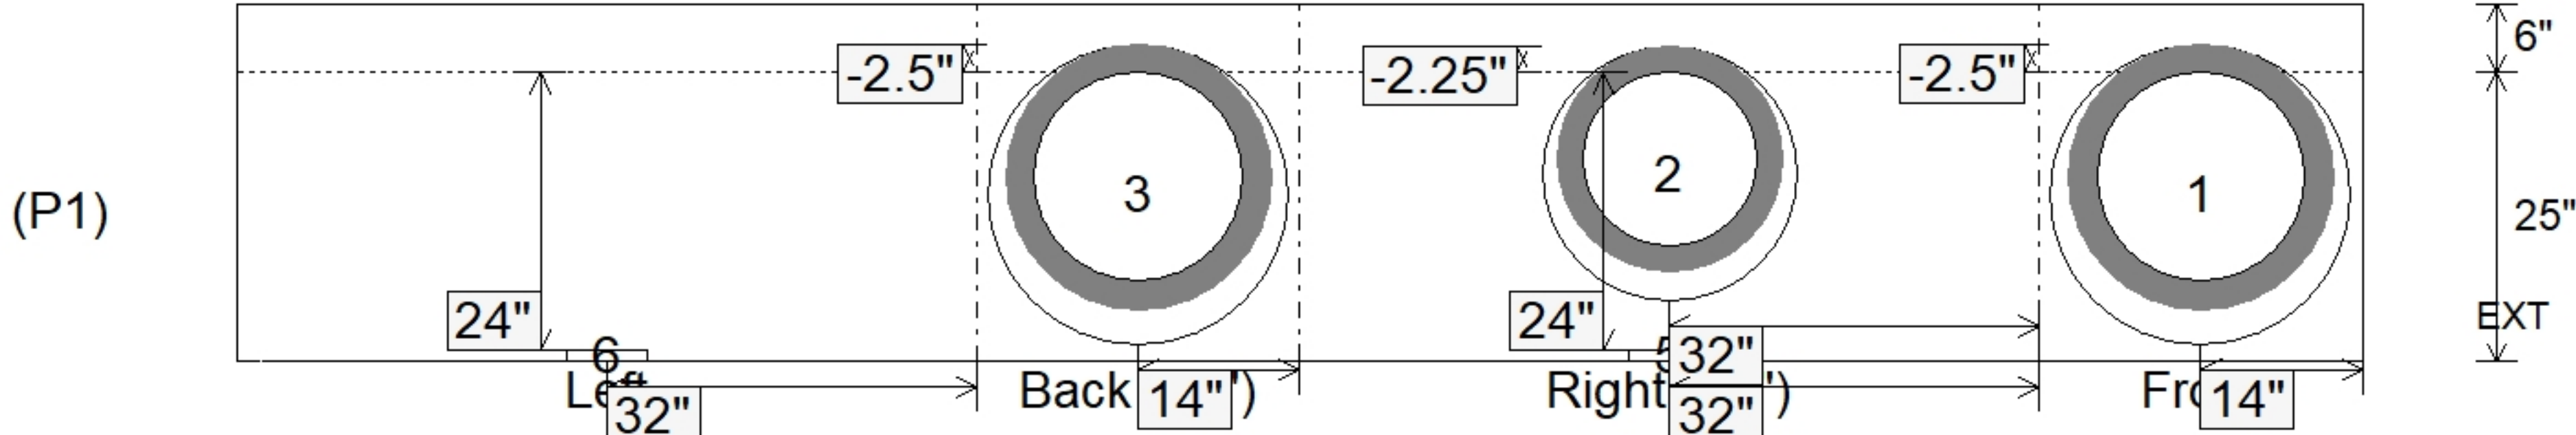


Job Name: 24-3511 Coles Ferry Section 18 & 19 Job Location: Lebanon, TN Contractor: Covenant Constructors, LLC					Plant: Beaver Dam, KY 6/18/2026 10:58:14 AM		Tech: J. Horsley PC: A. Chambers				
Structure ID: CB6											
P1		BX28640606-VH			BOX BASE 6inW, 6inF, Variable Ht F/n						
P2) 28" x 64" - CASTING HEIGHT - 6" P1) 28" x 64" - BOX BASE 6inW, 6inF, Variable Ht F/n - 25" 1) CASTING - JBS 3101 Double Set (F/G/H) 1) 28" x 64" - Conseal CS-102 1.00" 2) Hole - 26 1) Hole - 22 2) LINTEL BAR SLOT n/n - 7"x1"					0 lb 3416 lb 1238 lb 0 lb 0 lb 0 lb 0 lb 0 lb Structure Total: 4654 lb		Structure Notes: . 1. PER ASTM C913 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. NO INVERT CHANNEL. . REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W. - WALLS (As .12) #5 BARS AT 12" C.C.E.W. - FLOOR (As .12) #5 BARS AT 12" C.C.E.W.				
Rim: 571.82'		Rim to Invert: 2.6'		Slack: 0.2"		Sump: 0"		Step Position:			
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	569.22'	0°	20"	18" RCP B WALL	23"	Hole 26	26"	26"	-2.5"	0"	
Invert 2	569.22'	90°	38"	15" RCP B WALL	19.5"	Hole 22	22"	22"	-2.25"	0"	
Invert 3	569.22'	180°	20"	18" RCP B WALL	23"	Hole 26	26"	26"	-2.5"	0"	
Invert 4											
Invert 5	571.22'	90°	38"	7" x 1" LINTEL BAR SLOT	7" x 1"	LINTEL BAR SLOT 7"x1"	7" x 1"	7"	24"	0"	
Invert 6	571.22'	270°	38"	7" x 1" LINTEL BAR SLOT	7" x 1"	LINTEL BAR SLOT 7"x1"	7" x 1"	7"	24"	0"	
Invert 7											
Invert 8											
 RIGHT-SIDE UP VIEW (int. dimensions)  UPSIDE-DOWN VIEW (int. dimenions)  INSIDE WALL DIMENSIONS 											
Coating (Int): Coating (Ext):				Seam Up: Flat Seam Dn: n/a		Wall Thickness: 6" Floor Height: 6"		Height (Int): 25" Height (Ext): 31"		Weight (Net): 3416 lb Volume (Net): 0.87cu.yd	
