



Job Name: 25-2952 - KYTC Jefferson Co Call 106 (251315) Job Location: Indiana, KY Contractor: Louisville Paving and Construction					Plant: 100 6/12/2026 3:09:37 PM		Tech: J. Horsley - A PC: J. Jarvis				
Structure ID: 13											
P1 MH048BAVF		MH BASE Custom Ht T/n									
P3) 24" - CASTING HEIGHT - 4" P2) 48" - MH FLAT LID w/24in ECC Hole F/G - 12" P1) 48" - MH BASE Custom Ht T/n - 39" 1) 48" - Conseal CS-102 1.00" 1) 24" - Conseal CS-102 1.00" 2) Hole - 32 1) Hole - 18 3) MH Step ML-10-TDS-NCR - 10"						0 lb 1561 lb 3219 lb 0 lb 0 lb 0 lb 0 lb 0 lb 0 lb		Structure Notes: ** KYTC STATE PROJECT ** 1. PER KYTC MANHOLE TYPE A / ASTM C-478 SPECS 2. CONCRETE: 4,000 PSI AT 28 DAYS 3. REINFORCEMENT: PER ASTM A615 4. NO STORM INVERT 5. STEPS AT 270 DEGREES 6. HOE KY-206 FRAME & COVER "STORM" SUPPLIED BY OTHERS			
Rim: 563.82' Rim to Invert: 4.25' Slack: 0" Sump: 4" Step Position: 270°						Structure Total: 4780 lb					
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	559.57'	0°	0"	24" HDPE	27.8"	Hole 32	32"	35.027"	0"	0"	
Invert 2	559.57'	90°	45.5"	12" HDPE	14.5"	Hole 18	18"	18.451"	1"	0"	
Invert 3	559.57'	180°	91.125"	24" HDPE	27.8"	Hole 32	32"	35.027"	0"	0"	
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											


RIGHT-SIDE UP VIEW (int. dimensions)

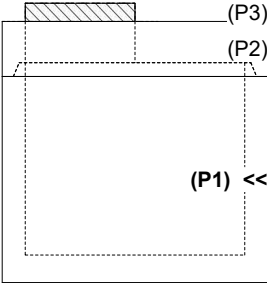

UPSIDE-DOWN VIEW (int. dimensions)

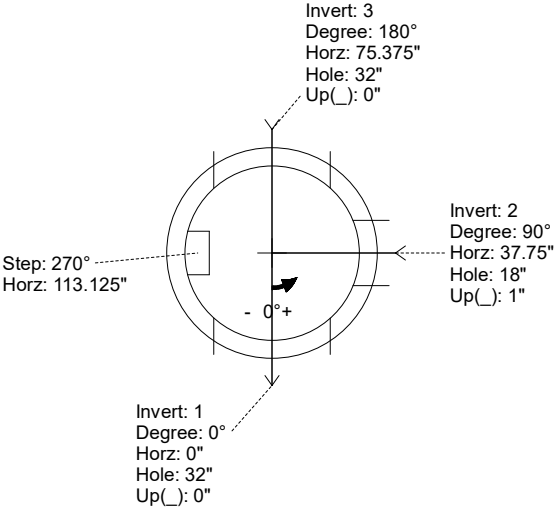

INSIDE WALL DIMENSIONS

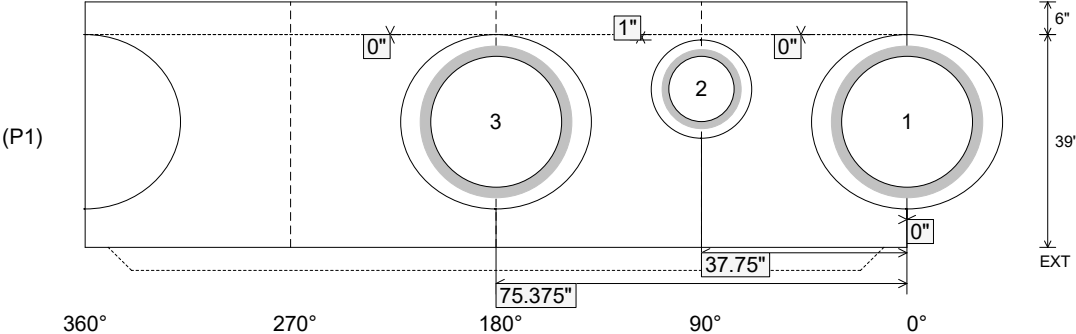

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 39" Height (Ext): 45"	Weight (Net): 3219 lb Volume (Net): 0.82cu.yd
----------------------------------	---------------------------------	--	--	--
