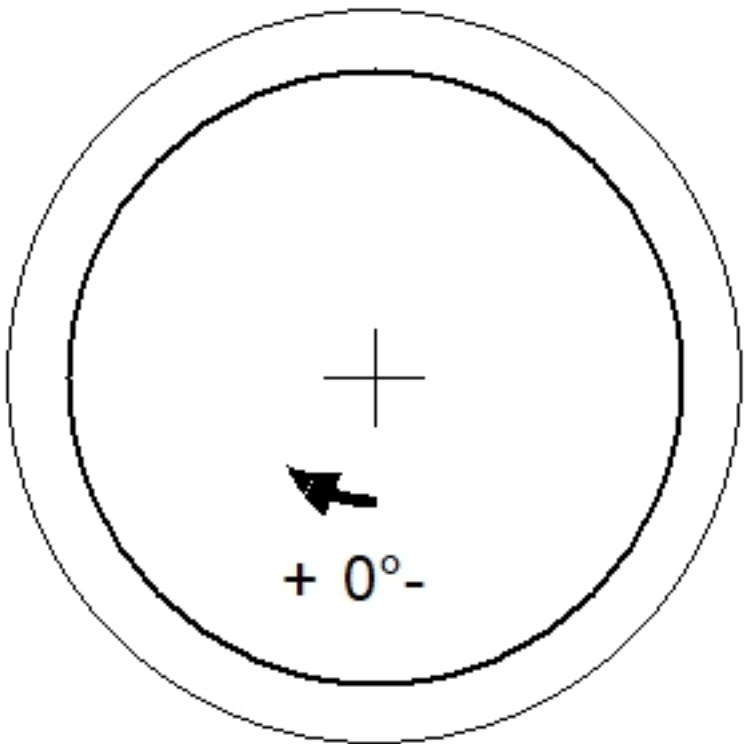
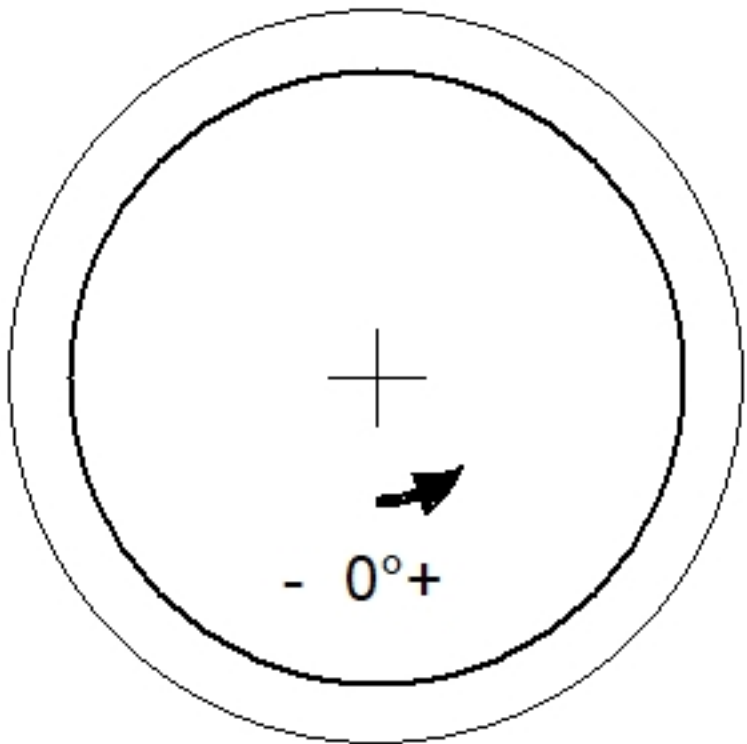
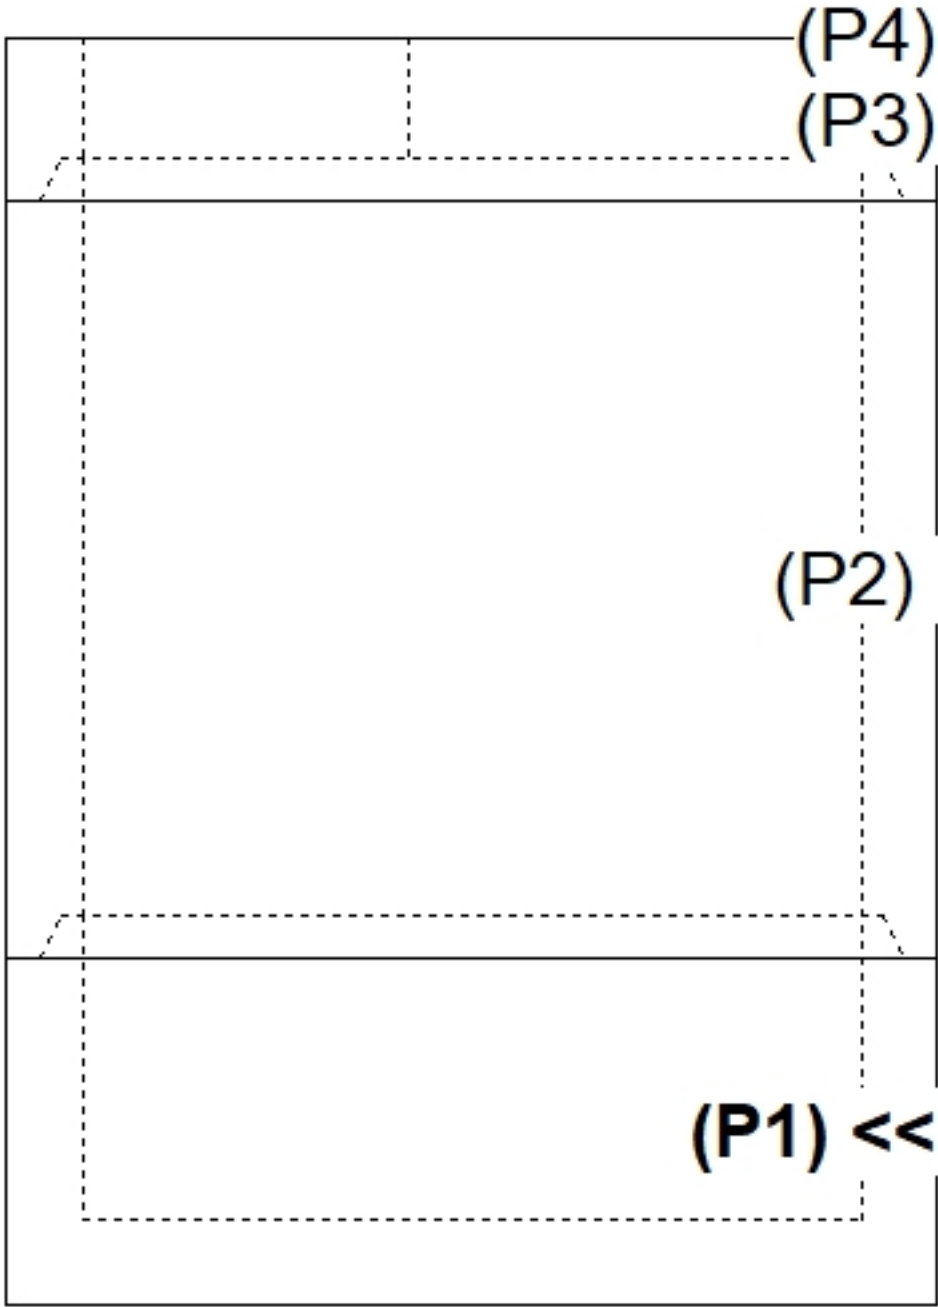
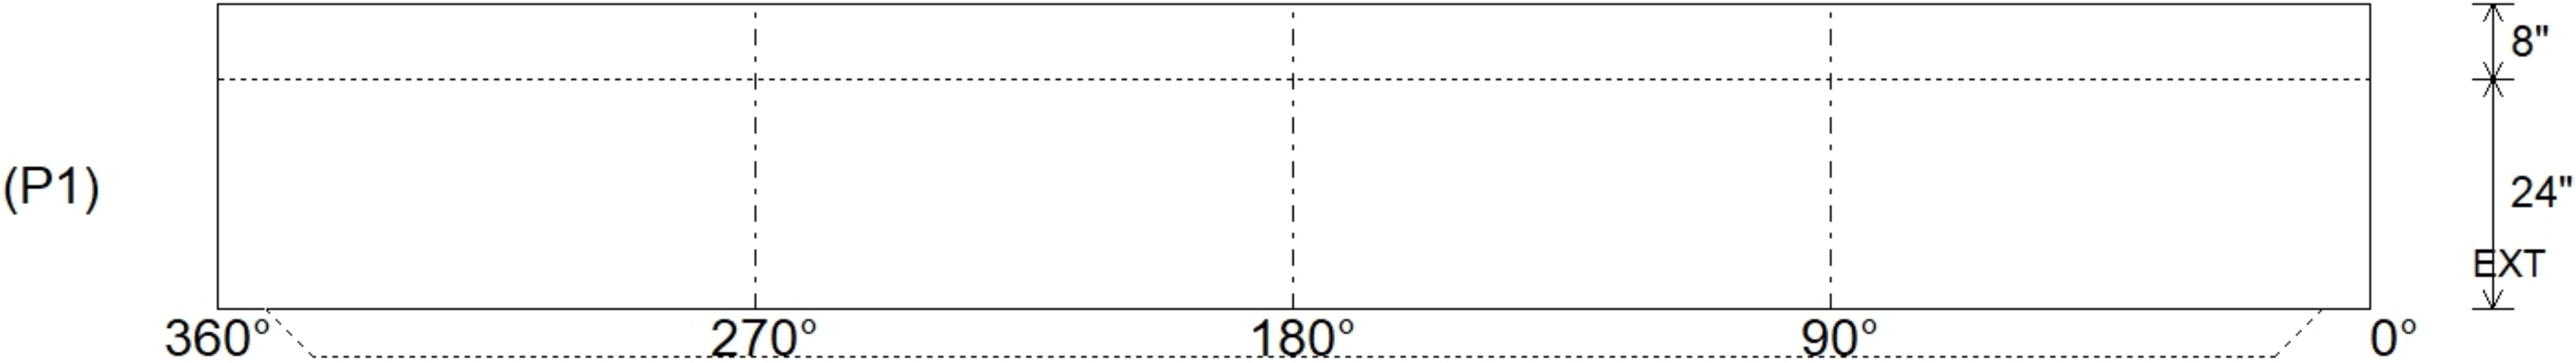


Job Name: 26-2800 901652 13635 Telegraph Road Job Location: CPU Contractor: Contech Engineering Solutions					Plant: Beaver Dam 6/24/2026 10:19:02 AM		Tech: S. Felletter PC: C. Goff				
Structure ID: 15-CS-6											
P1		MH072BA24			MH BASE T/n						
P4) 30" - CASTING HEIGHT - 0" P3) 72" - MH FLAT TOP w/ 30" CASTING CAST IN F/G - 15" P2) 72" - MH RISER Custom Ht T/G - 70" P1) 72" - MH BASE T/n - 24" 1) ASSEMBLY REQUIRED 1) CVSTENCILING 2) 72" - Conseal CS-102 1.00" 2) Hole - 16						0 lb 4663 lb 9967 lb 7398 lb 0 lb 0 lb 0 lb 0 lb ----- 22028 lb		Structure Notes: 4" CASTING BY OTHERS . LIFTING ANCHORS TO BE INSTALLED ON THE OUTSIDE OF THE STRUCTURE . ICAST TO INSTALL THE INTERNALS . CONTECH'S LOGO AS WELL AS THE INLET AND OUTLET MUST BE STENCILED ONTO THE STRUCTURE			
Rim: 611.88' Rim to Invert: 3.33' Slack: -0.004" Sump: 69.036" Step Position:											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1											
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											
RIGHT-SIDE UP VIEW (int. dimensions)  UPSIDE-DOWN VIEW (int. dimenions) 											
 INSIDE WALL DIMENSIONS 											
Coating (Int): Coating (Ext):				Seam Up: Tongue Seam Dn: n/a		Wall Thickness: 7" Floor Height: 8"		Height (Int): 24" Height (Ext): 32"		Weight (Net): 7398 lb Volume (Net): 1.89cu.yd	
