




Job Name: 25-4547 - WWTP Improvements & Hydraulic Expansion Job Location: Shepherdsville, KY Contractor: Pace Contracting, LLC					Plant: 100 6/4/2026 1:36:33 PM		Tech: Jared - F PC: J Jarvis				
Structure ID: MH-4											
P2		MH060RS54		MH RISER T/G							
P5) 24" - CASTING HEIGHT - 7" P4) 48" - ECC CONE w/ 24" HOLE F/G - 42" P3) 60" - MH Transition Slab 48" Hole T/G - 13" P2) 60" - MH RISER T/G - 54" P1) 60" - MH BASE T/h - 24" 1) Chimney Seal - Cretex Chimney Seal 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) 60" - MH INVERT CHANNEL - FULL HEIGHT 1) CASTING - HOE MC-375-WT F/C Sanitary 2) 60" - Conseal CS-102 1.00" (Double) 1) 48" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 2) PSX - 16Y NYLO 11) MH Step ML-10-TDS-NCR - 10"					0 lb 3200 lb 1928 lb 5637 lb 5034 lb 10 lb 0 lb 0 lb 2692 lb 271 lb 0 lb 0 lb 0 lb 0 lb 16 lb 0 lb		Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING SUPPLIED BY I-CAST (HOE MC-375-WT F/C SANITARY). 4. 8.5" EXTERNAL CHIMNEY SEAL BY I-CAST. REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - TRANS. SLAB (As .31) #5 BARS AT 6" C.C.E.W. - RISER/WALLS (As .18) - FLOOR (As .37) #5 BARS AT 10" C.C.E.W.				
Rim: 449'		Rim to Invert: 11.45'		Slack: 0.4"		Sump: 3"		Structure Total: 18788 lb		Step Position: 90°	
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1											
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											

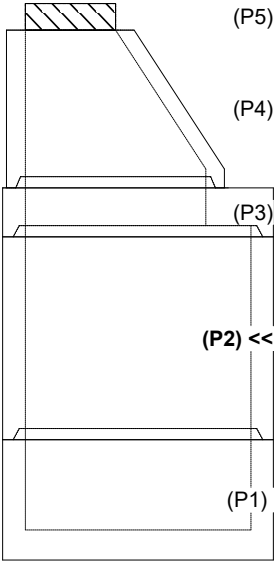

RIGHT-SIDE UP VIEW (int. dimensions)



INSIDE WALL DIMENSIONS

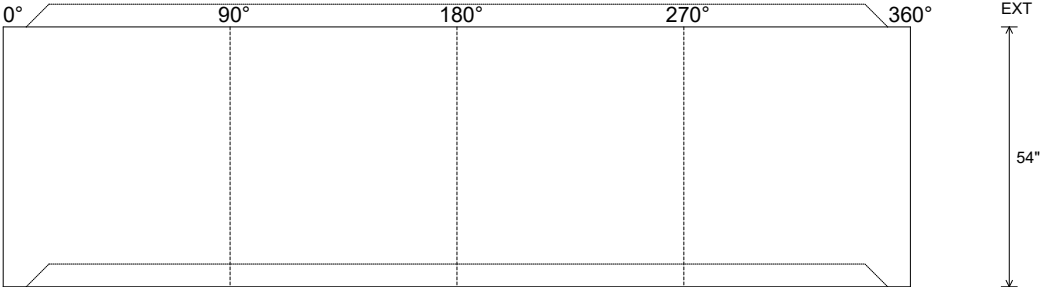

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: Groove	Wall Thickness: 6" Floor Height: 0"	Height (Int): 54" Height (Ext): 54"	Weight (Net): 5637 lb Volume (Net): 1.44cu.yd
----------------------------------	------------------------------------	--	--	--
