

Job Name: 26-2800 901652 13635 Telegraph Road
Job Location: CPU
Contractor: Contech Engineering Solutions

Plant: Beaver Dam

6/24/2026 10:19:45 AM

Tech: S. Felletter

PC: C. Goff



Structure ID: 15-CS-6

P3 MH072LD15SP

MH FLAT TOP w/ 30" CASTING CAST IN F/G


- P4) 30" - CASTING HEIGHT - 0"
P3) 72" - MH FLAT TOP w/ 30" CASTING CAST IN F/G - 15"
P2) 72" - MH RISER Custom Ht T/G - 70"
P1) 72" - MH BASE T/n - 24"
1) ASSEMBLY REQUIRED
1) CVSTENCILING
2) 72" - Conseal CS-102 1.00"
2) Hole - 16

0 lb
4663 lb
9967 lb
7398 lb
0 lb
0 lb
0 lb
0 lb

22028 lb


Structure Notes:
4" CASTING BY OTHERS
LIFTING ANCHORS TO BE INSTALLED
ON THE OUTSIDE OF THE STRUCTURE
ICAST TO INSTALL THE INTERNALS
CONTECH'S LOGO AS WELL AS THE
INLET AND OUTLET MUST BE
STENCILED ONTO THE STRUCTURE

Structure Total:

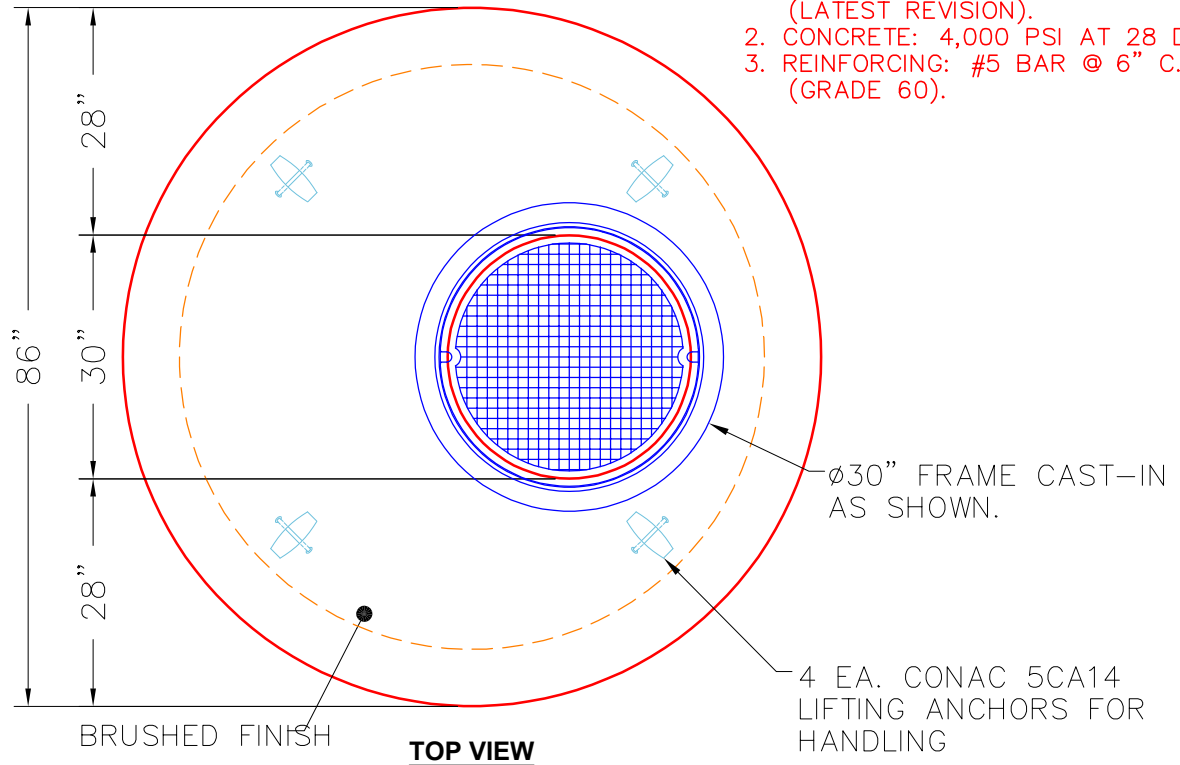

NOTES:

1. MANUFACTURED TO ASTM C-478 (LATEST REVISION).
2. CONCRETE: 4,000 PSI AT 28 DAYS.
3. REINFORCING: #5 BAR @ 6" C.C. E.W. (GRADE 60).

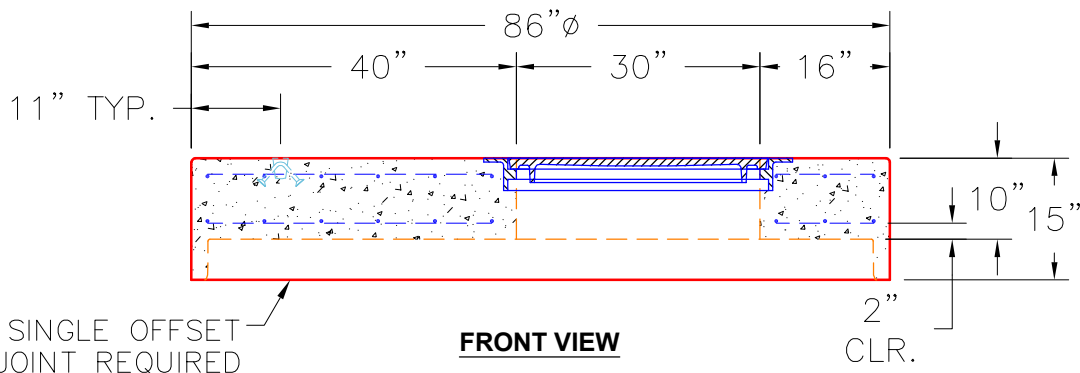

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Groove

Wall Thickness: 7"

Height (Ext): 15"

Weight (Net): 4663 lb
Volume (Net): 1.19cu.yd
