

Job Name: 25-2952 - KYTC Jefferson Co Call 106 (251315)
Job Location: Indiana, KY
Contractor: Louisville Paving and Construction

Plant: 100

6/12/2026 3:12:24 PM

Tech: J. Horsley - A

PC: J. Jarvis



Structure ID: 56

P3 BX024030-08LD08-15X27

CB FLAT TOP 8"W w/15"x27" HOLE F/F



P4) 15" x 27" - P.I.P. - BY OTHERS - 8"
P3) 24" x 30" - CB FLAT TOP 8"W w/15"x27" HOLE F/F - 8"
P2) 24" x 30" - BOX RISER 8inW F/G - 24"
P1) 24" x 30" - BOX BASE 8inW, 8inF, Variable Ht T/n - 26"
2) 24" x 30" - Conseal CS-102 1.00"
1) 15" x 27" - Conseal CS-102 1.00"
2) Hole - 24
1) Hole - 18
2) Hole - 4

Structure Total: 6254 lb

Structure Notes:

** KYTC STATE PROJECT **

1. PER KYTC DBI TYPE 13G / ASTM C-913 SPECS
2. CONCRETE: 4,000 PSI AT 28 DAYS
3. REINFORCEMENT: DOUBLE MAT #5 BAR @ 6" C.C.
E.W. (GRADE 60) - 2" MIN. REBAR CLEARANCE (TYP)
4. HOE KY-230G FRAME & GRATE SUPPLIED BY
OTHERS - POURED IN PLACE BY OTHERS
5. WET STICK #5 BAR @ 12" C.C. (GRADE 60) 6" OUT TOP
OF FLAT LID AROUND 15" X 27" OPENING FOR FIELD
POUR TIE-IN - 4" MIN. PENETRATION INTO FLAT LID
6. LIFTERS: 4 EA. WRA016 CONAC WIRE ROPE
ANCHORS FOR PLANT & FIELD HANDLING
7. TOP SURFACE TO RECEIVE FLOATED FINISH

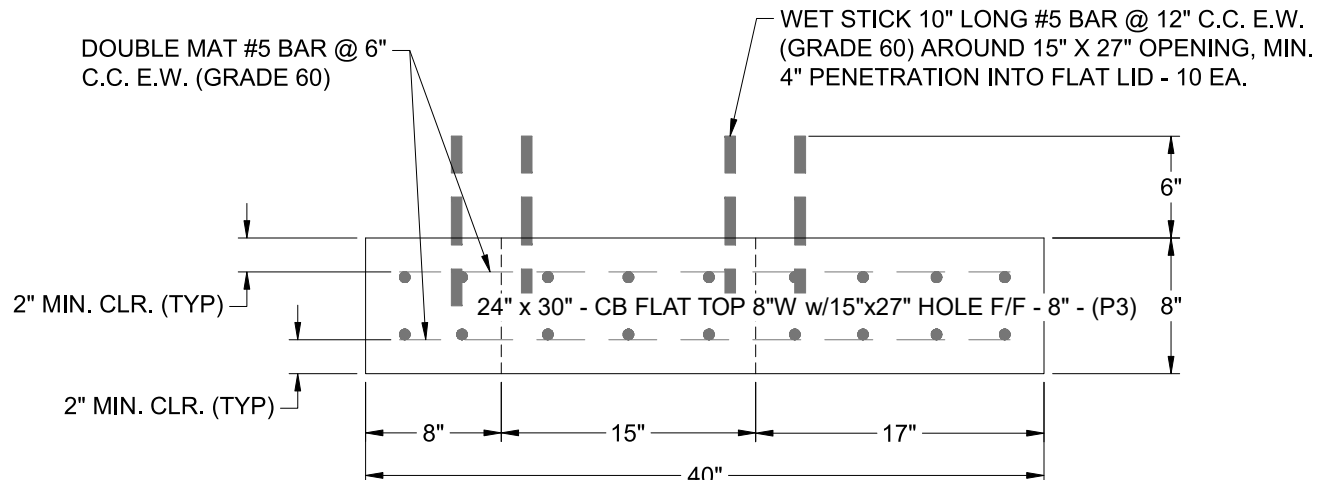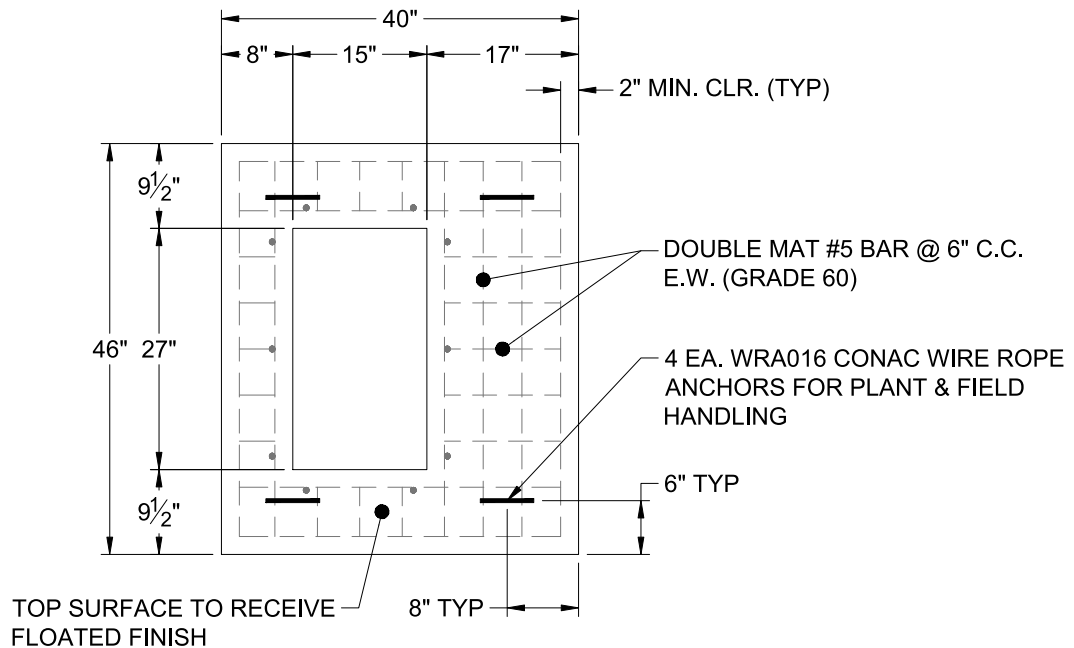

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Flat

Wall Thickness: 8"

Height (Ext): 8"

Weight (Net): 963 lb
Volume (Net): 0.25cu.yd
