

Job Name: 25-2952 - KYTC Jefferson Co Call 106 (251315)  
 Job Location: Indiana, KY  
 Contractor: Louisville Paving and Construction

Plant: 100

5/12/2026 1:01:36 PM

Tech: J. Horsley - A

PC: J. Jarvis



**Structure ID: 80**

**P2 BX024030-08LD08-15X27**

**CB FLAT TOP 8"W w/15"x27" HOLE F/F**



- P3) 15" x 27" - P.I.P. - BY OTHERS - 8"
- P2) 24" x 30" - CB FLAT TOP 8"W w/15"x27" HOLE F/F - 8"
- P1) 24" x 30" - BOX BASE 8inW, 8inF, Variable Ht F/n - 38"
- 1) 24" x 30" - Conseal CS-102 1.00"
- 1) 15" x 27" - Conseal CS-102 1.00"
- 1) Hole - 20
- 2) Hole - 4

0 lb  
 963 lb  
 4579 lb  
 0 lb  
 0 lb  
 0 lb  
 0 lb  
 -----  
 5542 lb

Structure Total: 5542 lb

Structure Notes:

- \*\*KYTC STATE PROJECT\*\*
- 1. PER KYTC DBI TYPE 13G / ASTM C-913 SPECS
- 2. CONCRETE: 4,000 PSI AT 28 DAYS
- 3. REINFORCEMENT: DOUBLE MAT #5 BAR @ 6" C.C. E.W. (GRADE 60) - 2" MIN. REBAR CLEARANCE (TYP)
- 4. HOE KY-230G FRAME & GRATE SUPPLIED BY OTHERS
- 5. STUB #5 BAR SPACED @ 12" C.C. (GRADE 60) 6" OUT TOP OF FLAT LID AROUND 15" X 27" OPENING FOR FIELD POUR TIE-IN
- 6. LIFTERS: 4 EA. WRA016 CONAC WIRE ROPE ANCHORS FOR PLANT & FIELD HANDLING
- 7. TOP SURFACE TO RECEIVE FLOATED FINISH

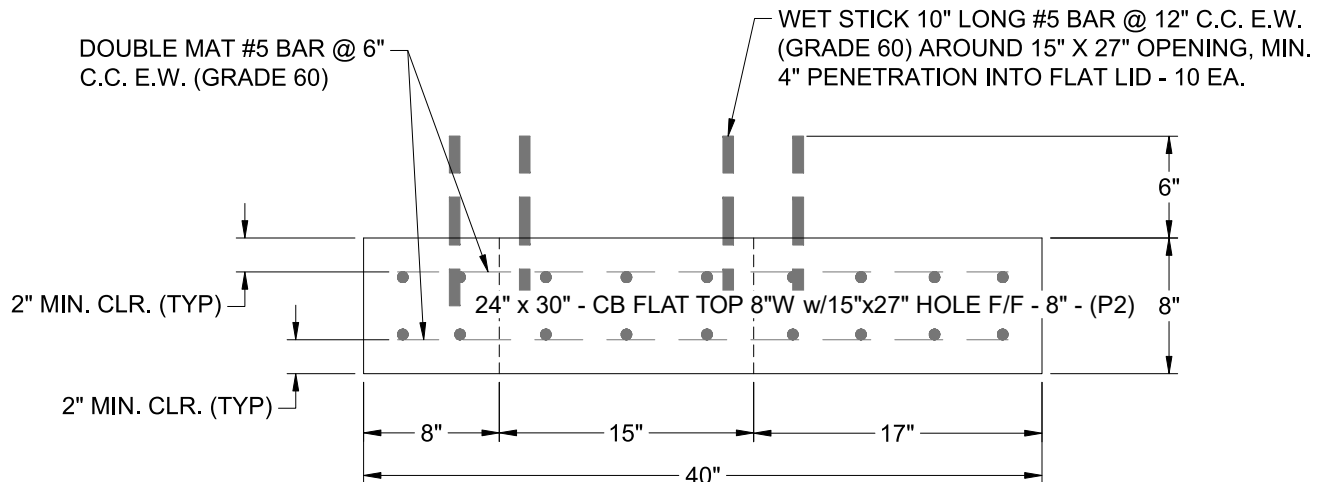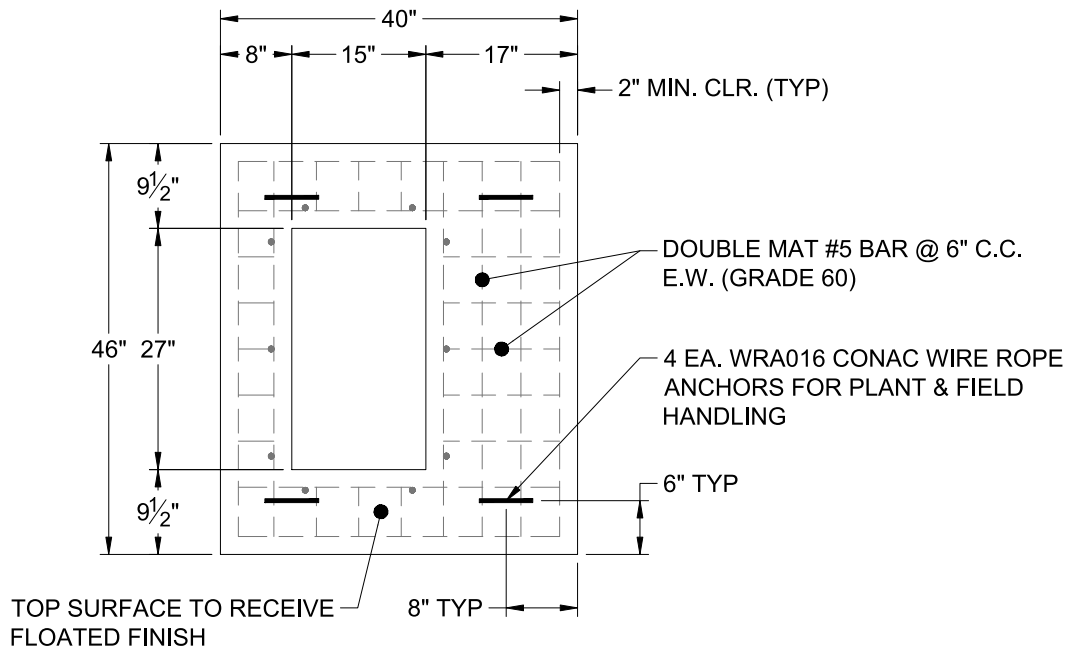

Coating (Int):  
 Coating (Ext):

Seam Up: Flat  
 Seam Dn: Flat

Wall Thickness: 8"

Height (Ext): 8"

Weight (Net): 963 lb  
 Volume (Net): 0.25cu.yd
