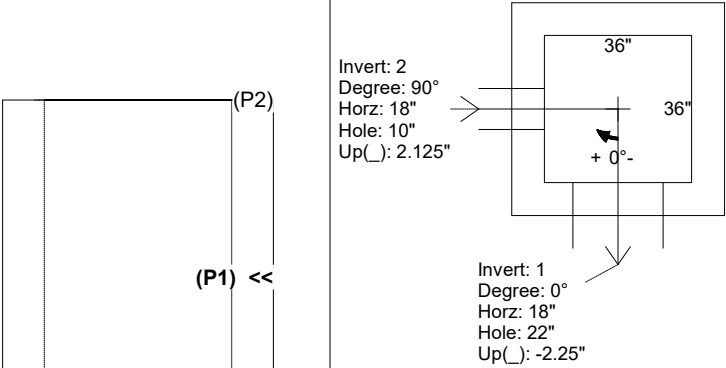
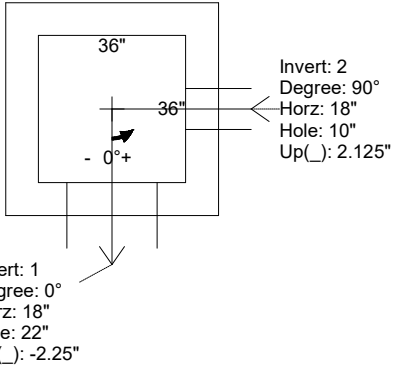
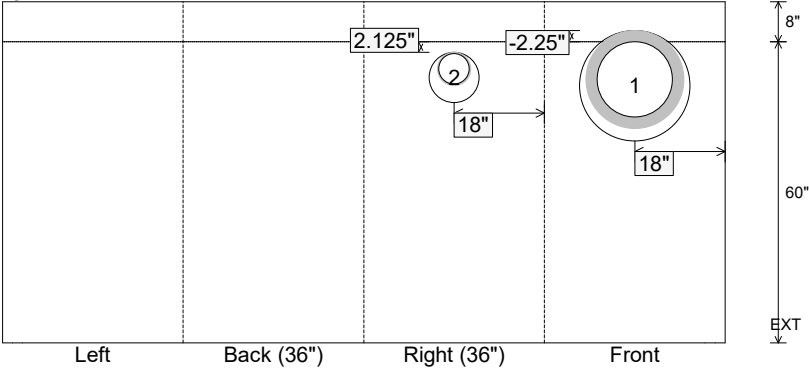


Job Name: 26-1185 - Wells Fargo Smyrna Job Location: Smyrna, TN 37167 Contractor: Hayes Pipe Supply					Plant: 100 7/21/2026 3:56:01 PM		Tech: Jared - F PC: E. Bradley					
Structure ID: A13-7 ST-OCS												
P1		BX3636-08BA60		BOX BASE 8inW, 8inF F/n								
P2) 36" x 36" - CASTING HEIGHT - 0" P1) 36" x 36" - BOX BASE 8inW, 8inF F/n - 60" 1) 36" x 36" - Conseal CS-102 1.00" 1) Hole - 22" 1) Hole - 10"					0 lb 8596 lb 0 lb 0 lb 0 lb ----- Structure Total: 8596 lb		Structure Notes: 1. PER ASTM C913 SPECIFICATIONS. 2. CONCRETE = 4,500 PSI AT 28 DAYS. 3. NO STEPS AND NO INVERT CHANNEL. 4. CASTING SUPPLIED BY OTHERS. REINFORCING PER ASTM A615 (GRADE 60). - WALLS (As .12) #5 BARS AT 12" C.C.E.W. - FLOOR (As .12) #5 BARS AT 12" C.C.E.W.					
Rim: 588.15'					Rim to Invert: 5.05'		Slack: 0.598"		Sump: 0"		Step Position:	
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset		
Invert 1	583.1'	0°	26"	15" RCP B WALL	19.5"	Hole 22	22"	22"	-2.25"	0"		
Invert 2	583.3'	90°	26"	6" PVC SCH40	6.625"	Hole 10	10"	10"	2.125"	0"		
Invert 3												
Invert 4												
Invert 5												
Invert 6												
Invert 7												
Invert 8												
RIGHT-SIDE UP VIEW (int. dimensions)  UPSIDE-DOWN VIEW (int. dimensions)  INSIDE WALL DIMENSIONS 												
Coating (Int): Coating (Ext):			Seam Up: Flat Seam Dn: n/a		Wall Thickness: 8" Floor Height: 8"		Height (Int): 60" Height (Ext): 68"		Weight (Net): 8596 lb Volume (Net): 2.2cu.yd			
