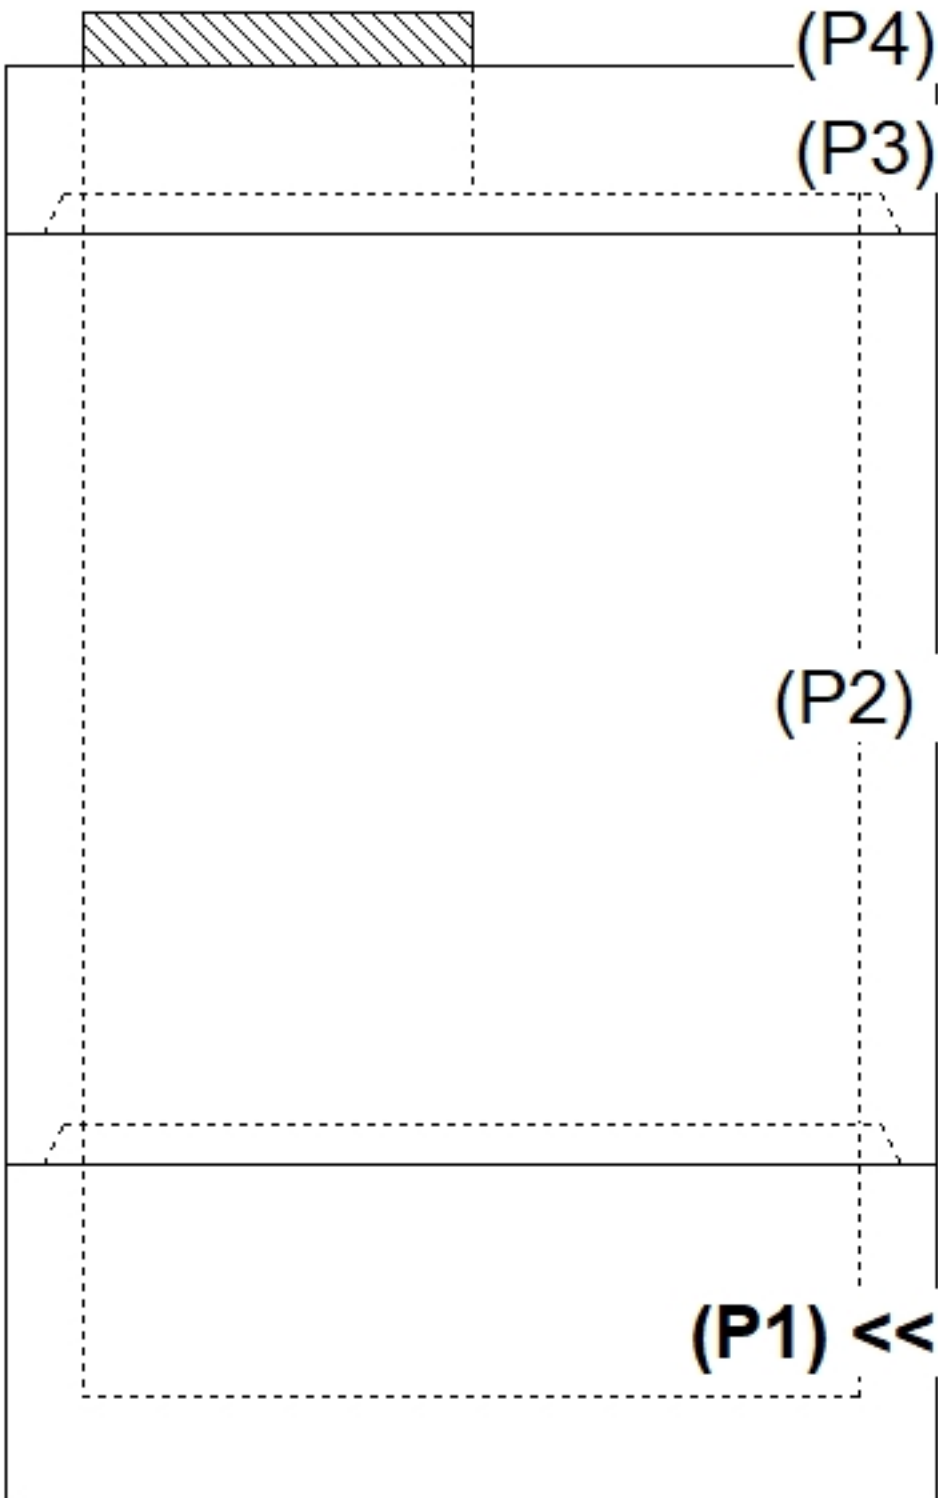
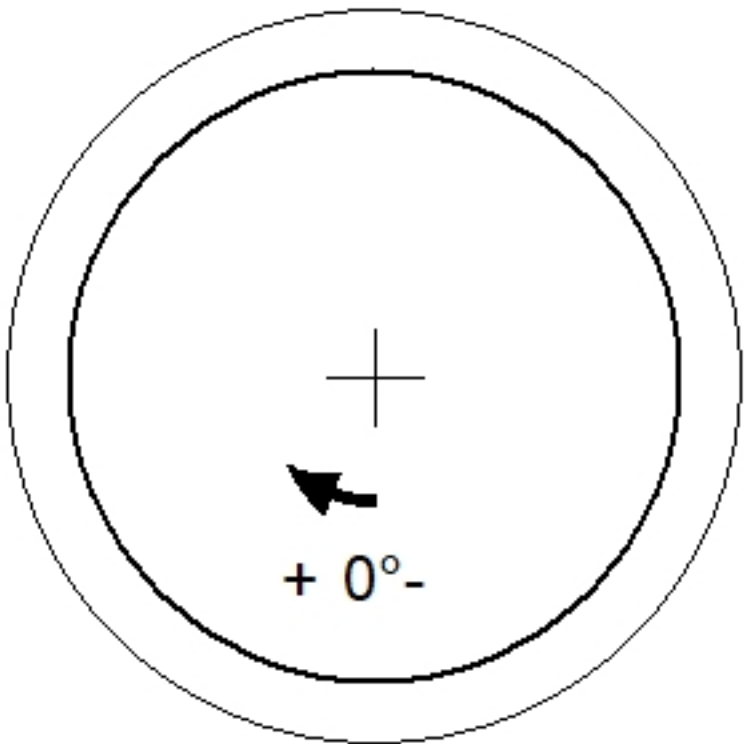
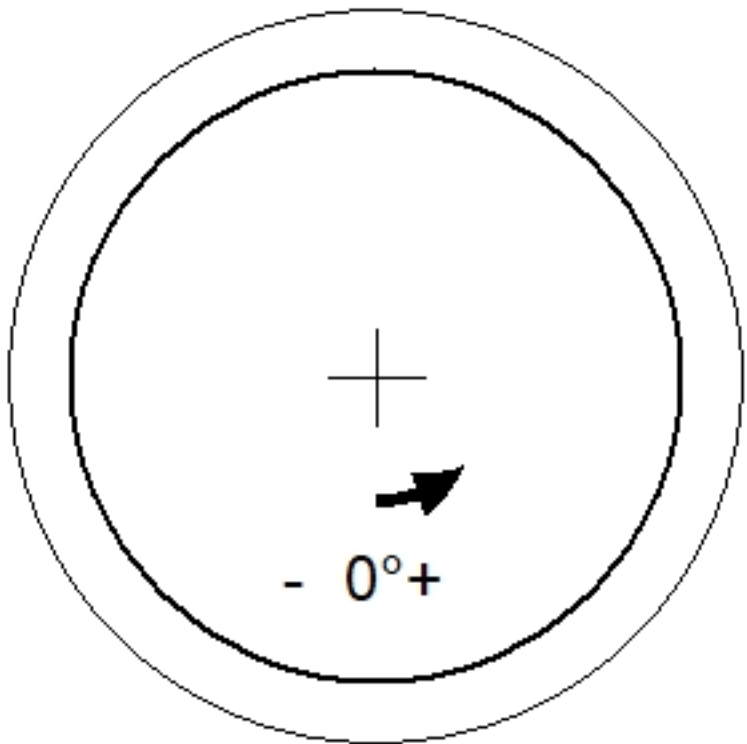
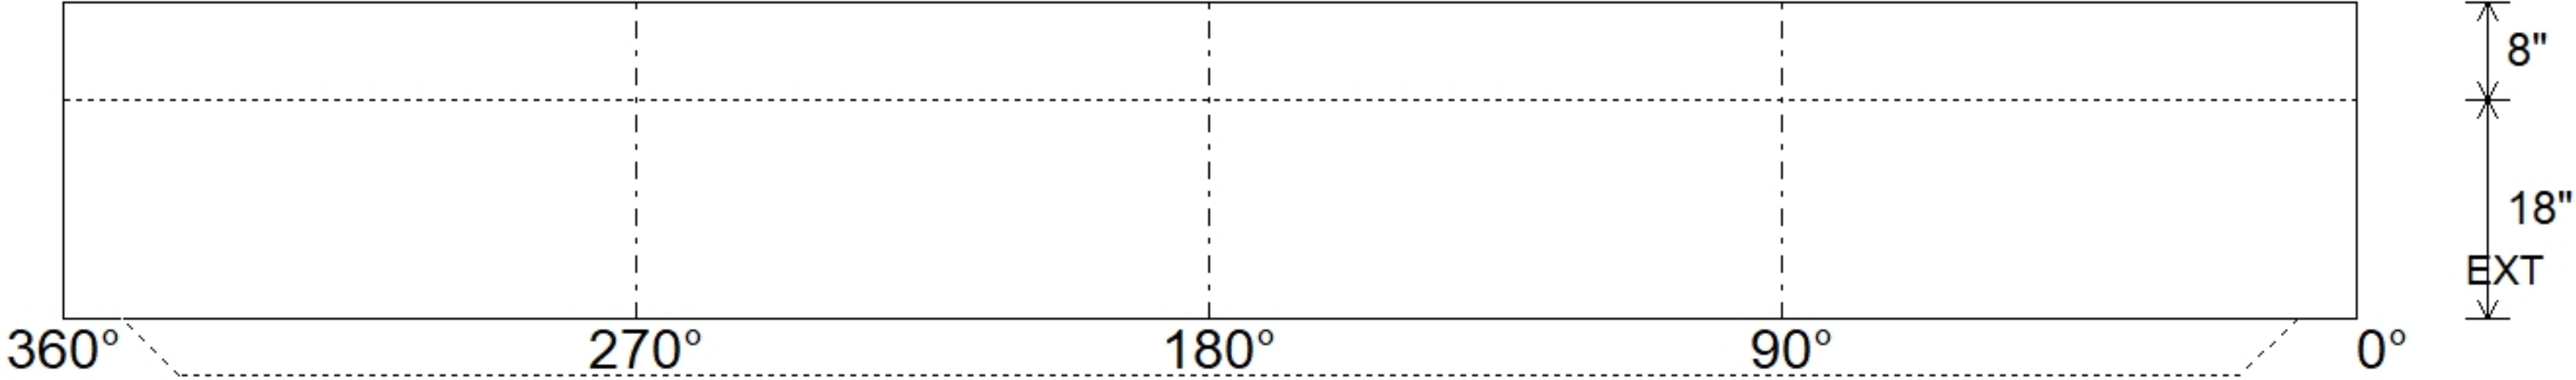


Job Name: 26-3266 903262 Enterprise Leasing Hazelwood Job Location: Hazelwood, MO Contractor: Contech Engineering Solutions					Plant: Beaver Dam 8/17/2026 4:03:53 PM		Tech: S. Felletter PC: C. Goff				
Structure ID: 10-CS-5											
P1		MH060BA18			MH BASE T/n						
P4) 30" - CASTING HEIGHT - 4" P3) 60" - MH FLAT TOP SPEC. (30" ECC HOLE) F/G - 13" P2) 60" - MH RISER T/G - 72" P1) 60" - MH BASE T/n - 18" 1) ASSEMBLY REQUIRED 1) CVSTENCILING 2) 60" - Conseal CS-102 1.00" 2) PSX - 20Y DD					0 lb 2589 lb 7187 lb 4612 lb 0 lb 0 lb 0 lb 16 lb ----- Structure Total: 14404 lb		Structure Notes: 4" CASTING BY OTHERS . LIFTING ANCHORS TO BE INSTALLED ON THE OUTSIDE OF THE STRUCTURE . ICAST TO INSTALL THE INTERNALS . CONTECH'S LOGO AS WELL AS THE INLET AND OUTLET MUST BE STENCILED ONTO THE STRUCTURE				
Rim: 529.28' Rim to Invert: 4.68' Slack: 10.156" Sump: 60.996" Step Position: 0°											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (┘)	Offset	
Invert 1											
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											
					RIGHT-SIDE UP VIEW (int. dimensions) 					UPSIDE-DOWN VIEW (int. dimenions) 	
INSIDE WALL DIMENSIONS 											
Coating (Int): Coating (Ext):			Seam Up: Tongue Seam Dn: n/a		Wall Thickness: 6" Floor Height: 8"		Height (Int): 18" Height (Ext): 26"		Weight (Net): 4612 lb Volume (Net): 1.18cu.yd		
