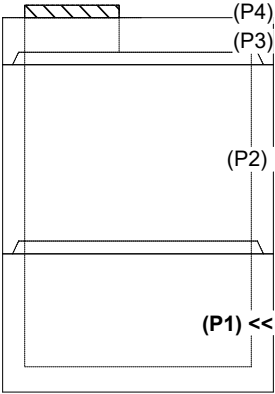





Job Name: 26-2582 - 739729 Teal Drive Job Location: Nashville, TN Contractor: Contech Engineering Solutions					Plant: Beaver Dam 6/16/2026 1:01:31 PM		Tech: J. Coppage PC: T. Sekula				
Structure ID: 15-CS-6											
P1 MH072BA36			MH BASE T/n								
P4) 30" - CASTING HEIGHT - 4" P3) 72" - MH FLAT TOP SPEC. (30" ECC HOLE) F/G - 15" P2) 72" - MH RISER T/G - 60" P1) 72" - MH BASE T/n - 36" 1) CVSTENCILING 1) ASSEMBLY REQUIRED 2) 72" - Conseal CS-102 1.00" 2) Hole - 36"						0 lb 4661 lb 7504 lb 9148 lb 0 lb 0 lb 0 lb 0 lb 0 lb ----- 21312 lb		Structure Notes: SITE DESIGNATION: STM A2 (4" TALL CASTING PROVIDED BY OTHERS) ICAST TO INSTALL THE INTERNALS BASE TO BE MECHANICALLY ATTACHED TO THE BOTTOM OF THE CONTROL RISER CONTECH'S LOGO AS WELL AS THE INLET AND THE OUTLET MUST BE STENBCILED ONTO THE STRUCTURE			
Rim: 470.12' Rim to Invert: 5.08' Slack: 5.96" Sump: 60" Step Position:											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset	
Invert 1											
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											
 RIGHT-SIDE UP VIEW (int. dimensions)  UPSIDE-DOWN VIEW (int. dimenions)  INSIDE WALL DIMENSIONS 											
Coating (Int): Coating (Ext):				Seam Up: Tongue Seam Dn: n/a		Wall Thickness: 7" Floor Height: 8"		Height (Int): 36" Height (Ext): 44"		Weight (Net): 9148 lb Volume (Net): 2.34cu.yd	
