

Job Name: 26-2582 - 739729 Teal Drive
Job Location: Nashville, TN
Contractor: Contech Engineering Solutions

Plant: Beaver Dam
6/16/2026 1:01:44 PM

Tech: J. Coppage
PC: T. Sekula



Structure ID: 15-CS-6

P3 MH072LD15-30ECC

MH FLAT TOP SPEC. (30" ECC HOLE) F/G



P4) 30" - CASTING HEIGHT - 4"
P3) 72" - MH FLAT TOP SPEC. (30" ECC HOLE) F/G - 15"
P2) 72" - MH RISER T/G - 60"
P1) 72" - MH BASE T/n - 36"
1) CVSTENCILING
1) ASSEMBLY REQUIRED
2) 72" - Con Seal CS-102 1.00"
2) Hole - 36

0 lb
4661 lb
7504 lb
9148 lb
0 lb
0 lb
0 lb
0 lb
0 lb
Structure Total: 21312 lb

Structure Notes:
SITE DESIGNATION: STM A2
(4" TALL CASTING PROVIDED BY OTHERS)
ICAST TO INSTALL THE INTERNALS
BASE TO BE MECHANICALLY ATTACHED TO THE BOTTOM OF THE CONTROL RISER
CONTECH'S LOGO AS WELL AS THE INLET AND THE OUTLET MUST BE STENBCILED ONTO THE STRUCTURE

NOTES:

1. MANUFACTURED TO ASTM C-478 (LATEST REVISION).
2. CONCRETE: 4,000 PSI AT 28 DAYS.
3. REINFORCING: #5 BAR @ 6" O.C. E.W. (GRADE 60).

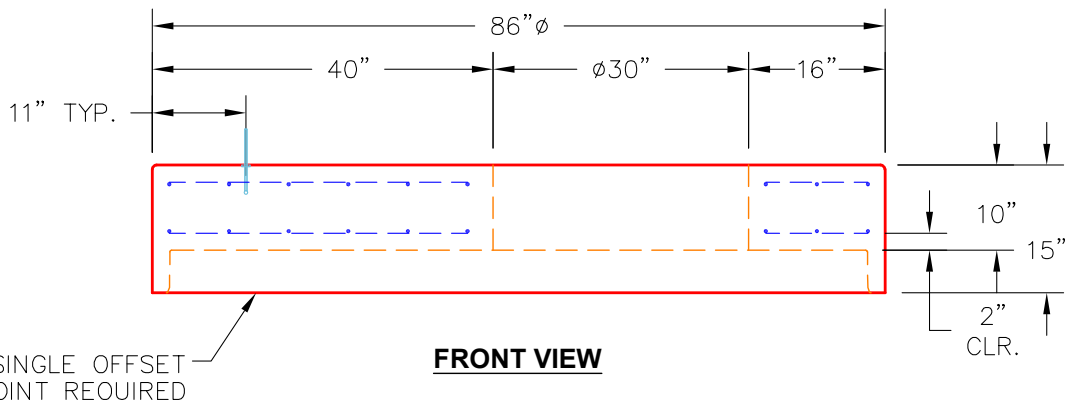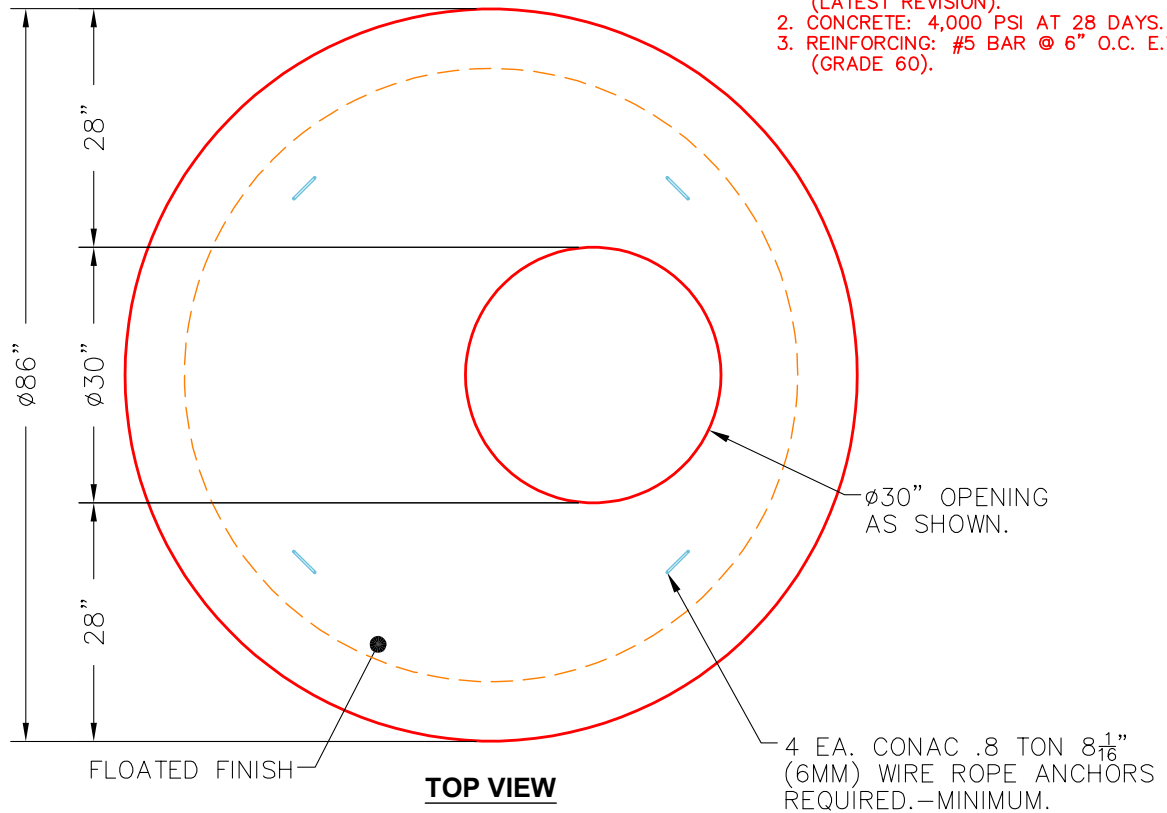

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: Groove	Wall Thickness: 7"	Height (Ext): 15"	Weight (Net): 4661 lb Volume (Net): 1.19cu.yd
----------------------------------	----------------------------------	--------------------	-------------------	--
