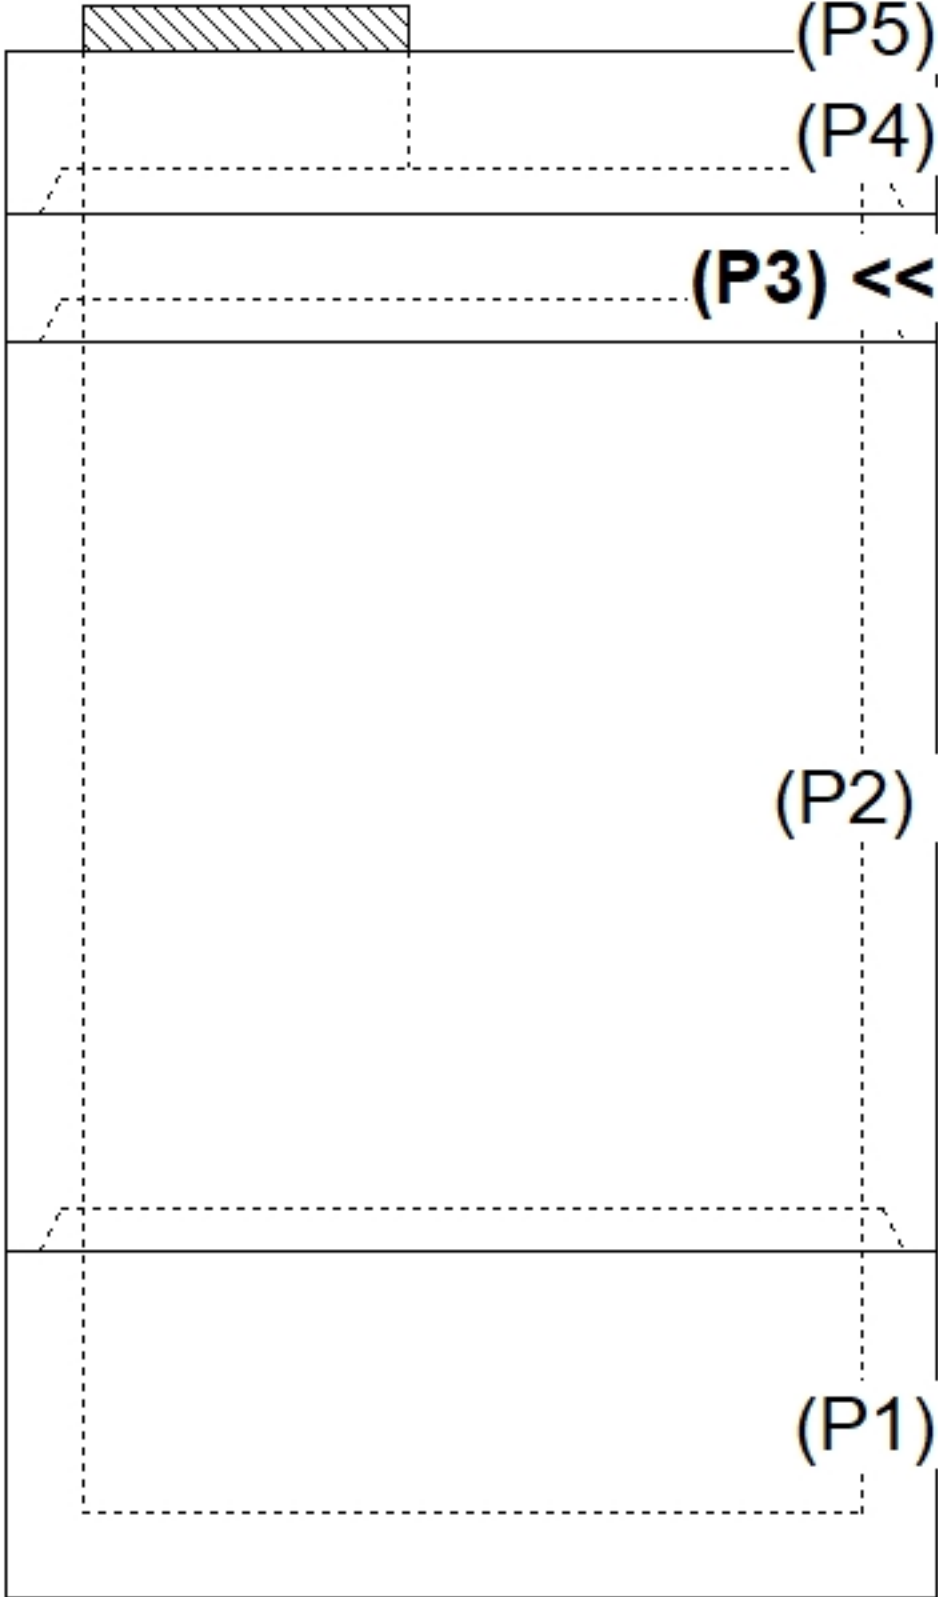
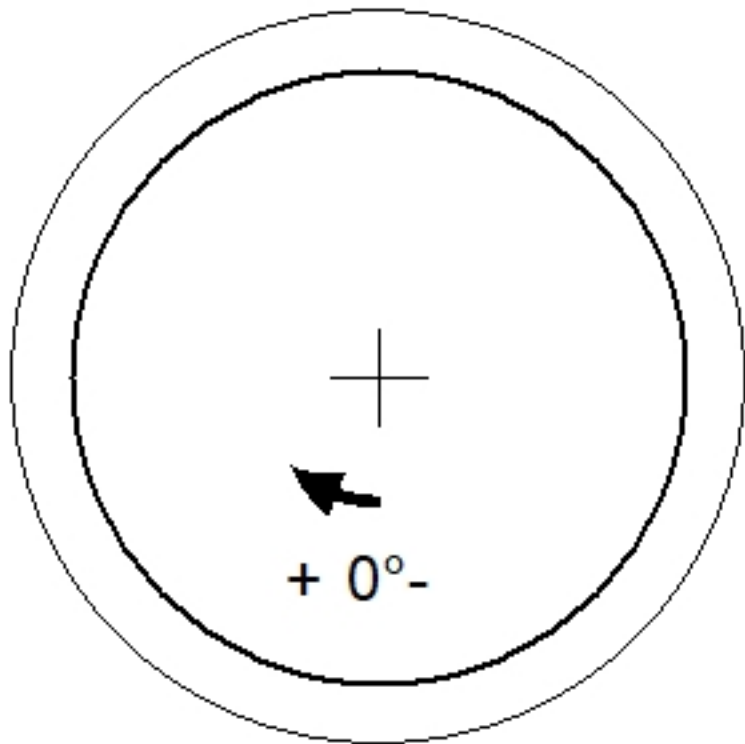
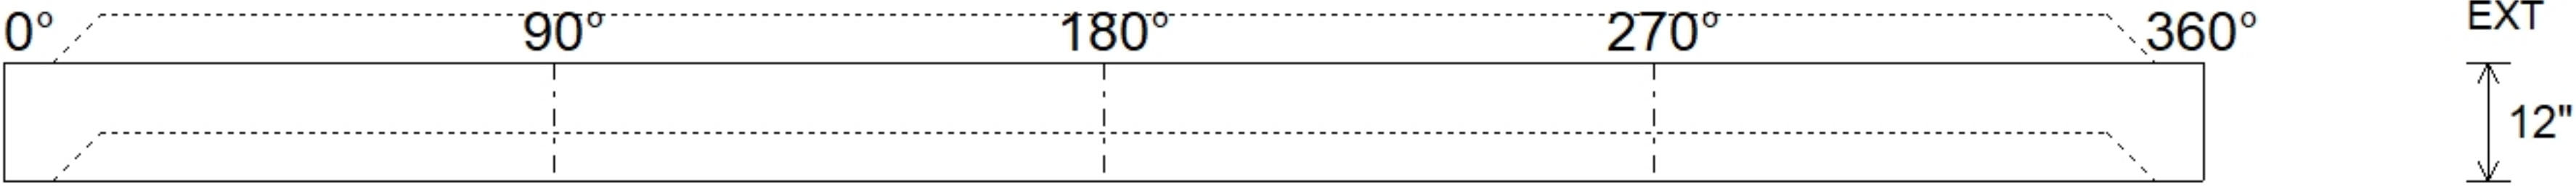


Job Name: 26-2744 904618 Jeffersonville HS Job Location: Jeffersonville, IN Contractor: Contech Engineering Solutions					Plant: 6/24/2026 2:31:20 PM		Tech: S. Felletter PC: C. Goff						
Structure ID: 10-CS-6													
P3			MH072RS12			MH RISER T/G							
P5) 30" - CASTING HEIGHT - 4" P4) 72" - MH FLAT TOP SPEC. (30" ECC HOLE) F/G - 15" P3) 72" - MH RISER T/G - 12" P2) 72" - MH RISER T/G - 84" P1) 72" - MH BASE T/n - 24" 1) ASSEMBLY REQUIRED 1) CVSTENCILING 3) 72" - Conseal CS-102 1.00" 2) Hole - 36						0 lb 4661 lb 1749 lb 11003 lb 7398 lb 0 lb 0 lb 0 lb 0 lb ----- 24811 lb		Structure Notes: 4" CASTING BY OTHERS . LIFTING ANCHORS TO BE INSTALLED ON THE OUTSIDE OF THE STRUCTURE . ICAST TO INSTALL THE INTERNALS . CONTECH'S LOGO AS WELL AS THE INLET AND OUTLET MUST BE STENCILED ONTO THE STRUCTURE					
Rim: 483' Rim to Invert: 6.14' Slack: 4.796" Sump: 70.116" Step Position: 90°													
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (┘)	Offset			
Invert 1													
Invert 2													
Invert 3													
Invert 4													
Invert 5													
Invert 6													
Invert 7													
Invert 8													
RIGHT-SIDE UP VIEW (int. dimensions)													
													
INSIDE WALL DIMENSIONS													
(P3)													
Coating (Int): Coating (Ext):				Seam Up: Tongue Seam Dn: Groove		Wall Thickness: 7" Floor Height: 0"		Height (Int): 12" Height (Ext): 12"		Weight (Net): 1749 lb Volume (Net): 0.45cu.yd			
