

Job Name: 26-2744 904618 Jeffersonville HS  
Job Location: Jeffersonville, IN  
Contractor: Contech Engineering Solutions

Plant:  
6/24/2026 2:31:04 PM

Tech: S. Felletter  
PC: C. Goff



**Structure ID: 10-CS-6**

**P4 MH072LD15-30ECC**

**MH FLAT TOP SPEC. (30" ECC HOLE) F/G**

P5) 30" - CASTING HEIGHT - 4"  
P4) 72" - MH FLAT TOP SPEC. (30" ECC HOLE) F/G - 15"  
P3) 72" - MH RISER T/G - 12"  
P2) 72" - MH RISER T/G - 84"  
P1) 72" - MH BASE T/n - 24"  
1) ASSEMBLY REQUIRED  
1) CVSTENCILING  
3) 72" - Conseal CS-102 1.00"  
2) Hole - 36



Structure Total:

0 lb  
4661 lb  
1749 lb  
11003 lb  
7398 lb  
0 lb  
0 lb  
0 lb  
0 lb  
-----  
24811 lb

Structure Notes:  
4" CASTING BY OTHERS  
LIFTING ANCHORS TO BE INSTALLED  
ON THE OUTSIDE OF THE STRUCTURE  
ICAST TO INSTALL THE INTERNALS  
CONTECH'S LOGO AS WELL AS THE  
INLET AND OUTLET MUST BE  
STENCILED ONTO THE STRUCTURE

**NOTES:**

1. MANUFACTURED TO ASTM C-478 (LATEST REVISION).
2. CONCRETE: 4,000 PSI AT 28 DAYS.
3. REINFORCING: #5 BAR @ 6" C.C. E.W. (GRADE 60).

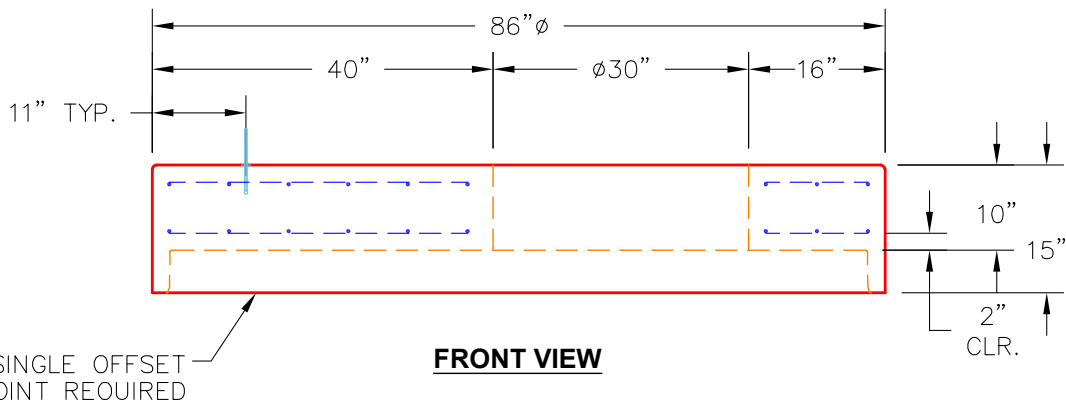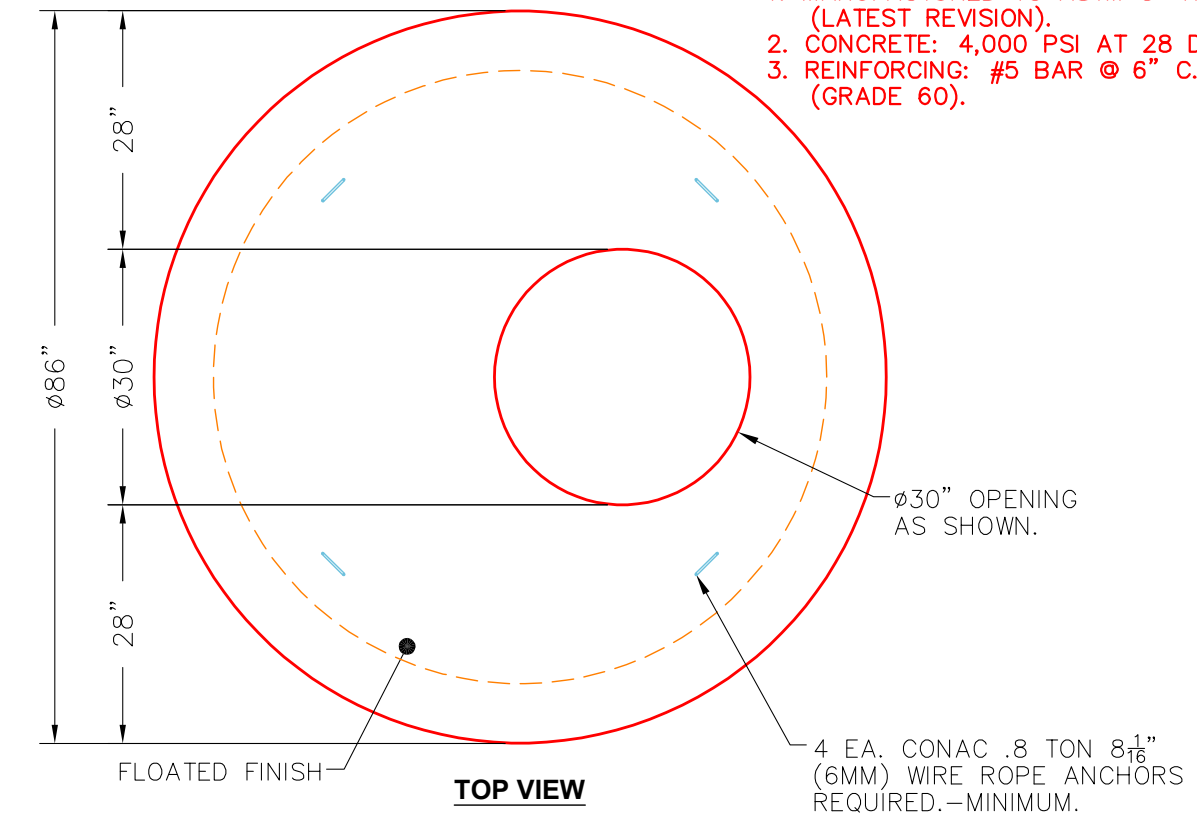

|                                  |                                  |                    |                   |                                                  |
|----------------------------------|----------------------------------|--------------------|-------------------|--------------------------------------------------|
| Coating (Int):<br>Coating (Ext): | Seam Up: Flat<br>Seam Dn: Groove | Wall Thickness: 7" | Height (Ext): 15" | Weight (Net): 4661 lb<br>Volume (Net): 1.19cu.yd |
|----------------------------------|----------------------------------|--------------------|-------------------|--------------------------------------------------|
