

Job Name: 26-1000P2 Clark Distributing New HQ - Site Structures
Job Location: Bowling Green, KY
Contractor: Scotty's Contracting & Stone, LLC

Plant: Beaver Dam

Tech: S. Felletter

8/11/2026 9:22:07 AM

PC: M. Sullivan



Structure ID: DBI-15

P3 MH072LD15-24x30 LOUMSD



MH FLAT TOP w/24"x30" Hole LOU-MSD F/G

- P4) 24" x 30" - CASTING HEIGHT - 3.50"
P3) 72" - MH FLAT TOP w/24"x30" Hole LOU-MSD F/G - 15"
P2) 72" - MH RISER Custom Ht T/G - 31"
P1) 72" - MH BASE T/n - 60"
1) CASTING - HOE KY-460-11 F/G (DBI 11)
2) 72" - Con Seal CS-102 1.00"
1) 24" x 30" - Con Seal CS-102 1.00"
2) Hole - 50
1) Hole - 16
5) MH Step ML-10-TDS-NCR - 10"

0 lb
6405 lb
4519 lb
10022 lb
421 lb
0 lb
0 lb
0 lb
0 lb
0 lb
Structure Total: 21367 lb

Structure Notes:

1. PER ASTM C478 SPECIFICATIONS.
 2. CONCRETE = 4,000 PSI AT 28 DAYS.
 3. CASTING BY ICAST (HOE KY-460-11 F/G).
- REINFORCING PER ASTM A615 (GRADE 60).
- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W..
 - RISER/WALLS (As .18)
 - FLOOR (As .37) #5 BARS AT 10" C.C.E.W.

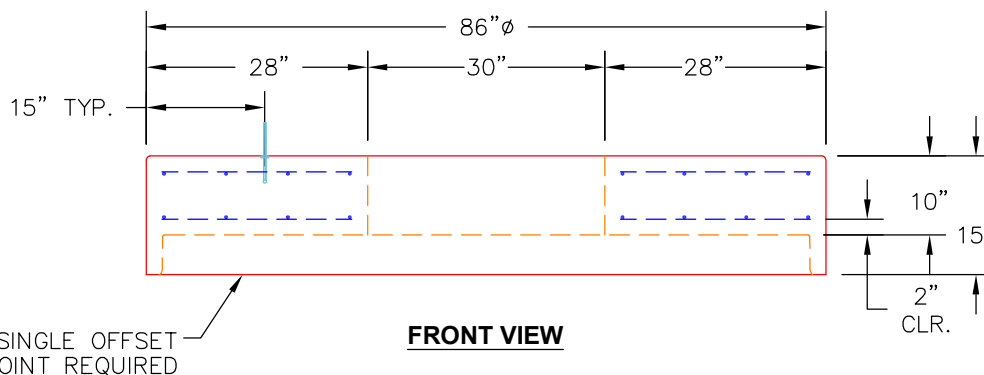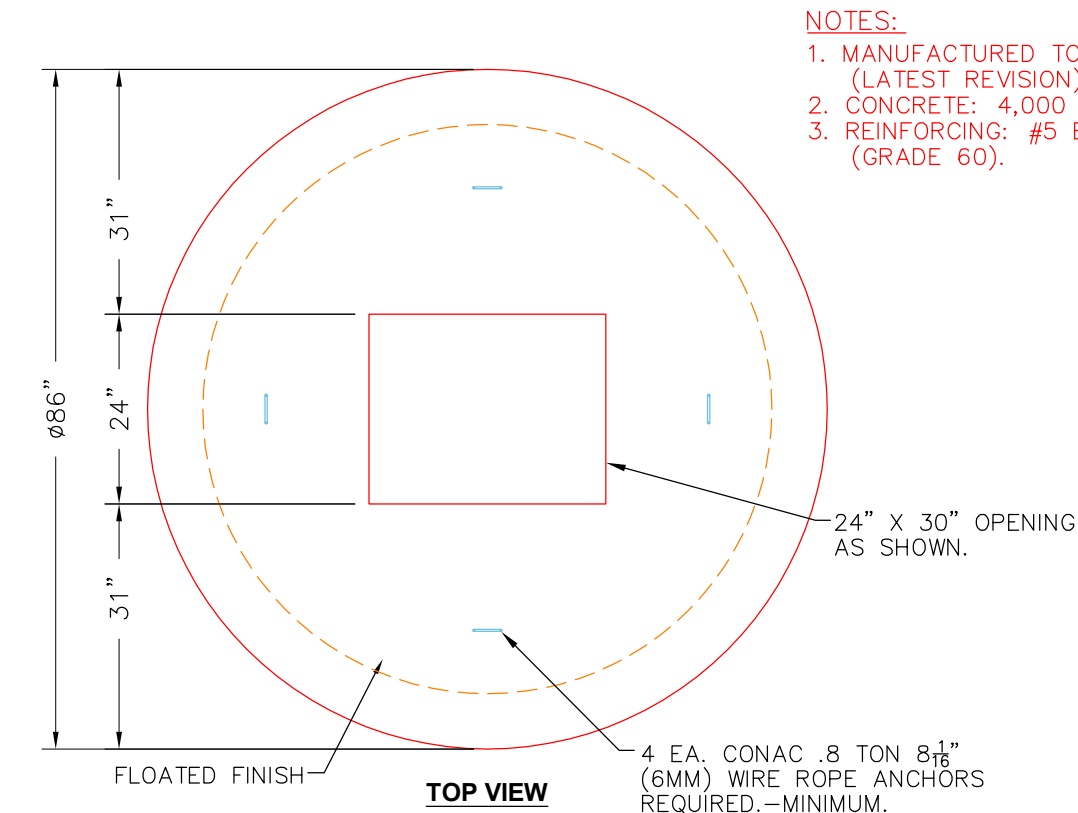

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Groove

Wall Thickness: 7"

Height (Ext): 15"

Weight (Net): 6405 lb
Volume (Net): 1.64cu.yd
