

Job Name: 26-3091 907597 Ives Field Rec Enhance
Job Location: Shelby Twp, MI
Contractor: Contech Engineering Solutions

Plant: Beaver Dam

7/20/2026 9:18:10 AM

Tech: S. Felletter

PC: C. Goff



Structure ID: 10-CS-3



P3 MH036LD10-30ECC

MH FLAT LID w/30in ECC Hole F/G

- P4) 30" - CASTING HEIGHT - 4"
P3) 36" - MH FLAT LID w/30in ECC Hole F/G - 10"
P2) 36" - MH RISER T/G - 72"
P1) 36" - MH BASE T/n - 12"
1) ASSEMBLY REQUIRED
1) CVSTENCILING
2) 36" - Conseal CS-102 1.00"
2) Hole - 16

0 lb
683 lb
2898 lb
1272 lb
0 lb
0 lb
0 lb
0 lb
Structure Total: 4852 lb

Structure Notes:
4" CASTING BY OTHERS
LIFTING ANCHORS TO BE INSTALLED
ON THE OUTSIDE OF THE STRUCTURE
ICAST TO INSTALL THE INTERNALS
CONTECH'S LOGO AS WELL AS THE
INLET AND OUTLET MUST BE
STENCILED ONTO THE STRUCTURE

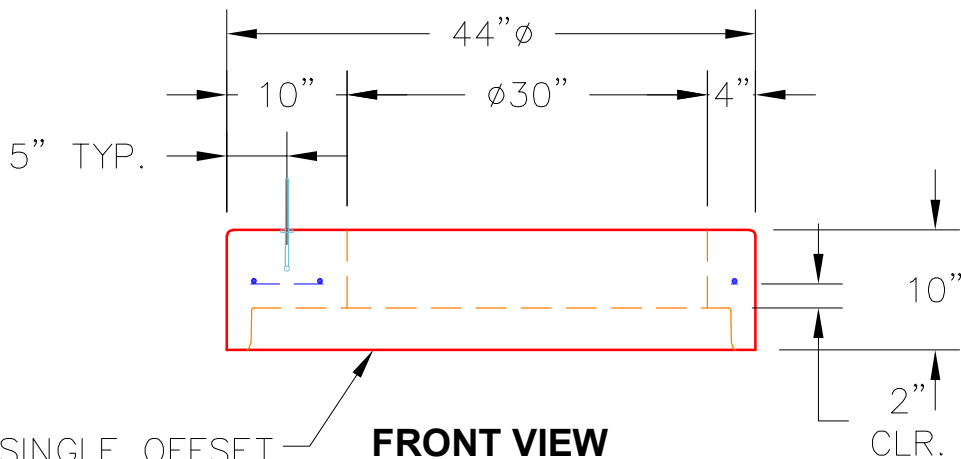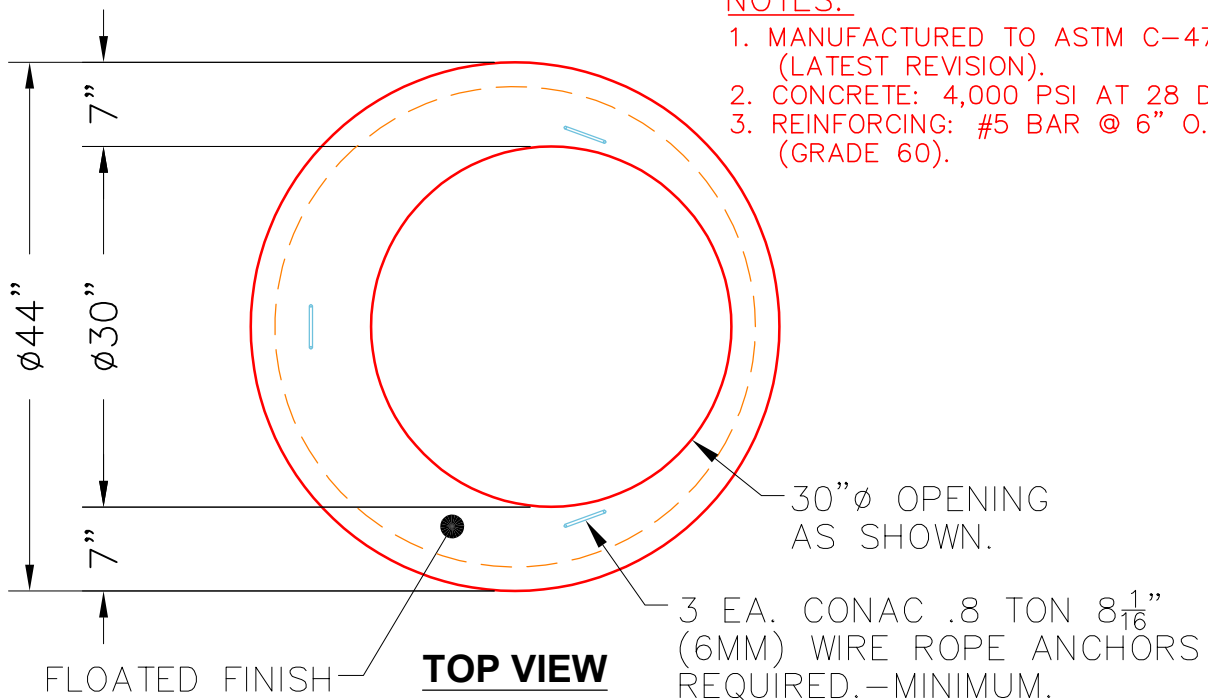

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Groove

Wall Thickness: 4"

Height (Ext): 10"

Weight (Net): 683 lb
Volume (Net): 0.17cu.yd
