


GENERAL NOTES:

1. MANUFACTURED PER ASTM C-913 (LATEST REVISION).
2. CONCRETE : 4,500 PSI AT 28 DAYS.
3. REINFORCING: PER ASTM 615 (GRADE 60).
- TOP SLAB (As. 62) #5 BAR @ 6" C.C.E.W.
4. WEIGHT: TOP SLAB = 3,100 LBS.
5. JOINT SEALED WITH CONCRETE SEALANTS CS-102.
(SUPPLIED BY ICAST).
6. 2 EA. J.R. HOE MCS-288 FRAME & SOLID "STORM"
COVER CAST INTO TOP SLAB (SUPPLIED BY ICAST).

PRODUCTION WORK ORDER

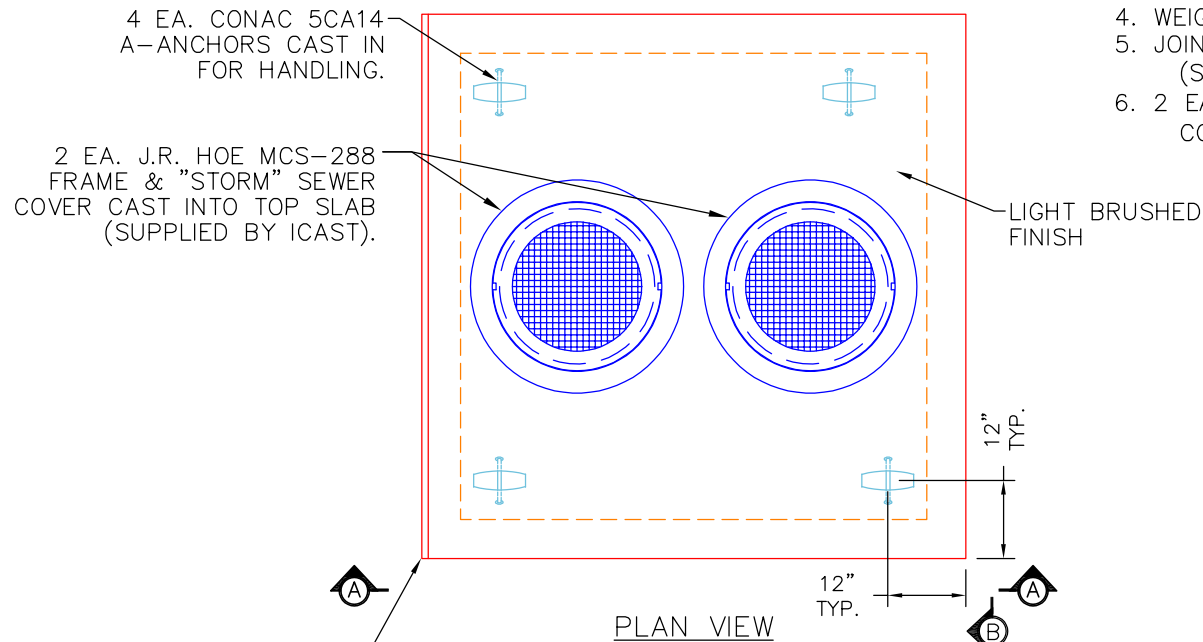

QUALITY CONTROL CHECKLIST

- ☐ ALL DIMENSIONS CORRECT.
- ☐ LIFTERS INSTALLED.
- ☐ OPENING CENTERED.
- ☐ REINFORCING CORRECT.
- ☐ SURFACE QUALITY ACCEPTABLE.
- ☐ EDGES CHAMFERED.
- ☐ ALL PATCHWORK ACCEPTABLE.

PRODUCT I.D.: BX072072-06LD06-SP

PRODUCT VIEW: RIGHT SIDE UP

PLANT: BEAVER DAM, KY.

WEIGHT: 3,100 LBS

TOP SECTION JOINT: N/A

BASE SECTION JOINT: N/A

QC CHECK INITIALS:

DESCRIPTION: 72" X 72" X 6" THICK TOP SLAB W/ 2X 24" HOLES

CUSTOMER: CONVERGENT WATER TECHNOLOGIES

PROJECT: PRETX CURB INLET

STRUCTURE I.D.: QL1

SALES ORDER NO.: 26-2562

P.C.: C. GOFF

DRAWING: S. FELLETTER

DATE: 06/09/26

SCALE: NTS

PG. 1 of 1
